

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F – SFOBB – SAS – Superstructure
Week Ending 2008-12-19

Tuesday December 16, 2008 Observation via Engineer's Boat between 0830 and 11:00: Showers, Cold, Moderate Wind

- E2 – West Elevation from TT "F" E-Line Driving Frame



E2 – East Elevation – Note Diagonal Form Braces have been removed




46.02

REC'D '09 JAN-12 #008355

E2 – West Elevation – Diagonal form braces removed – curing mats being collected.



E2 – south Elevation – Cooling water system has been disassembled

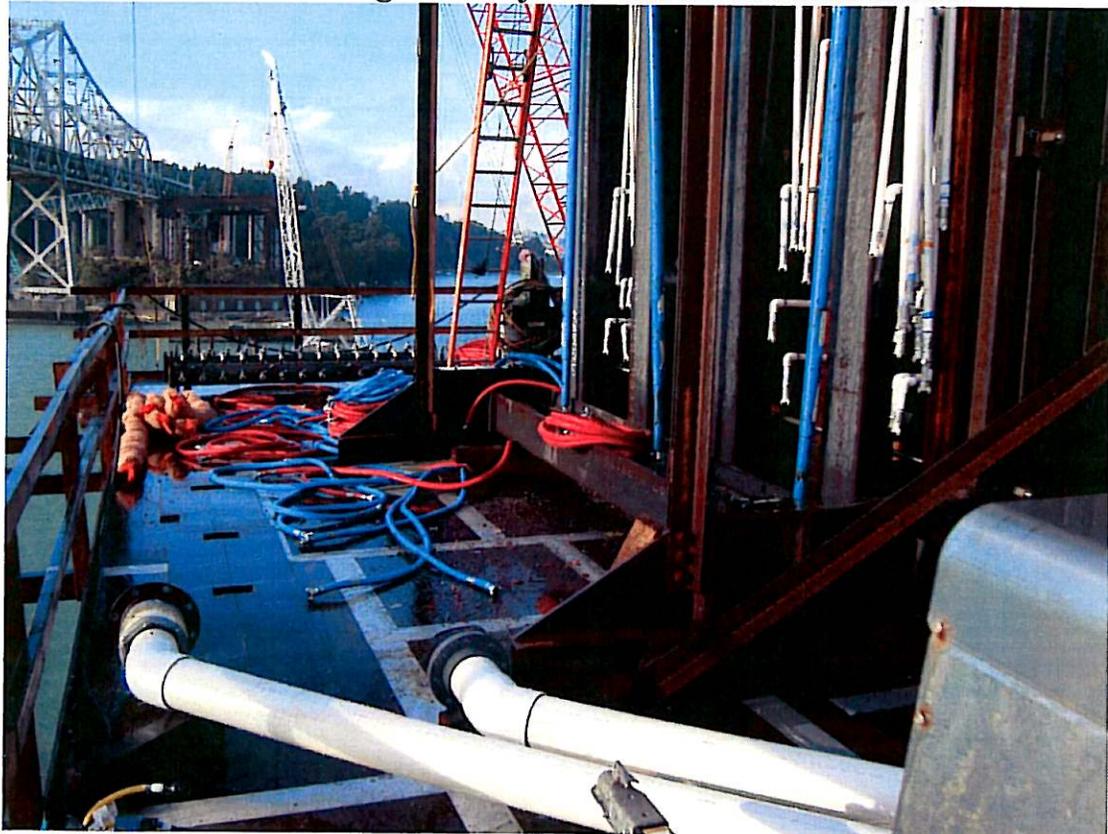

E2 – Southerly top view from Skyway



E2 – Northerly top view from Skyway



E2 – Top Closer View from Skyway



E2 – Skyway Deck: Runway, Cooling water mains & Concrete slick lines removed.



- **TT “F” Driving Frame – View from E2 Barge level**



TT “F” - Southerly Elevation of E-Line Driving Frame



TT "F" – View of W-Line Driving frame from E-Line: note King Piles have been driven (no battered piles)



TT "F" – West Line Driving Frame View from Pile Driving Barge



- **TT “D” Surveying only activity observed**



- **E-Line TT Truss from “B” toward “C” – no observed activity**




**Wednesday December 17, 2008 – Observation from Yerba Buena Island
between 1000 and 1200: Clear, Very Cold, Calm**

- **E2 – View from top of W2**



- **TT “F” W-Line: Wait period for king piles re-tapping**

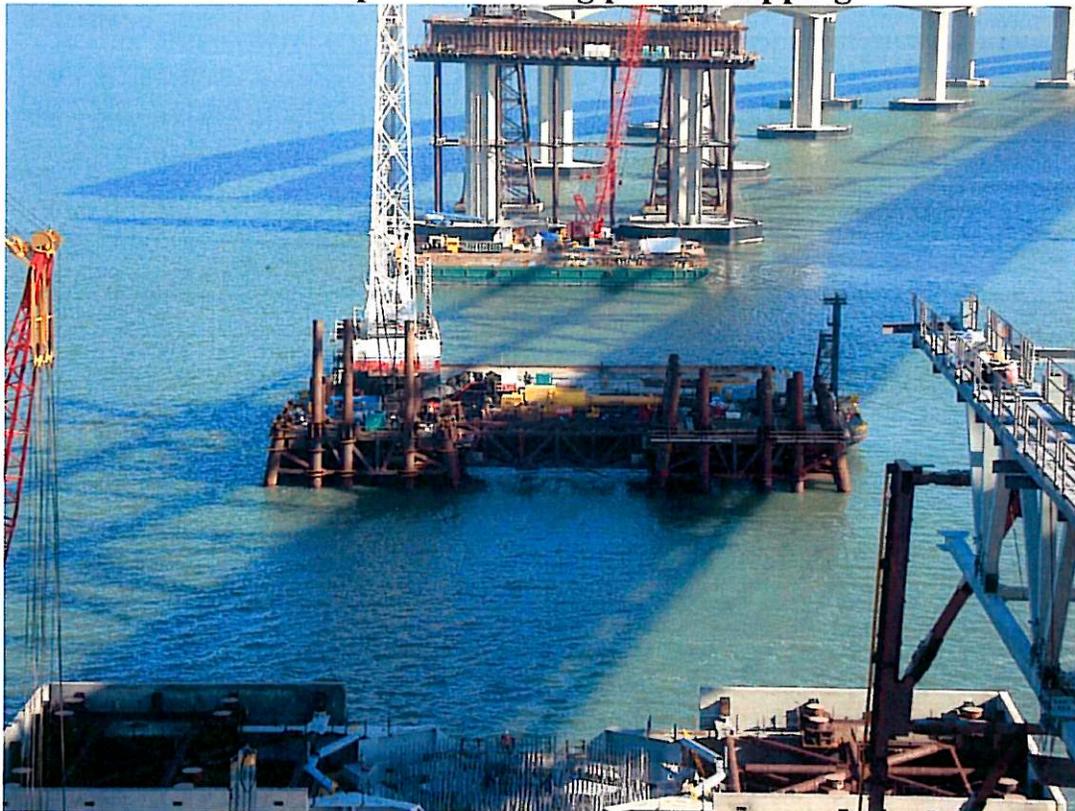

- **Temporary Truss E-Line between TT “B” toward TT “C”:** no observed activity



W-Line Truss TT “A” to TT “B” + : no observed activity since mid September




- **W2 – Curing mats on Pour #5 pour area (North portion – West Bound)**



W2 Water Cooling system for Pour #5 in operation



W2 – South Area : Prepping for pour #6 (South portion – East Bound)

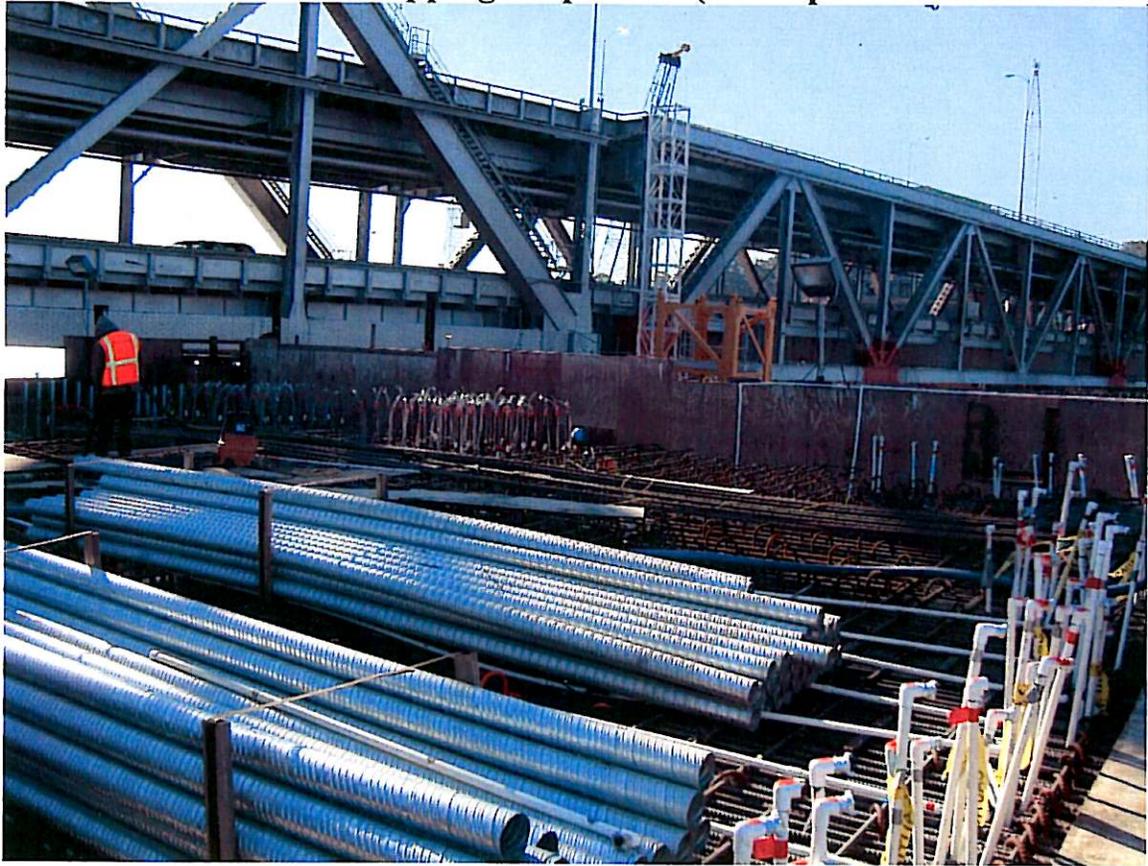

W2- another South portion view

