

Job Stamp
04-0120F4
SFOBB SAS

Construction Calendar no.	748
Project working days no.	958
Date	12/30/2008
Inspectors	Start 07:00 Stop 11:00
Hours	
Shift Hours	Start 06:30 Stop 15:30

### Assistant Structure Rep.'s Daily Report

Location & Description of Operation	SAS-Temporary towers, Tower A, B and C erections
Weather	HI: 54 F Low: 40 F Partly cloudy/foggy

Equipment and/or labor			Hours – ITEM no.							Remarks
Equip no.	# personnel	Description (of equipment or labor)	Regular	OT	DT	Rental			IDLE	
	C	4100W crane								ABF
006-18-4293	C	Ingresoll Compressor								ABF
481-93-6013	R	Gnie Boom lift								ABF
	1	Jeff Scott	8	2						ABF crane operator
	1	Ed Meyer	8	2						ABF Foreman (erection)
	1	Carlos Valverde	8	2						ABF Foreman (bolt)
	1	Matt Chamberlain	8	2						ABF Iron worker
	1	James Sturgeon	8	2						ABF Foreman (erection)
	1	David Lucero	8	2						ABF Iron worker
	1	Mike Naday	8	2						ABF Iron worker
	1	Jerry Kubala, Jr.	8	2						ABF Iron worker
	1	Alex Bartlett	8	2						ABF Iron worker
	1	Casey Lux	8	2						ABF Iron worker
	1	Ernesto Fresquez	8	2						ABF Iron worker
	1	Jason Kent	8	2						ABF Iron worker

**Description of Operation:**

- Daily activity of contractors
  - ABF continue to prepare delivery from China
  - ABF assembled north panel of E5-E6 (see Fig 1).
  - See Art Pannu's diary for contractors' activities and comments and working hours.
- Note
  - Informed Art that I wasn't able to check the bolts of the members beyond tower AE and BE, because I don't have any safe access. Moreover, the bolts of tower CE and CW, which were pretensioned after the erection, were not checked either due to the same reason.
  - Attend a safety meeting from 08:00.
  - Informed Art that steel members delivered from China have bolts and that we need to know information about the bolts, e.g. whether they are pretensioned or not, who did pre-installation test and etc (see Figs 2 and 3).



Fig 1



Fig 2

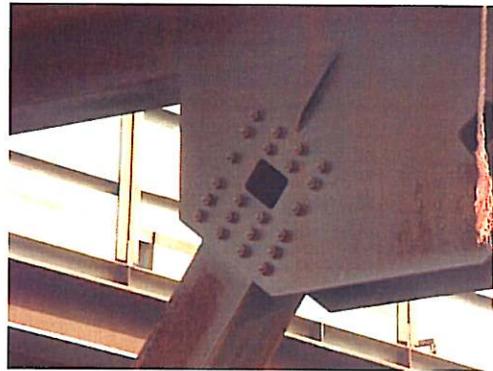


Fig 3

Inspector:  
SeongHyeok Song

Trans Engineer (Civil) / Asst. Struct. Rep
