

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 758
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 968
Form HC-10A (Rev. 6/80)	04-0120F4	Date	01/09/2009

Inspectors Hours	Start	0630	Stop	1800
Shift Hours	Start	0630	Stop	1800

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT								IDLE OR DOWN	Name	Contractor
		Big Digger barge	0											
		DB # 5 Marine barge	8											
		APE 600 Vibration hammer	8											
		Delmag 100 - Diesel hammer	0											
		Superintendant	8	3									Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	3									Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	8	0									Adams Price	Traylor Dutra
		Operator	8	3									Joe Boracci	Traylor Dutra
		Pile driver Journeyman	8	3									Ventura Ochoa	Traylor Dutra
		Operator	0	0									Theo Roth	Traylor Dutra
		Pile driver Journeyman	0	0									Phillip Baker	Traylor Dutra
		Pile driver Journeyman	8	0									Robert Utley	Traylor Dutra
		Pile driver Journeyman	0	0									Bradley Mc Marley	Traylor Dutra
		Pile driver Journeyman	8	3									Lee Tucker	
		Pile driver Journeyman	0	0									Danny Vega	Traylor Dutra
		Pile driver Journeyman	8	0									Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	0	0									Jake Lavas	Traylor Dutra
		Pile driver Journeyman	0	0									Gary Lewis	Traylor Dutra
		Operator	8	3									Bud Germany	Traylor Dutra
		Operator	8	3									Steve Gordon	Traylor Dutra
		Pile driver Journeyman	8	0									Travis Logsdon	Traylor Dutra
		Operator	8	3									Kurt Dillard	Traylor Dutra
		Pile driver Apprentice	8	3									Richard Hilbert J.	Traylor Dutra
		Pile driver Journeyman	0	0									Todd Labarb	Traylor Dutra
		Pile driver Journeyman	8	3									Richard Hilbert	Traylor Dutra
		Pile driver Journeyman	0	0									Randall Lesley	Traylor Dutra

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.


## Description of Operation:


### 1. Temporary Tower F – Pile driving and splicing TTF North .

#### Activities:


1. Office work:
  - Review plans, special provisions, RFI and ABF submittals for TTF and TTG
2. Field work:
  - DB 5 crew continued pile splicing on TTF North, pile F117 was 80% completed.
  - Michael Johnson and Gary Ehram from Smith Emery were present for QA/QC welding inspection.
  - Andrew Erthum from CWI consultant was present for QC transition to replace Gary Ehram from Smith Emery.
  - Michael Johnson performed UT testing on pile F120
  - Sean Hanser and Sierra Maxwell from SRS consultant were present for mammal monitoring, the driving operation was delay app. 30minutes at noon time due to the appearance of the seal
  - John Halloway was present for PDA testing.
  - Manuel Reyes from KCB was present for pile driving monitoring.
  - DB5 crew performed operation by using Delmag 100 such as:
    - F118: was driven to 72.25 m at top of the annulus. (1322-1339)
    - F121: was driven to 66.00 m at top of the annulus.(0948-1000)
    - F119: was driven to 66.00 m at top of the annulus. (started at 1208, finished at 1222)
3. Conversation and discussion:
4. Overtime reason:  
Work three hours overtime for construction observation because contractor worked overtime.

Thanh V Le

  
Trans Engineer (D)/Asst. Struct. Rep

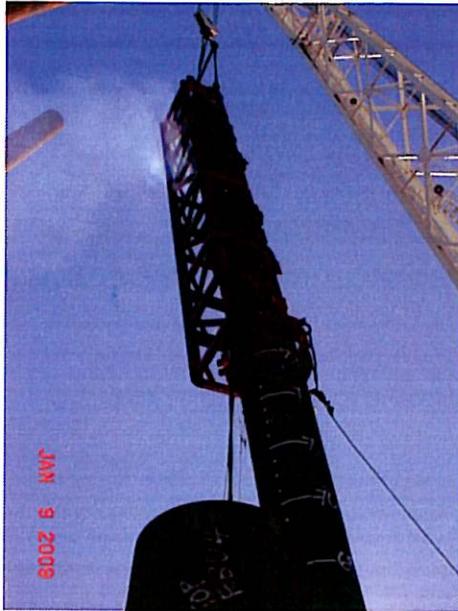

Pile driving with Delmag 100

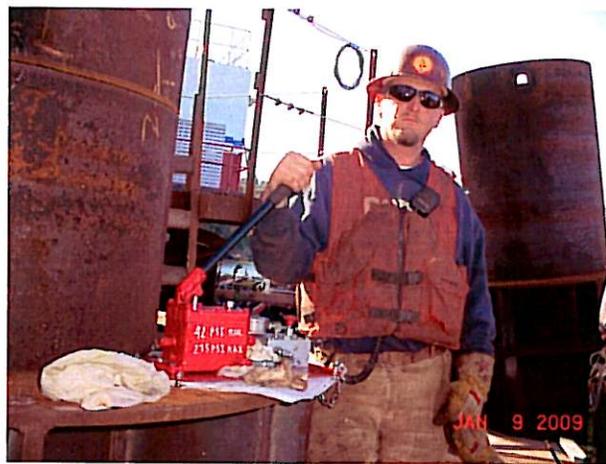

Fuel pump control for diesel hammer

