

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 762
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 972
Form HC-10A (Rev. 6/80)	04-0120F4	Date	01/13/2009

Inspectors Hours	Start	0630	Stop	1030
Shift Hours	Start	0630	Stop	1030

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	N O M E N	DESCRIPTION (Of Equipment or Labor)	Regular	OT								IDLE OR DOWN	Name	Contractor
		Big Digger barge	0											
		DB # 5 Marine barge	8											
		APE 600 Vibration hammer	8											
		Delmag 100 - Diesel hammer	0											
		Superintendant	8	2									Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	2									Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	8	2									Adams Price	Traylor Dutra
		Operator	8	2									Joe Boracci	Traylor Dutra
		Pile driver Journeyman	8	2									Ventura Ochoa	Traylor Dutra
		Operator	0	0									Theo Roth	Traylor Dutra
		Pile driver Journeyman	0	0									Phillip Baker	Traylor Dutra
		Pile driver Journeyman	8	2									Robert Utley	Traylor Dutra
		Pile driver Journeyman	0	0									Bradley Mc Marley	Traylor Dutra
		Pile driver Journeyman	8	2									Lee Tucker	
		Pile driver Journeyman	0	0									Danny Vega	Traylor Dutra
		Pile driver Journeyman	0	0									Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	8	2									Jake Lavas	Traylor Dutra
		Pile driver Journeyman	0	0									Gary Lewis	Traylor Dutra
		Operator	0	0									Bud Germany	Traylor Dutra
		Operator	0	0									Steve Gordon	Traylor Dutra
		Pile driver Journeyman	8	2									Travis Logsdon	Traylor Dutra
		Operator	8	2									Kurt Dillard	Traylor Dutra
		Pile driver Apprentice	8	2									Richard Hilbert J.	Traylor Dutra
		Pile driver Journeyman	0	0									Todd Labarb	Traylor Dutra
		Pile driver Journeyman	8	2									Richard Hilbert	Traylor Dutra
		Pile driver Journeyman	0	0									Randall Lesley	Traylor Dutra


Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.


Description of Operation:

1. Temporary Tower F – Pile driving and splicing TTF North .

Activities:

1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTF and TTG
2. Field work:
 - DB 5 crew continued pile splicing operation: F104 completed and UT and F112 was 80% completed.
 - Michael Johnson and Andrew /CWI Arthur from Smith Emery were present for QA/QC welding inspection.
 - BD5 crew cut off piles at TTF South 8 of 48" piles at North and South of TTF South.(2ft above the annulus).
 - Thanh left the site at 1030; Jason was on board in the afternoon for construction observation.
3. Conversation and discussion:
4. Overtime reason:

Thanh V Le  Trans Engineer (D)/Asst. Struct. Rep

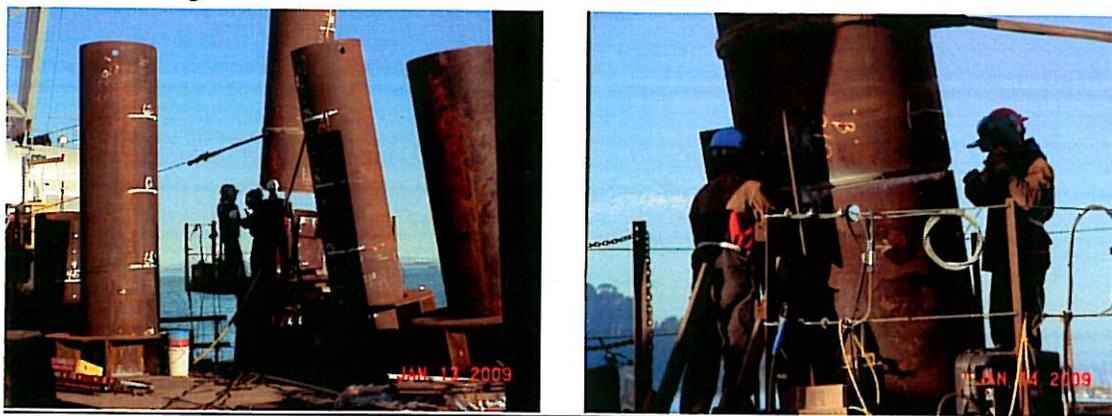

Piles splicing operation
