

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 735
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 945
Form HC-10A (Rev. 6/80)	04-0120F4	Date	12/17/2008

Inspectors Hours	Start	0630	Stop	1700
Shift Hours	Start	0630	Stop	1700

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

HOURS - ITEM NO.												REMARKS	
Equip. #	N O M E N	DESCRIPTION (Of Equipment or Labor)	Regular	OT							IDLE OR DOWN	Name Contractor	
												Name	Contractor
		Big Digger barge	0										
		DB # 5 Marine barge	8										
		APE 600 Vibration hammer	0										
		Delmag 100 - Diesel hammer	0										
		Superintendant	8	2								Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	2								Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	8	2								Adams Price	Traylor Dutra
		Operator	8	2								Joe Boracci	Traylor Dutra
		Pile driver Journeyman	8	2								Ventura Ochoa	Traylor Dutra
		Operator	8	2								Theo Roth	Traylor Dutra
		Pile driver Journeyman	8	2								Phillip Baker	Traylor Dutra
		Pile driver Journeyman	8	2								Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	2								Bradly Mc Malley	Traylor Dutra
		Pile driver Journeyman	8	2								Lee Tacker	
		Pile driver Journeyman	8	2								Danny Vaga	Traylor Dutra
		Pile driver Journeyman	8	2								Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	8	2								Jake Lavash	Traylor Dutra
		Pile driver Journeyman	8	2								Gary Lewis	Traylor Dutra
		Operator	0	0								Bud Germany	Traylor Dutra
		Operator	0	0								Steve Gordon	Traylor Dutra
		Pile driver Journeyman	8	2								Travis Logsdon	Traylor Dutra
		Operator	0	0								Ernie Hamilton	Traylor Dutra
		Pile driver Apprentice	8	2								Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	8	2								Todd Labarb	Traylor Dutra
		Pile driver Journeyman	0	0								Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	0	0								Randell Lesley	Traylor Dutra

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

**Description of Operation:**

**1. Temporary Tower F – Bridge frame installation.**

**Activities:**

1. Office work:

- Review plans, special provisions, RFI and ABF submittals for TTF and TTG

2. Field work:


- DB 5 crew drilled and installed bolts to bridge frame connections.
- Stabbed 4 @ 42" piles West and East of North node TTF.
- Vibrated 6 @ 42" piles at West and East of North node TTF.
- Moved BD 5 to North of TTF.
- Continued installing working platform for drilling and bolting.

DB 5


3. Overtime reason:

Worked two hours overtime for construction observation because contractor worked overtime

Thanh V Le



Trans Engineer (D)/Asst. Struct. Rep

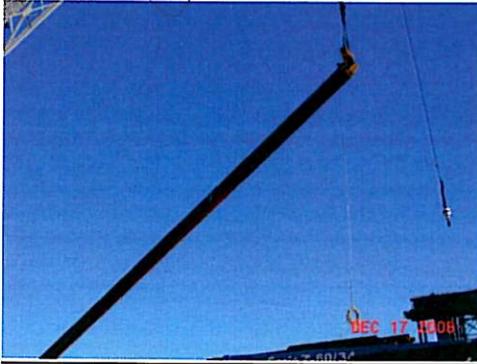

Pick up piles



Stabbing piles
