

| | | | |
|------------------------------|-----------|-----------------------|-------------|
| STATE OF CALIFORNIA | Job Stamp | 7-day Const. Calendar | Day No. 740 |
| DEPARTMENT OF TRANSPORTATION | SFOBB SAS | Project Work Day No. | Day No. 950 |
| Form HC-10A (Rev. 6/80) | 04-0120F4 | Date | 12/22/2008 |

| | | | | |
|------------------|-------|------|------|------|
| Inspectors Hours | Start | 0630 | Stop | 1500 |
| Shift Hours | Start | 0630 | Stop | 1500 |

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

| HOURS - ITEM NO. | | | | | | | | | | | | REMARKS | |
|------------------|-----------------------|--|---------|----|--|--|--|--|--|--|--------------|--------------------|---------------|
| Equip. # | N O M E N | DESCRIPTION (Of Equipment or Labor) | Regular | OT | | | | | | | IDLE OR DOWN | Name Contractor | |
| | | | | | | | | | | | | Name | Contractor |
| | | Big Digger barge | 8 | | | | | | | | | | |
| | | DB # 5 Marine barge | 0 | | | | | | | | | | |
| | | APE 600 Vibration hammer | 0 | | | | | | | | | | |
| | | Delmag 100 - Diesel hammer | 0 | | | | | | | | | | |
| | | Superintendant | 8 | 0 | | | | | | | | Terry Murray | Traylor Dutra |
| | | Pile driver Journeyman | 8 | 0 | | | | | | | | Gilbert Moya | Traylor Dutra |
| | | Pile driver Journeyman | 0 | 0 | | | | | | | | Adams Price | Traylor Dutra |
| | | Operator | 0 | 0 | | | | | | | | Joe Boracci | Traylor Dutra |
| | | Pile driver Journeyman | 8 | 0 | | | | | | | | Ventura Ochoa | Traylor Dutra |
| | | Operator | 0 | 0 | | | | | | | | Theo Roth | Traylor Dutra |
| | | Pile driver Journeyman | 0 | 0 | | | | | | | | Phillip Baker | Traylor Dutra |
| | | Pile driver Journeyman | 8 | 0 | | | | | | | | Robert Utley | Traylor Dutra |
| | | Pile driver Journeyman | 0 | 0 | | | | | | | | Bradly Mc Malley | Traylor Dutra |
| | | Pile driver Journeyman | 0 | 0 | | | | | | | | Lee Tacker | |
| | | Pile driver Journeyman | 8 | 0 | | | | | | | | Danny Vaga | Traylor Dutra |
| | | Pile driver Journeyman | 8 | 0 | | | | | | | | Stephen Mc Grew | Traylor Dutra |
| | | Pile driver Journeyman | 8 | 0 | | | | | | | | Jake Lavash | Traylor Dutra |
| | | Pile driver Journeyman | 0 | 0 | | | | | | | | Gary Lewis | Traylor Dutra |
| | | Operator | 8 | 0 | | | | | | | | Bud Germany | Traylor Dutra |
| | | Operator | 8 | 0 | | | | | | | | Steve Gordon | Traylor Dutra |
| | | Pile driver Journeyman | 0 | 0 | | | | | | | | Travis Logsdon | Traylor Dutra |
| | | Operator | 0 | 0 | | | | | | | | Ernie Hamilton | Traylor Dutra |
| | | Pile driver Apprentice | 0 | 0 | | | | | | | | Richard Hiebert J. | Traylor Dutra |
| | | Pile driver Journeyman | 0 | 0 | | | | | | | | Todd Labarb | Traylor Dutra |
| | | Operator | 8 | 0 | | | | | | | | Kurt Dillar | Traylor Dutra |
| | | Pile driver Journeyman | 0 | 0 | | | | | | | | Richard Hiebert | Traylor Dutra |
| | | Operator | 8 | | | | | | | | | Scott Eichenberger | Drill Tech |
| | | Pile driver Journeyman | 8 | 0 | | | | | | | | Randell Lesley | Traylor Dutra |

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F. Cold and windy.

Description of Operation:

1. Temporary Tower F – Bridge frame continued bolting and plumb pile plugs grouting .


Activities:


1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTF and TTG

2. Field work:
 - Big Digger crew continued bridge frame bolting on top deck.
 - Big Digger crew pour the plug grouting (app. 2ft at bottom of the annulus of four plumb piles F129 – F132.). Grouting schedule as follow:
 - * F131 : 1245 - 1257
 - * F129 : 1258 – 1312
 - * F130 : 1314 – 1328
 - * F132 : 1328 - 1340
 - DCI technician – Salvador Marino – took four grout cylinders for testing.

3. Conversation and discussion:

4. Overtime reason

Thanh V Le  Trans Engineer (D)/Asst. Struct. Rep

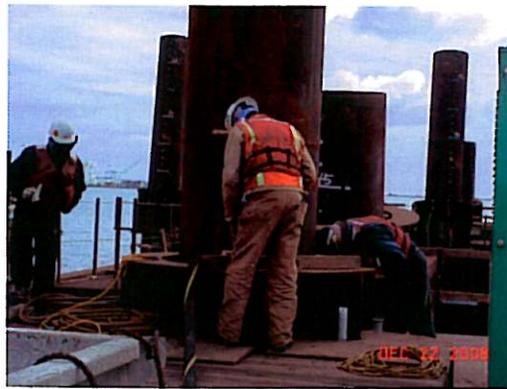

Annulus plug grouting operation
