

Job Stamp 04-0120F4 SFOBB SAS

Const. Calendar:	792			
Project Work Day No.:	1002			
Date	02/12/2009			
Inspectors	Start	09:10	Stop	11:10
Hours		12:00		15:20
Shift Hours		07:00		15:30

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR – ABFJV, Subs CMC-RS and SDI**

Weather: Partly overcast in the morning with mild temperature, overcast late in the afternoon with cool temperatures – Hi 54°F Low 41°F (per weather.com forecast)

Description of Operations @ W2 Cap Beam:

ABF

- Continued to strip and clean miscellaneous debris of the seismic joint forms near W2E.
- Continued to install vertical PT bar and tendon blockout forms near W2W.
- Continued to remove channels on the deviation saddle forms at W2E (Panel C).
- Began to clean the bearing plates for the vertical PT tendons near W2E.
- Continued to build the south end of pour 6 north template for the barrier couplers.
- Surveyors continued to as-built the deviation saddle anchor rods at Panel B of W2E.

CMC-RS

- Continued to tie the #43 transverse and #25 longitudinal bars for pour 6 north to the #25 vertical hooked bars.
- Resumed installing the #19 formsavers into the washers fastened to the east bulkhead.
- Began to place temperature steel in the vertical PT bar and tendon blockout forms.
- Began to place the 45° bars near the vertical PT bar and tendon blockout forms.

Description of Operations @ E2 Cap Beam:

SDI

- Grouted 3 tendons starting from the southwest end of the E2 cap beam while I was in the field. See Saman and Massoud's diary for testing the grout prior to placement and the remaining operations.

Surveying:

- Shot the top of the bearing plates and trumpets for continuity tendons W-1A to W-42A with the assistance of Ron Marin.


Office work:

- Continued to review the specifications and submittal 150 for the grouting operations over at the E2 cap beam.
- Wrote today's diary.

Inspector:

Matt Bruce *Matt Bruce* Transportation Engineer (D)

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow

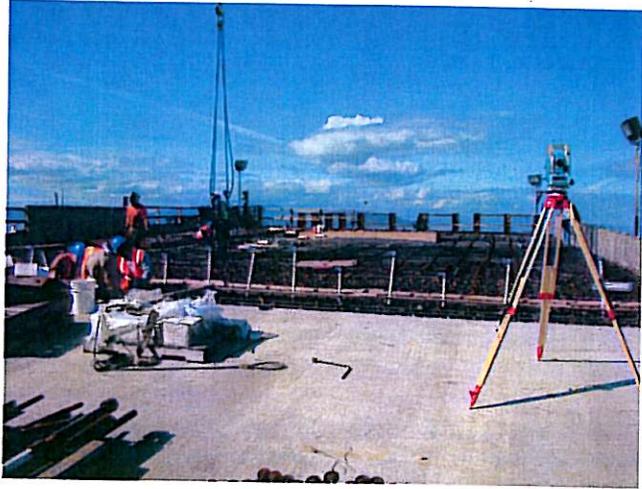

File Name:	Feb-12-2009 W2 Cap 006		
Date:	02-12-09	By Int:	M Bruce

Description: SDI ironworker injecting grout at the low end of the E2 cap beam.

File Name:	Feb-12-2009 W2 Cap 008		
Date:	02-12-09	By Int:	M Bruce

Description: Construction progress to date for pour 6 north.
