

Job Stamp  
**04-0120F4**  
**SFOBB SAS**

Const. Calendar: 806  
Project Work Day No.: 1016  
Date: 02/26/2009  
Inspectors Start 12:40 Stop 13:20  
Hours  
Shift Hours 07:00 15:30

ASSISTANT RESIDENT ENGINEER'S **CONTRACTOR - ABFJV**

EQUIPMENT AND/OR LABOR:			HOURS - ITEM NO.										REMARKS			
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	#38 Str. Concrete, Bridge											IDLE OR DOWN	Name	Contractor
1	1	General Foreman	8												Terry Cronk	ABF, at E2
2	1	W2 Pile Driver Foreman	12												Nigel Lohse	ABF, day
3	1	Pile Driver	12												Tony Creighton	ABF, night
4	1	Pile Driver	12												George McNeil	ABF, night
5	1	Laborer	8												Jose Molina	ABF
6	1	Laborer	8												Rigiberto Campos	ABF
7	1	Pile Driver J/M	8												Audre Hudson	ABF
8	1	Pile Driver/Welder	8												Henry Wheat	ABF
9	1	Elevator Operator	12												Howard Schroyer	ABF, day
10	1	Pile Driver	8												Aaron Gilpatrick	ABF
11	1	Pile Driver	8												Andrew Adams	ABF
12	1	Pile Driver	8												Kurt Chaisson	ABF
13	1	Pile Driver	8												Jesse Johnasen	ABF
14	1	Crane Operator	8												Dale Thomas	ABF
15	1	Operator Apprentice/Oiler	8												Scott Ross	ABF
16	1	Pile Driver	8												Abasi Delley	ABF
17	1	Pile Driver	8												Kenneth Reynolds	ABF
18	1	Laborer	8												Joseph Ruiz	ABF
19	1	Elevator Operator	12												Douglas Greene	ABF, night
LR1300	1	Crane	8												Liebherr	ABF
	1	Elevator	24													ABF
5573-140	1	Forklift 544D-10	4													ABF
481-93-6013	1	Manlift S-125											4		Hertz Rental	ABF
													8		Hertz Rental	ABF
768-50-4005	1	Welding Machine	8												Lincoln	ABF
	1	Main Power Generator	24												MQ 220	ABF central
549-20-4044	1	Mobile Power Generator											8		MQ Whisper Watt 7000	ABF
549-20-4007	1	Mobile Power Generator											8		MQ Whisper Watt 7000	ABF
	1	Air Compressor	8												Ingersoll Rand	ABF
185R	1	Air Compressor													Ingersoll Rand	ABF deck
	1	Chiller	24												Aggreko	ABF

1	Water Tank	24										Baker	ABF
1	Water Pump	24										Aggreko	ABF
3	Concrete Washouts								8				ABF
1	Pickup	8										Ford	ABF

**Weather:** Partly overcast with mild temperature – Hi 62°F Low 44°F (per weather.com forecast)

**Description of Operations @ W2 Cap Beam:**

ABF

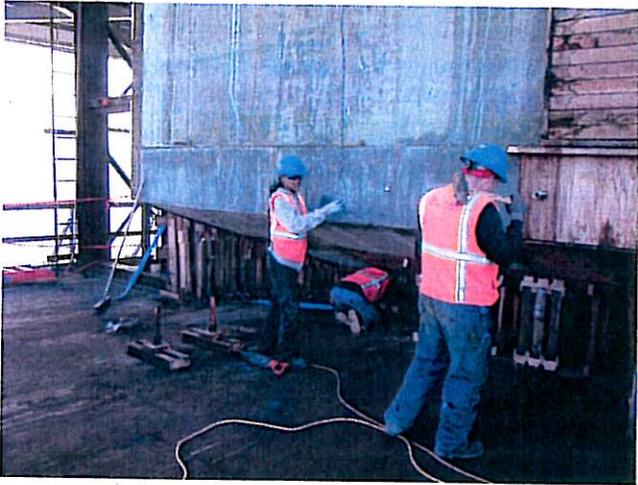
- Continued to remove the strongbacks (steel channels), bolts, and steel plates located on the south end of the cap beam. Also installed PVC pipes on the deviation saddle anchor rods as the forms were being stripped.
- Continued to remove the blockout forms for E-30B to E-44 on the west end of the cap beam.
- Began to remove the soffit forms in the southeast corner of the cap beam, see photo below.
- Continued thermal control of the pour 6 north concrete as the west manifold temperature was 45°F and the east manifold temperature was 43°F with a pressure of 38psi.

**Office work:**

- Attended biweekly Safety Tailgate and SAS meeting at 8:00am.
- Completed surveying documents for pour 6 north where the surveying was done prior to concrete placement.
- Worked on request to calibrate the Nikon total station DTM-851.
- Wrote today's diary.

**Inspector:**

Matt Bruce Matt Bruce Transportation Engineer (D)

EA		04-0120F4	
Co-Rte-KP (PM)		SF-080-13.2/13.9 (8.2/8.7)	
Structure Rep.		Rick Morrow	
			
File Name:	Feb-26-2009 W2 Cap 001	File Name:	Feb-26-2009 W2 Cap 002
Date:	02-26-09	By Int:	M Bruce
Description: PVC pipes installed on the deviation saddle anchor rods at Panel C near W2E.		Description: Pile drivers removing soffit forms in the southeast corner of the cap beam.	
