


Job Stamp
04-0120F4
SFOBB SAS

Const. Calendar: 807
Project Work Day No.: 1017
Date: 02/27/2009
Inspectors Start 08:30 Stop 14:40
Hours
Shift Hours 07:00 15:30

ASSISTANT RESIDENT ENGINEER'S CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:			HOURS - ITEM NO.										REMARKS			
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	#38 Str. Concrete, Bridge											IDLE OR DOWN	Name	Contractor
1	1	General Foreman	8												Terry Cronk	ABF, at E2
2	1	W2 Pile Driver Foreman	12												Nigel Lohse	ABF, day
3	1	Pile Driver	12												Tony Creighton	ABF, night
4	1	Pile Driver	12												George McNeil	ABF, night
5	1	Laborer	8												Jose Molina	ABF
6	1	Laborer	8												Rigiberto Campos	ABF
7	1	Pile Driver J/M	8												Audre Hudson	ABF
8	1	Pile Driver/Welder	8												Henry Wheat	ABF
9	1	Elevator Operator	12												Howard Schroyer	ABF, day
10	1	Pile Driver	8												Aaron Gilpatrick	ABF
11	1	Pile Driver	8												Andrew Adams	ABF
12	1	Pile Driver	8												Kurt Chaisson	ABF
13	1	Pile Driver	8												Jesse Johnasen	ABF
14	1	Crane Operator	8												Dale Thomas	ABF
15	1	Operator Apprentice/Oiler	8												Scott Ross	ABF
16	1	Pile Driver	8												Abasi Delley	ABF
17	1	Pile Driver	8												Kenneth Reynolds	ABF
18	1	Laborer	8												Joseph Ruiz	ABF
19	1	Elevator Operator	12												Douglas Greene	ABF, night
LR1300	1	Crane	8												Liebherr	ABF
	1	Elevator	24													ABF
5573-140	1	Forklift 544D-10	4										4		Hertz Rental	ABF
481-93-6013	1	Manlift S-125											8		Hertz Rental	ABF
768-50-4005	1	Welding Machine	8												Lincoln	ABF
	1	Main Power Generator	24												MQ 220	ABF central
549-20-4044	1	Mobile Power Generator											8		MQ Whisper Watt 7000	ABF
549-20-4007	1	Mobile Power Generator											8		MQ Whisper Watt 7000	ABF
	1	Air Compressor	8												Ingersoll Rand	ABF
185R	1	Air Compressor											8		Ingersoll Rand	ABF deck
	1	Chiller	24												Aggreko	ABF

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow

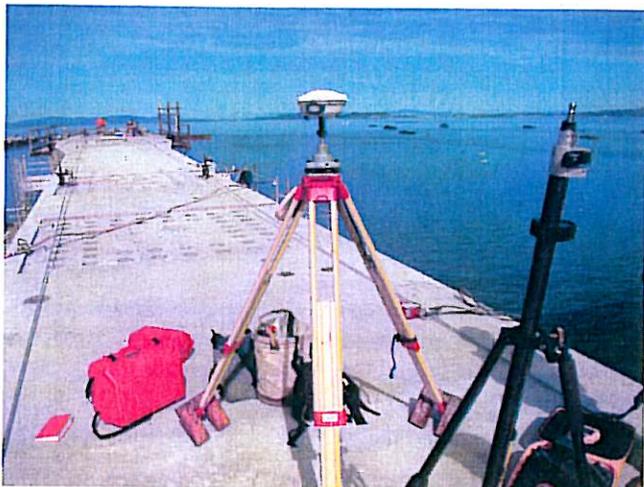

File Name:	Feb-27-2009 W2 Cap 001		
Date:	02-27-09	By Int:	M Bruce

Description: GPS unit (Trimble GNSS R8) taking measurements on ABF control point TD2001 before 11:00am.


File Name:	Feb-27-2009 W2 Cap 007		
Date:	02-27-09	By Int:	M Bruce

Description: ABF pile drivers placing concrete with the bucket at the north blockout.



File Name:	Feb-27-2009 W2 Cap 008		
Date:	02-27-09	By Int:	M Bruce


Description: Crushed wedges on the northeast end of the cap beam after concrete was placed to a height of approximately 5m.

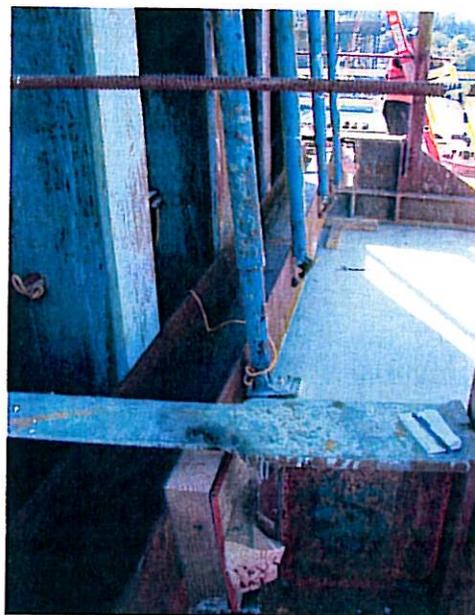

File Name:	Feb-27-2009 W2 Cap 010		
Date:	02-27-09	By Int:	M Bruce

Description: North end supports where the wedges failed in bearing under a liquid head of 4m.

EA	04-0120F4
Co-Rte-KP (PM)	SF-080-13.2/13.9 (8.2/8.7)
Structure Rep.	Rick Morrow

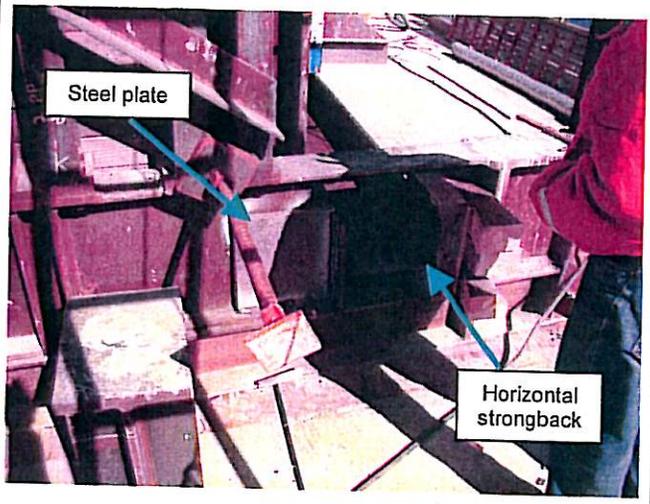

File Name:	Feb-27-2009 W2 Cap 011		
Date:	02-27-09	By Int:	M Bruce

Description: Northwest end of the blockout forms where the deflection at the bottom was 45mm.

File Name:	Feb-27-2009 W2 Cap 013		
Date:	02-27-09	By Int:	M Bruce

Description: Steel plate welded to the flange of the horizontal strongback to prevent further deflection at the bottom.
