

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F - SFOBB - Superstructure
Week ending 2009-03-05

Thursday March 5, 2009: Observation from Yerba Buena Island between 1000 and 1130
Partly Cloudy, Cool, and Calm

- E2 - West Elevation



- Preparing to Erect Temp Tower "FE" (in foreground)



REC'D 09 MAR 16 #009053

- Temp Tower "GE" - Driving Frame in Place - Preparing to drive piles



- "W" Line - Truss @ TT "BW+", TT "CW" & "DWW" - No progress this period



• "E" Line - Truss work continuing between TT "C" & "D"



"E" Line - Closer view of Truss Work



- **W2 - Pour 6 North Area - Curing & Cooling complete.**




Stripping inserts



W2- Stripping West Elevation



More West Elevation Stripping

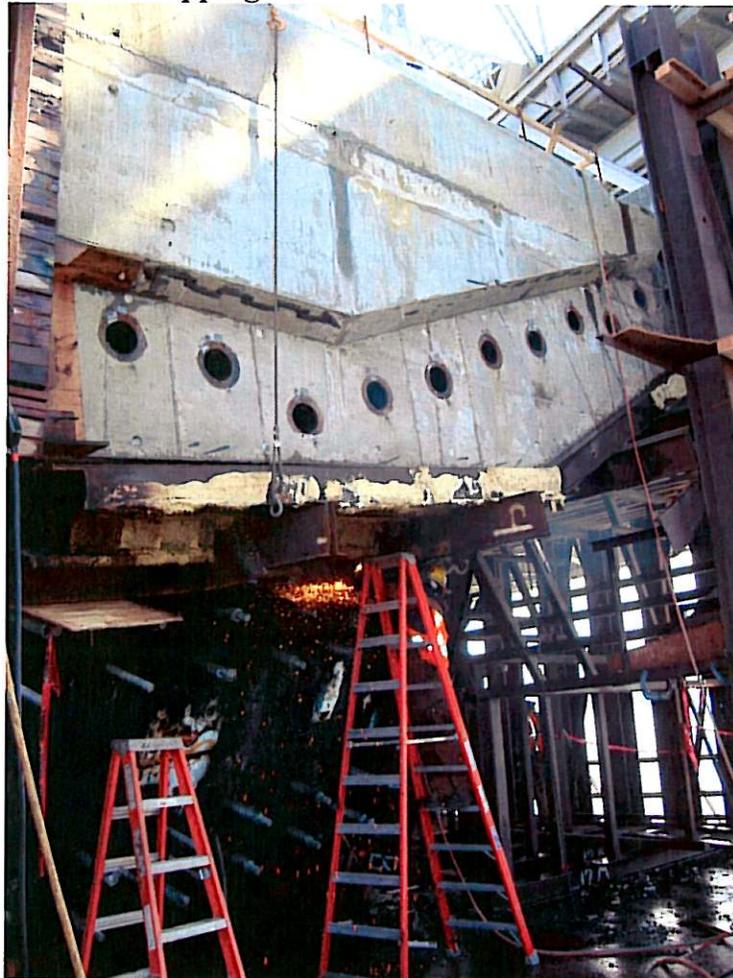

Stripping W2 East Elevation



Close-up of East Elevation Stripping

