

STATE OF CALIFORNIA  
DEPARTMENT OF TRANSPORTATION  
Contract 0120F - SFOBB - Superstructure  
Week ending 2009-03-13

Tuesday March 10, 2009: Observation from Engineer's boat between 0930 and 1000 -  
Clear, Cold and Calm

- E2 West Elevation - Note falsework lowering beams



**E2 - East Elevation**



RECT 09 MAR-16 H009064

**E2 - Removing form ties**



**E2 - West Elevation finished concrete**




**E2 - East Elevation - Finished concrete**



**E2 - North Elevation - patching concrete**



**E2 - South end**

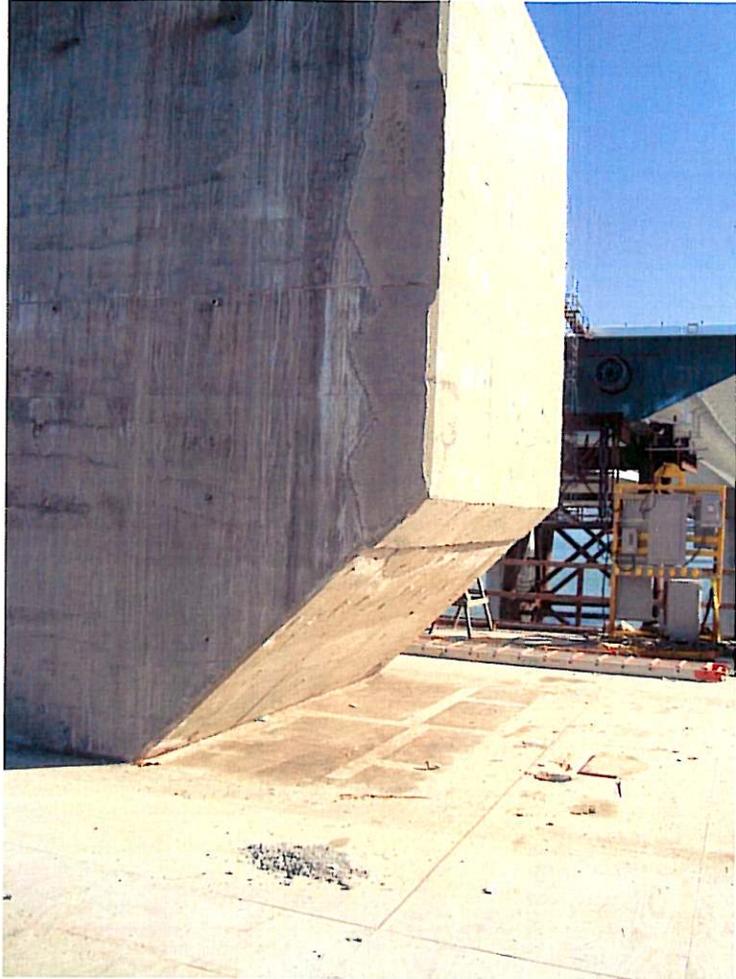

**E2 - View toward Skyway East Bound - Former Pedestrian Bridge location**



**E2 - View from South**



- **TT "GE" Driving frame - 1st lift Plumb Piles have been driven**



**TT "GE" - closer view from South East**



**TT "GE" - Big Digger Pile Driving Crane**




- **TT "F" - View from Northeast**




**TT "F" - No evidence of erecting Tower "FE"**



- **Temporary Truss East Line status to TT "D"**

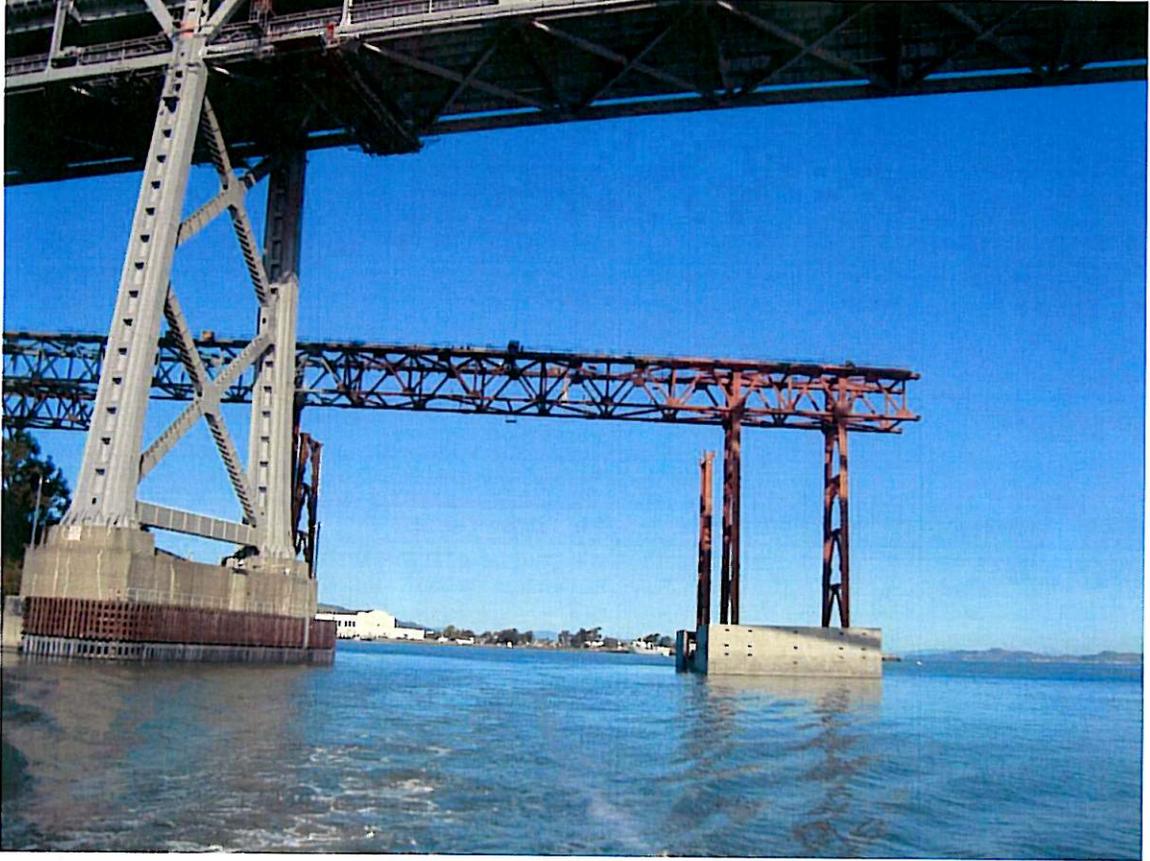

**Temporary Truss West Line Status to TT "B+"**

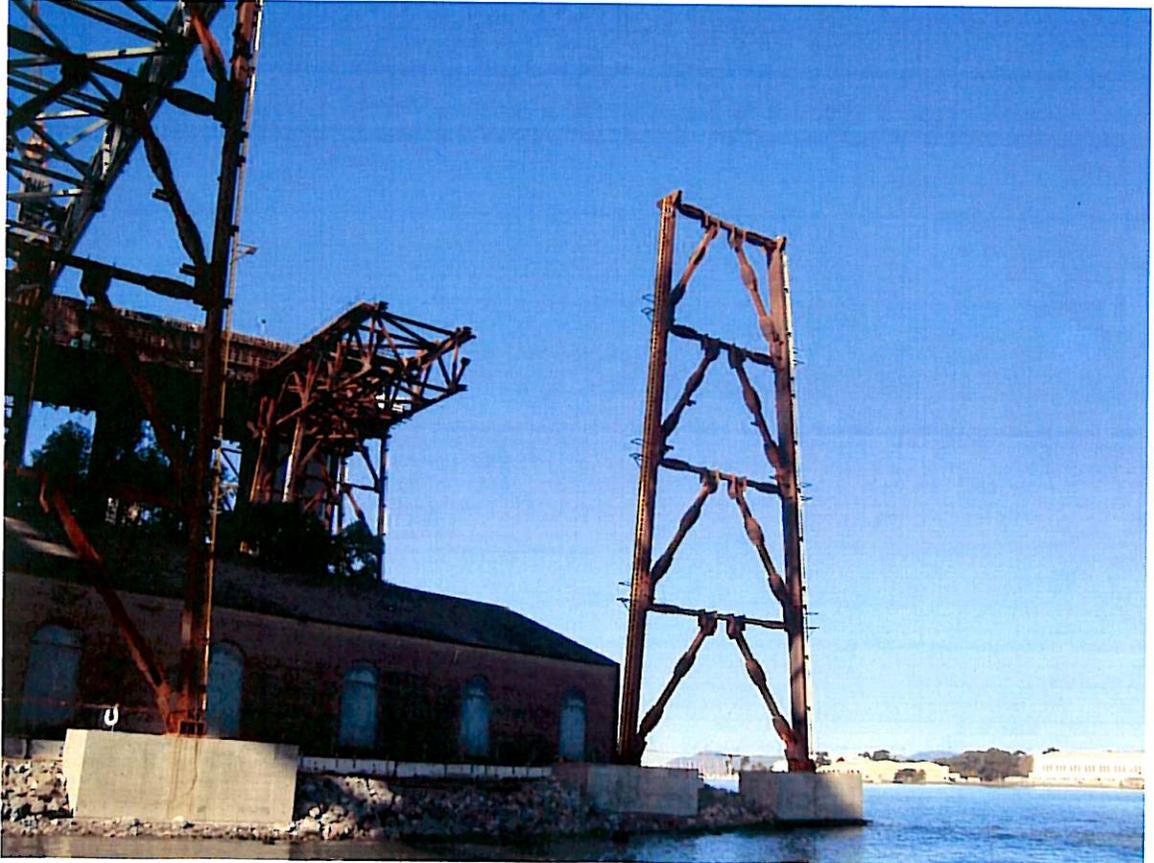

- **Assembling W Line Truss (B+ to D) @ Pier 7**



**Another view of Assembling Temporary Truss W Line (B+ to D)**



**Thursday March 12, 2009 : Observation from Yerba Buena Island - Generally Clear (some haze), cool, moderate wind**

- **E2 - West Elevation**



- **Temporary Tower "GE" Driving Frame - Prepping to drive 2<sup>nd</sup> lift plumb piles**




- **Temporary Tower "GE" - view showing support barge with supply of piles**



- **Temporary Tower "F" (in foreground) - Prepping to erect TT "FE"**




- **Temporary Truss E-Line - Bolting work continues (near TT "D")**

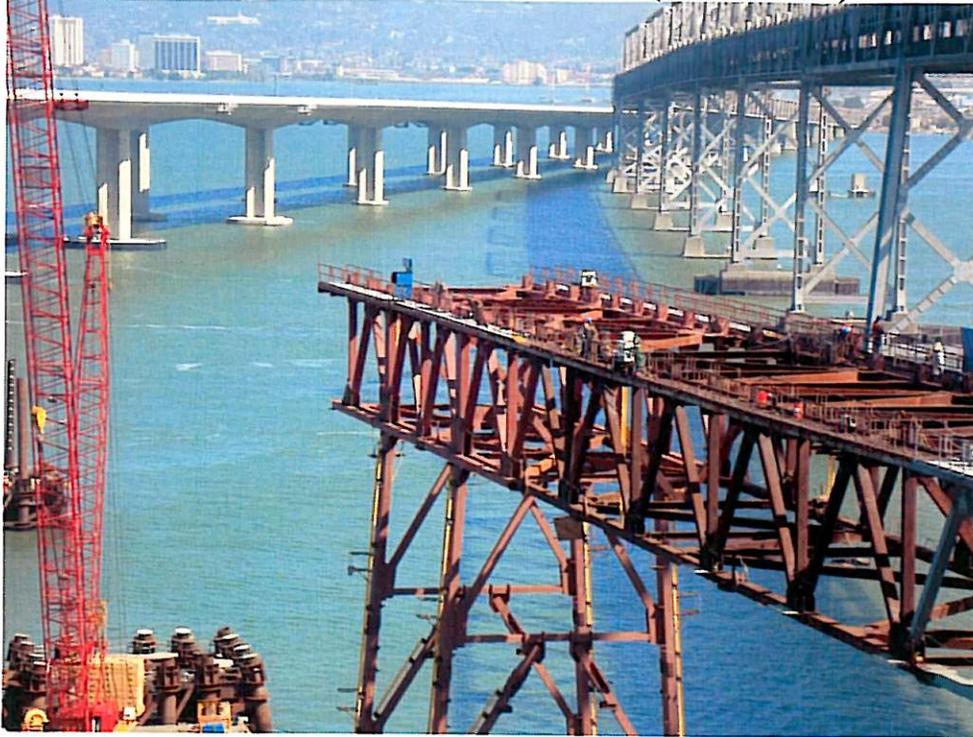

- **W2 - Form removal continues (Southwest corner)**



**W2 - Torch cutting of form shoring at Southwest corner**

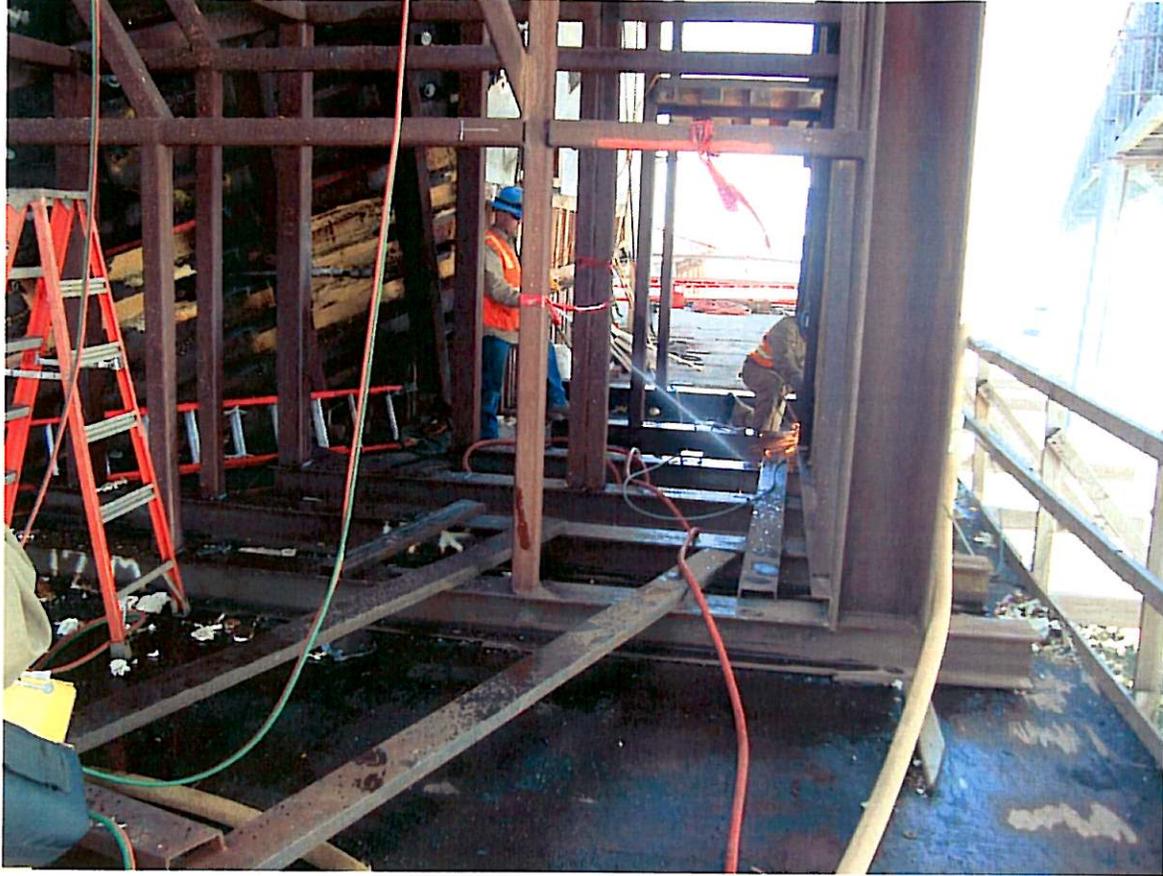

**W2 - Top Deck: stripping forms**



**W2 - Stripping forms East Elevation**



**W2 - Another view of form stripping at East elevation**



**W2 - Form stripping at South Elevation**




**W2 - More results of form stripping at South Elevation**



**W2 - Loosening strongback**



**W2 - "Flying" strongback**

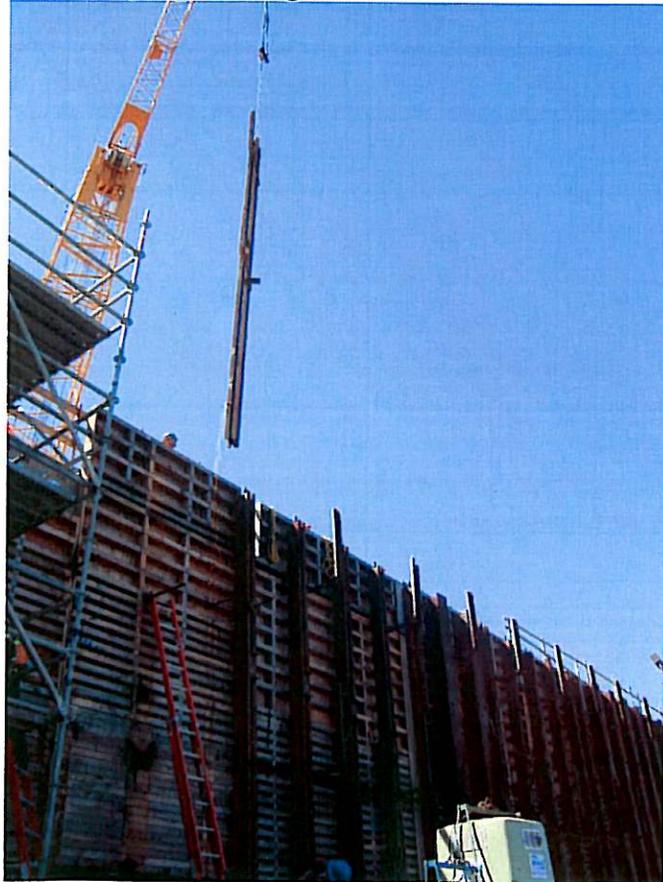

- **Shearleg Crane - Passing through Golden Gate**



**Shearleg Crane arriving (San Francisco skyline in background) - Note Starboard anchor at the ready - Proceeded to Anchorage south of Bay Bridge**

