



STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F - SFOBB - Superstructure

Tuesday April 14, 2009: Observation from Yerba Buena Island - between 0800 and 0900 - Clear, Cold and Windy

- E2 - West Elevation - Most of Falsework Shoring, including First lift has been removed



- "GE" Piles - (beyond "FE") Completed



REC'D 09 APR 20 #009272


- **View to East from W2 - E & W Line Trusses, Temp Towers "C", "D" & "F" "GE Piles" & E2**




- **W2 - From removal at Southwest Corner**



W2 - Providing Rebar stock for East Closure Pour

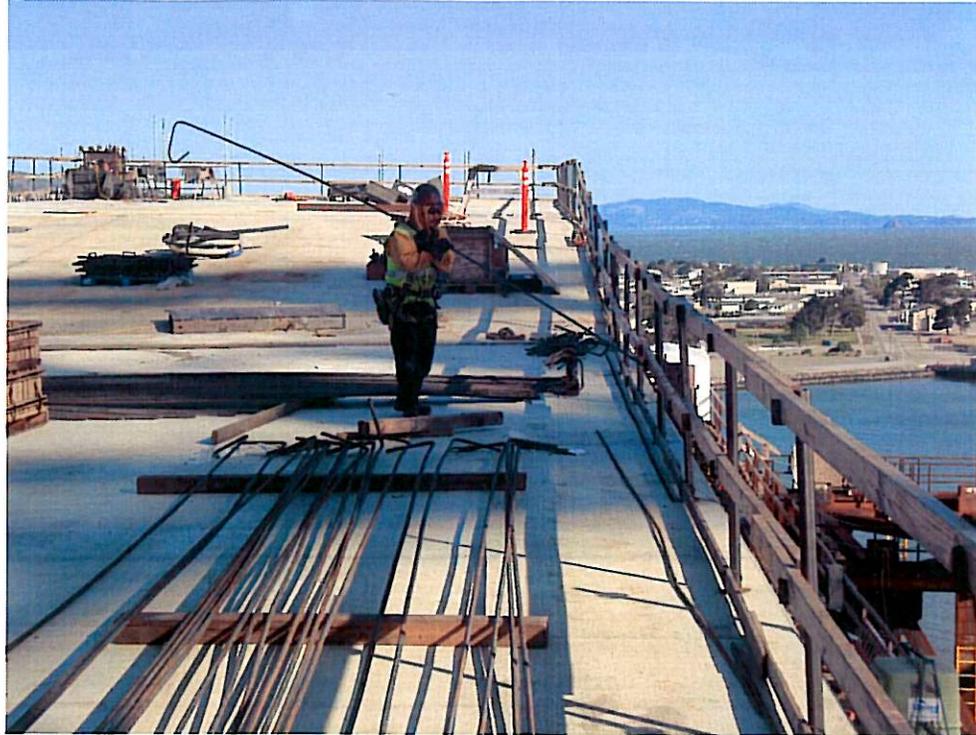

W2 - Installing Rebar at Southeast Closure Pour

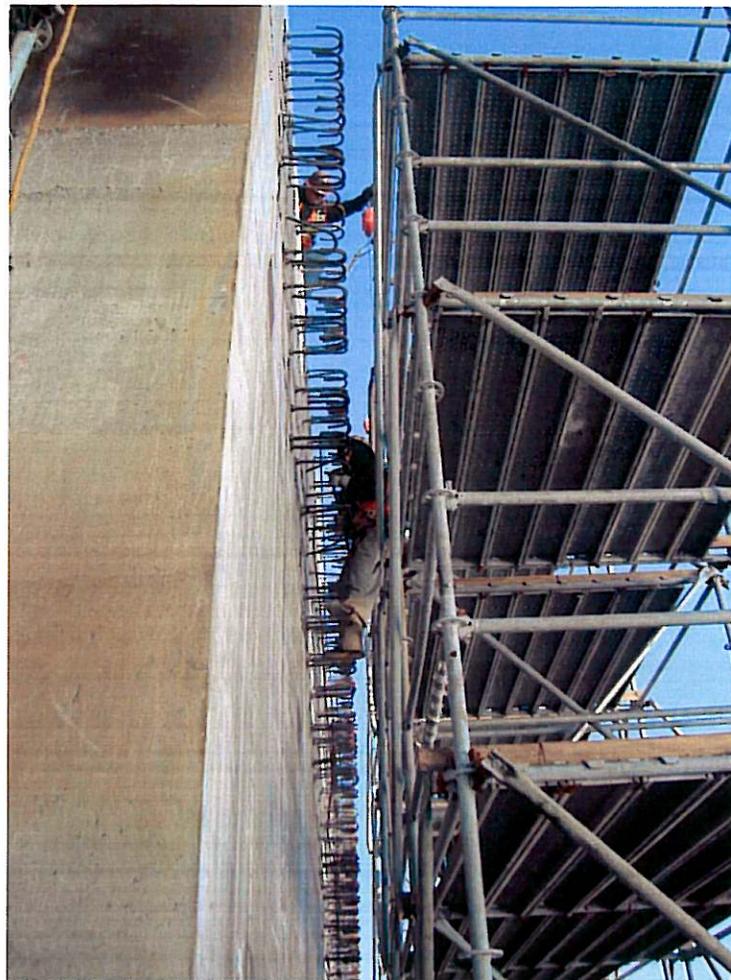

W2 - Southern portion of East Elevation - Currently installing Rebar for closure pour



W2 - Central & Northern portions of East Elevation



W2 - Entire East Elevation



W2 Removing soffit forms at East elevation Northern portion



W2 - Falsework in place at North Elevation to work on PT Ducts



W2 - Removing Forms from East Elevation



W2 - East Elevation Form removal status



W2 - View of East Elevation from South Corner



"GW" Driving Frame being assembled at Pier 7



"GW" - A second view



- Pier 7 - Prepping for arrival of 2nd ZPMC Temporary Works ship - Secured dock space (Note that Shearleg Crane has been moved from dockside)



Pier 7 - Secured area with Guard along side pier where ZPMC ship is expected to dock this afternoon



Looking for the ZPMC Ship to reach the Gate



Wednesday April 15, 2009 : Observation from Pier 7 Approximately 1215 to 1245 - Clear, Cool, Breezy

- ZPMC Ship "Zenhua 18" had spent last night at anchor in San Francisco Bay, apparently due to high winds. Cargo reported to contain Temp Trusses "D to G (E &W)," Temp Tower "H," and "Cradles 1-6 (E & W)."

Zenhua 18 being docked with tug assistance at Pier 7 - Bow view



Stern View



Port side view



View of Temporary Works cargo



U.S. Customs awaiting boarding



Thursday April 16, 2009: Observations from Pier 7 and from Engineers Boat Approximately 0930 to 1100 - Clear, Cool Light Breeze

- **E2- West Elevation - Removal of form shoring continues**



E2 - South (East Bound) Column - showing remaining form shores at that location



E2- North Column (West Bound) - removing form shores



E2 - View from North



- **"GE" piles - On right side of photo - "GW" Driving Frame scheduled to be positioned next Monday 4/20/2009**




"GE" piles closer view



- Temporary Towers "FE" & "FW"



- "E" Line Status to "TT-D"

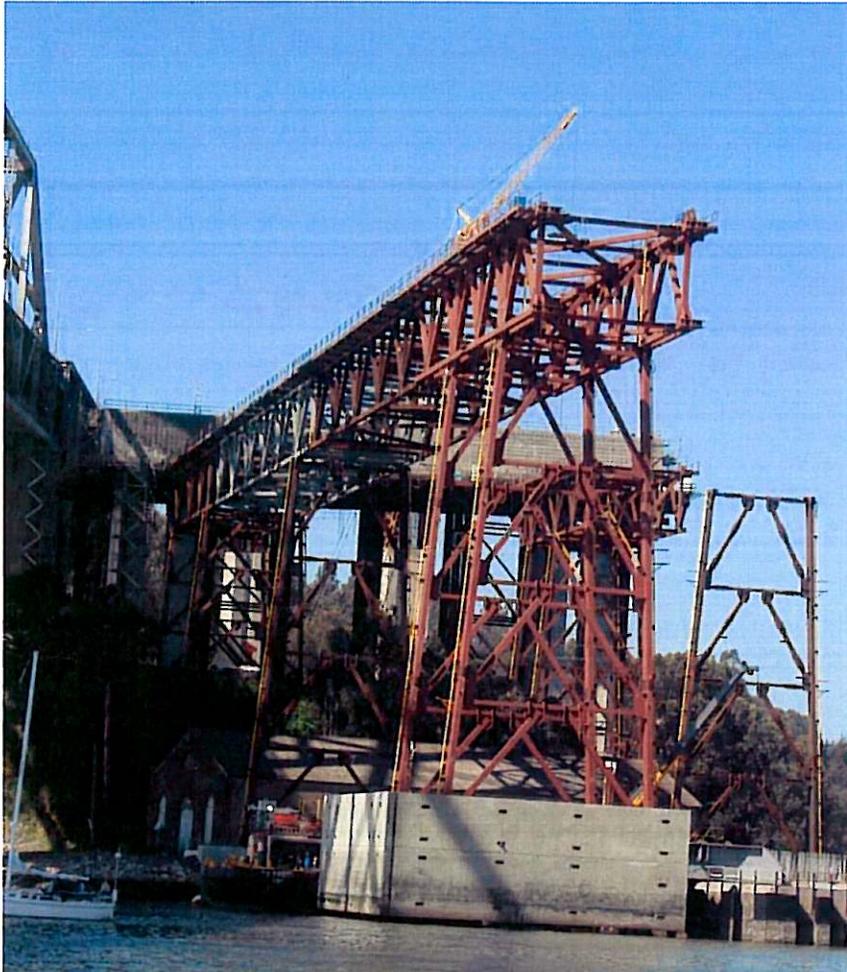

- **East Elevation of W2**



- **Temp Truss "W Line (B.5-D)" - Being assembled at Pier 7**



- **Shearleg Crane (West Coast Lifter) making first pick - unloading ZPMC ship Zhenhua 18**



Another photo of First Lift by "West Coast Lifter"



