

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 859
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1069
Form HC-10A (Rev. 6/80)	04-0120F4	Date	4/20/2009

MS

Weather: Clear and cool (AM)
Sunny and hot (PM)

Inspectors Hours	Start	0630	Stop	1700
Shift Hours	Start	0630	Stop	0630

ASSISTANT STRUCTURE REP.
JASON WILCOX

CONTRACTOR – TRAYLOR DUTRA JV

HOURS - ITEM NO. 8													
EQUIPMENT AND/OR LABOR:			REGULAR	OVERTIME	DOUBLE TIME	NIGHT PAY					IDLE OR DOWN	REMARKS	
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)										Name	Contractor
		Traylor Dutra											
		Foreman	4									Dan Dunn	ABF
		Ironworker	8									Hayes Steve Bastiste	ABF
		Ironworker	8									Declan Traenor	ABF
		Ironworker	8									Josue Galvan Jr	ABF
		Ironworker	8									Gabriel Rios	ABF
		Ironworker	8									Carlos Valverde	ABF

Description of Operation:
Erect Temporary Towers: 24 hour shift for placing TTGN; Access removal at TTFN

FIELD WORK:

Temp Tower G North:


I went out to the field around 1300 hours to check on the progress of the placing of the four plumb piles of Temp Tower G North. The node was brought out to the site first thing this morning and lashed up against the West side of the DB-5. Surveyors assisted on positioning the node while the four pile bottoms were picked and set through the node. Once all four pile bottoms were in position, the vibratory hammer was picked up and pile driving started around 1400 hours.



See Thanh Le's diary for the personnel and equipment for the day. Masoud Modanlou was on site in the afternoon to cover the operation as well. Ron Matin observed the evenings operation.

Temp Tower F North:

There was a small crew at the North tower of TTF removing scaffolding and performing general cleanup. All of the towers are already erected. The crew left at 1500 hours after working 8 hours. The foreman, Danny Dunn, left early today.

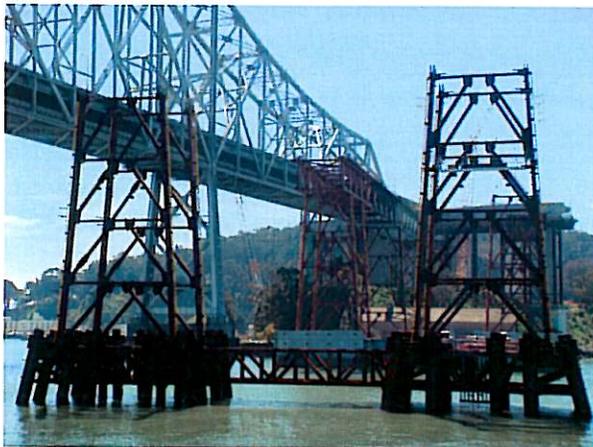

OFFICE WORK:

- Worked on Pay Estimate #36 in the morning.
- Attended Temp Tower staff Meeting at 0800 hours.
- Reviewed diaries
- Prepared for hosting the Safety Meeting this upcoming Thursday April 23, 2009.

OVERTIME: Accrued 2 hours of overtime covering the Contractors operations in the afternoon.

Inspector:

Jason Wilcox

Transportation Engineer (D)/Asst. Structure Rep.
