

JW

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 832
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1042
Form HC-10A (Rev. 6/80)	04-0120F4	Date	03/24/09

Inspectors Hours	Start	0630	Stop	1700
Shift Hours	Start	0630	Stop	1700

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR – ABFJV

THANH V LE

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS	
Equip. #	N O M E N (Of Equipment or Labor)	Regular	OT								IDLE OR DOWN	Name Contractor	
												Name	Contractor
	Big Digger barge	8											
	DB # 5 Marine barge	8											
	APE 600 Vibration hammer	0											
	Delmag 100 – Diesel hammer	0											
	Foreman	8	2									Terry Murray	Traylor Dutra
	Pile driver Journeyman	8	2									Gilbert Moya	Traylor Dutra
	Pile driver Journeyman	8	2									Price Adam	Traylor Dutra
	Operator	8	2									Joseph Boracci	Traylor Dutra
	Pile driver Journeyman	8	2									Ventura Ochoa	Traylor Dutra
	Pile driver Journeyman	8	2									Robert Utley	Traylor Dutra
	Pile driver Journeyman	8	2									Lee Tacker	
	Pile driver Journeyman	8	2									Danny Vega	Traylor Dutra
	Pile driver Journeyman	8	2									Stephen Mc Grew	Traylor Dutra
	Pile driver Journeyman	8	2									Jake Lavash	Traylor Dutra
	Pile driver Journeyman	8	2									Gary Lewis	Traylor Dutra
	Operator	8	2									Bud Germany	Traylor Dutra
	Operator	0	0									Steve Gordon	Traylor Dutra
	Pile driver Journeyman	8	2									Travis Logsdon	Traylor Dutra
	Operator	8	2									Kurt Dillard	Traylor Dutra
	Pile driver Apprentice	8	2									Richard Heibert J.	Traylor Dutra
	Pile driver Journeyman	8	2									Todd Labar	Traylor Dutra
	Pile driver Journeyman	8	2									Richard Heibert	Traylor Dutra
	Pile driver Journeyman	0	0									Adams Daniel	Traylor Dutra
	Pile driver Journeyman	0	0									Randall Lesley	Traylor Dutra
	Welding inspector	8	2									Andrew Erthum	CWI
	Welding inspector	8	2									Michael Johnson	Smith Emery
DB-5	Derrick Barge crane	8											
Big Digger		8											

Morty			8										
217			8										
L437	1	Multiquip Generator	8										
L478	1	Multiquip Generator								IDLE			
L270	1	Sullivan-Palatek Air Compressor	8										
	2	Red-D-Arc DC600 Welding Machines								IDLE			
P242	1	Manlift								IDLE			
L624	1	Light Station								IDLE			
L625	1	Light Station								IDLE			
L626	1	Light Station								IDLE			
L629	1	Light Station								IDLE			


Weather: Partly Cloudy Hi 67 °F, Lo 46 °F,


**Description of Operation:**

**1. Temporary Tower G -South: Pile splicing**


**Activities:**

1. Office work:
  - Review plans, special provisions, RFI and ABF submittals for TTG
2. Field work:
  - Db5 crew continued pile splicing operation: finished and UT @ G105 and G106, 50% completed G114.
  - Welder crew continued sealed welding at the backing bars for 48" dia. piles on Morty barge, shear plate welding on piles G125 and G128, and fresh head pile G114.
  - Michael Johnson and Andrew Erthum were present for QA/QC welding inspection.
3. Conversation and discussion:
4. Overtime reason:  
Worked two hours overtime for construction observation because contractor worked overtime.

Thanh V Le  Trans Engineer (D)/Asst. Struct. Rep

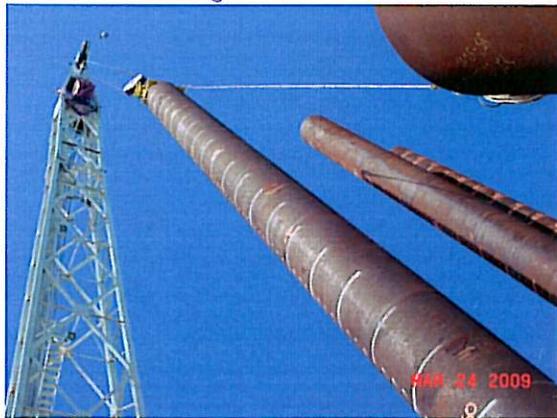

Lifting the top section of piles

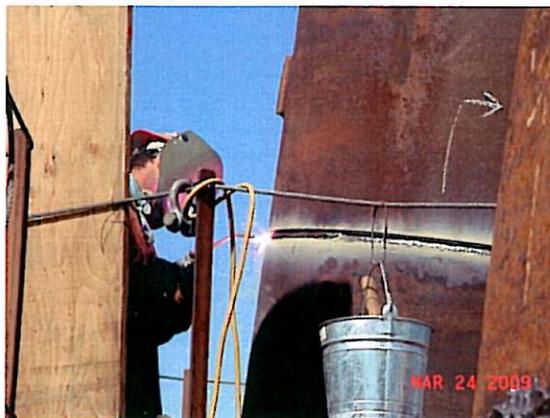

Pile splicing welding
