

15

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 839
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1049
Form HC-10A (Rev. 6/80)	04-0120F4	Date	03/31/09

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1700

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

THANH V LE

		HOURS - ITEM NO.												
EQUIPMENT AND/OR LABOR:		Regular	OT									IDLE OR DOWN	REMARKS	
Equip. #	NO. MEN												DESCRIPTION (Of Equipment or Labor)	Name
		8	2										Terry Murray	Traylor Dutra
		8	2										Gilbert Moya	Traylor Dutra
		8	2										Price Adam	Traylor Dutra
		8	2										Joseph Boracci	Traylor Dutra
		8	2										Ventura Ochoa	Traylor Dutra
		8	2										Robert Utley	Traylor Dutra
		8	2										Lee Tacker	
		8	2										Danny Vega	Traylor Dutra
		8	2										Stephen Mc Grew	Traylor Dutra
		8	2										Jake Lavash	Traylor Dutra
		8	2										Gary Lewis	Traylor Dutra
		8	2										Bud Germany	Traylor Dutra
		8	2										Steve Gordon	Traylor Dutra
		8	2										Travis Logsdon	Traylor Dutra
		8	2										Kurt Dillard	Traylor Dutra
		8	2										Richard Heibert J.	Traylor Dutra
		8	2										Todd Labar	Traylor Dutra
		8	2										Richard Heibert	Traylor Dutra
		0	0										Adams Daniel	Traylor Dutra
		8	2										Randall Lesley	Traylor Dutra
		8	2										Andrew Erthum	CWI
		8	2										Michael Johnson	Smith Emery
DB-5		8												
Big Digger		8												
Morty		8												
217		8												
L437	1	8												
L47B	1											IDLE		

L270	1	Sullivan-Palatek Air Compressor	8											
	2	Red-D-Arc DC600 Welding Machines											IDLE	
P242	1	Manlift											IDLE	
L624	1	Light Station											IDLE	
L625	1	Light Station											IDLE	
L626	1	Light Station											IDLE	
L629	1	Light Station											IDLE	
		APE 600 Vibration hammer	0											
		Delmag 100 – Diesel hammer	0											

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F,

Description of Operation:

1. Temporary Tower G -South: Pile shear plate welding – driving frame TTG North assemble.


Activities:


1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTG
2. Field work:
 - At TTG South: Big Digger crew performed works as following:
 1. Continued shear plate welding – finished piles G105,G106, G113 and G126 – on going G114,G124,G108 and G107
 2. Cutting off six 42" dia. piles at elevation of two feet above top ring of the annulus.
 - Michael Johnson and Andrew Erthum were present for QA/QC welding inspection.
 - Berth 7: DB5 crew performed works as following:
 1. Setting one middle section of the TTG North driving frame.
 2. Continued to install working platform at bottom and top decks of driving frame.
 3. Removed temporary attachments.
 4. Installed safety handrail on the top deck.

3. Conversation and discussion:

4. Overtime reason:

Worked eight hours overtime for construction observation because contractor worked on State holiday.

Thanh V Le  Trans Engineer (D)/Asst. Struct. Rep

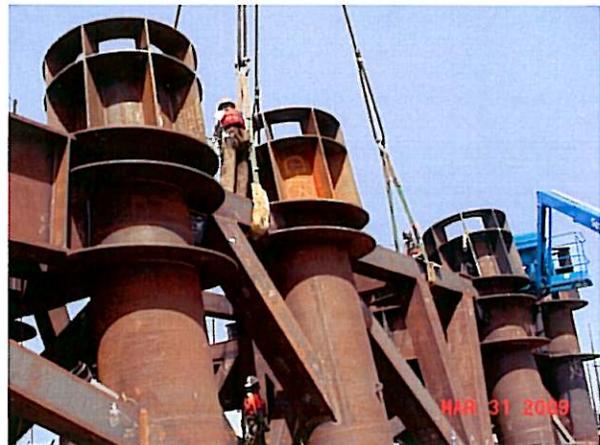

TTG North node assemble in progress
