

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 841
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1051
Form HC-10A (Rev. 6/80)	04-0120F4	Date	04/02/09

Inspectors Hours	Start	0630	Stop	1700
Shift Hours	Start	0630	Stop	1700

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR – ABFJV

THANH V LE

		HOURS - ITEM NO.												
		Regular	OT									IDLE OR DOWN	REMARKS	
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)											Name	Contractor
		Foreman	8	2									Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	2									Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	8	2									Price Adam	Traylor Dutra
		Operator	8	2									Joseph Boracci	Traylor Dutra
		Pile driver Journeyman	8	2									Ventura Ochoa	Traylor Dutra
		Pile driver Journeyman	8	2									Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	2									Lee Tacker	
		Pile driver Journeyman	8	2									Danny Vega	Traylor Dutra
		Pile driver Journeyman	8	2									Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	8	2									Jake Lavash	Traylor Dutra
		Pile driver Journeyman	8	2									Gary Lewis	Traylor Dutra
		Operator	8	2									Bud Germany	Traylor Dutra
		Operator	8	2									Steve Gordon	Traylor Dutra
		Pile driver Journeyman	8	2									Travis Logsdon	Traylor Dutra
		Operator	8	2									Kurt Dillard	Traylor Dutra
		Pile driver Apprentice	8	2									Richard Heibert J.	Traylor Dutra
		Pile driver Journeyman	8	2									Todd Labar	Traylor Dutra
		Pile driver Journeyman	8	2									Richard Heibert	Traylor Dutra
		Pile driver Journeyman	0	0									Adams Daniel	Traylor Dutra
		Pile driver Journeyman	8	2									Randall Lesley	Traylor Dutra
		APE 600 Vibration hammer	0											
		Delmag 100 – Diesel hammer	0											
DB-5		Derrick Barge crane	8											
Big Digger			8											
Morty			8											
217			8											
L437	1	Multiquip Generator	8											
L478	1	Multiquip Generator										IDLE		

L270	1	Sullivan-Palatek Air Compressor	8																
	2	Red-D-Arc DC600 Welding Machines																	IDLE
P242	1	Manlift																	IDLE
L624	1	Light Station																	IDLE
L625	1	Light Station																	IDLE
L626	1	Light Station																	IDLE
L629	1	Light Station																	IDLE


Weather: Partly Cloudy Hi 67 °F, Lo 46 °F,


**Description of Operation:**

**1. Temporary Tower G -South: Pile shear plate welding TTG South – Assemble North TTG driving frame.**

**Activities:**

1. Office work:
  - Review plans, special provisions, RFI and ABF submittals for TTG
2. Field work:
  - At TTG South: Big Digger crew performed work as follows:
    1. Continued shear plate welding on piles G107,105, and G106.
    2. Cutting off four 48" dia. piles at elevation of two feet above top ring of the annulus.
  - Michael Johnson and Andrew Erthum were present for QA/QC welding inspection.
  - Berth 7: DB5 crew performed works as following:
    1. Drilling and bolting bottom deck.
    2. Continued installing jacking system attachment.
    3. Continued installing working platform and safety handrail on top deck.
3. Conversation and discussion:
4. Overtime reason:  
Worked two hours overtime for construction observation because contractor worked overtime.

Thanh V Le  Trans Engineer (D)/Asst. Struct. Rep

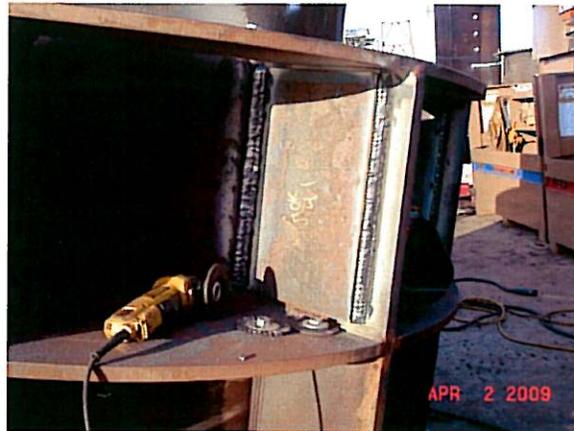

Shear plate welding in progress
