

afm

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 772
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 982
Form HC-10A (Rev. 6/80)	04-0120F4	Date	01/23/09

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

HOURS - ITEM NO.													REMARKS	
EQUIPMENT AND/OR LABOR:			Item 48 - Bar Reinforcing Steel (Bridge)									IDLE OR DOWN	Name Contractor	
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor) Regional Steel											Name	Contractor
1	1	General Foreman	8										Bognaes, Bob	RSC
2	1	Foreman	8										Greenlee, Tim	RSC
3	1	Ironworker	8										Pelayo, Jose	RSC
4	1	Ironworker	8										Reyes, Danial	RSC
5	1	Ironworker	8										Quiroz, Victor	RSC
6	1	Ironworker	0										Quiroz, Fermin	RSC
7	1	Ironworker	8										Ortiz, Lucino	RSC
8	1	Ironworker	0										Hurtado, Armando	RSC
9	1	Ironworker	0										Reyes, Franco	RSC
10	1	Ironworker	8										Rasmussen, John	RSC
11	1	Ironworker	0										Vasquez, Alvaro	RSC
12	1	Ironworker	8										Dennison, Andrew	RSC

Weather: Cloudy, scattered showers, cool, Hi 60 F Lo 50 F.

Description of Operation:

ABF

- See L. Mathur and M. Bruce diary for labor, equipment and remarks.

Daily for Regional Steel

North Side W2:


- RSC installing support bars for #43 transverse mat.
- RSC continue to install #43 transverse rebar between east face and cable tie down.

South Side W2:

- RSC installed bike path reinforcement southwest side.
- RSC continue to install #25 longitudinal hairpins.

NOTES:

- ABF/RSC complaining they cannot install 8 vertical spacing #25 form savers by 10 horizontal spacing #25 form savers at the upper southwest location. They can only install 8 vertical by 8 horizontal form savers. I discuss with T. Ho TYLin he said OK but add 4 #25 within center of 8 by 8 configuration – see drawing below. I informed B. Bedwell of change.

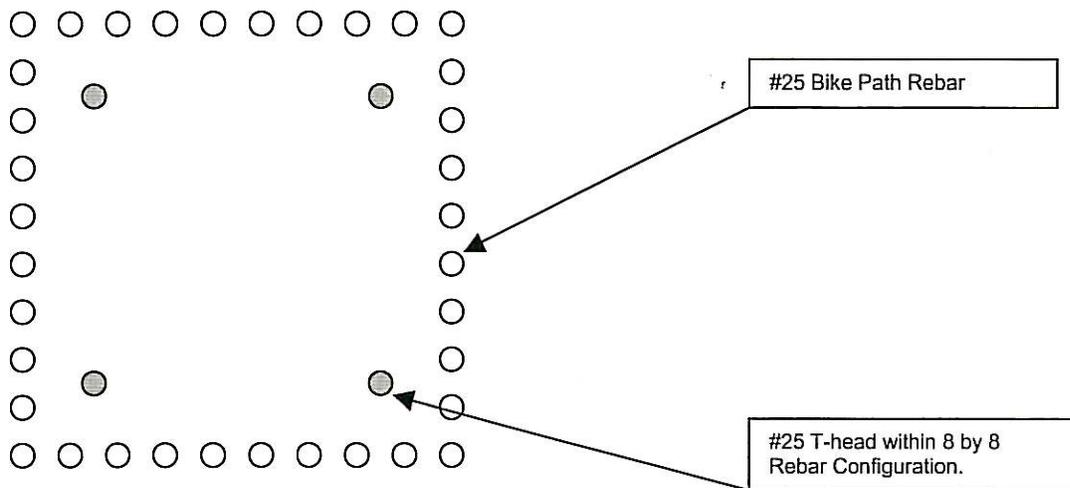

Office

- Wrote diaries.
- Misc job related office tasks.
- Review & responded to email.
- Reviewed bike path and barrier rebar plan sheets.

Inspector:

Pamela Gagnier *Pamela Gagnier* Trans Engineer (C)/Asst. Struct. Rep
