

JW

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 835
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1045
Form HC-10A (Rev. 6/80)	04-0120F4	Date	03/27/09

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

THANH V LE

		HOURS - ITEM NO.											
		Regular	OT								IDLE OR DOWN	REMARKS	
												Name	Contractor
EQUIPMENT AND/OR LABOR:													
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)											
		Foreman	0	0								Terry Murray	Traylor Dutra
		Pile driver Journeyman	0	0								Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	0	0								Price Adam	Traylor Dutra
		Operator	0	0								Joseph Boracci	Traylor Dutra
		Pile driver Journeyman	0	0								Ventura Ochoa	Traylor Dutra
		Pile driver Journeyman	0	0								Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	0								Lee Tacker	
		Pile driver Journeyman	8	0								Danny Vega	Traylor Dutra
		Pile driver Journeyman	8	0								Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	8	0								Jake Lavash	Traylor Dutra
		Pile driver Journeyman	8	0								Gary Lewis	Traylor Dutra
		Operator	8	0								Bud Germany	Traylor Dutra
		Operator	0	0								Steve Gordon	Traylor Dutra
		Pile driver Journeyman	0	0								Travis Logsdon	Traylor Dutra
		Operator	8	0								Kurt Dillard	Traylor Dutra
		Pile driver Apprentice	0	0								Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	0	0								Todd Labar	Traylor Dutra
		Pile driver Journeyman	0	0								Richard HIEbert	Traylor Dutra
		Pile driver Journeyman	0	0								Adams Daniel	Traylor Dutra
		Pile driver Journeyman	0	0								Randall Lesley	Traylor Dutra
		Welding inspector CWI	8	0								Andrew Erthum	CWI
		Welding inspector CWI	8	0								Michael Johnson	Smith Emery
DB-5		Derrick Barge crane	8										
Big Digger			8										
Morty			8										
217			8										
L437	1	Multiquip Generator	8										
L478	1	Multiquip Generator									IDLE		

L270	1	Sullivan-Palatek Air Compressor	8										
	2	Red-D-Arc DC600 Welding Machines										IDLE	
P242	1	Manlift										IDLE	
L624	1	Light Station										IDLE	
L625	1	Light Station										IDLE	
L626	1	Light Station										IDLE	
L629	1	Light Station										IDLE	
		APE 600 Vibration hammer	0										
		Delmag 100 – Diesel hammer	0										

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F,


Description of Operation:


1. Temporary Tower G -South: Pile shear plate welding

Activities:

1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTG
2. Field work:
 - Today, Big Digger crew performed works as following:
 1. Continued shear plate welding – finished piles G128, G127, G125 and G123 – on going G113, G126 and G 124.
 2. Removed formwork at bottom of annulus at vertical piles
 - Michael Johnson and Andrew Erthum were present for QA/QC welding inspection.
 - DB5 on the way to Vallejo to pick up TTG North driving frame.
3. Conversation and discussion:

4. Overtime reason:

Thanh V Le  Trans Engineer (D)/Asst. Struct. Rep

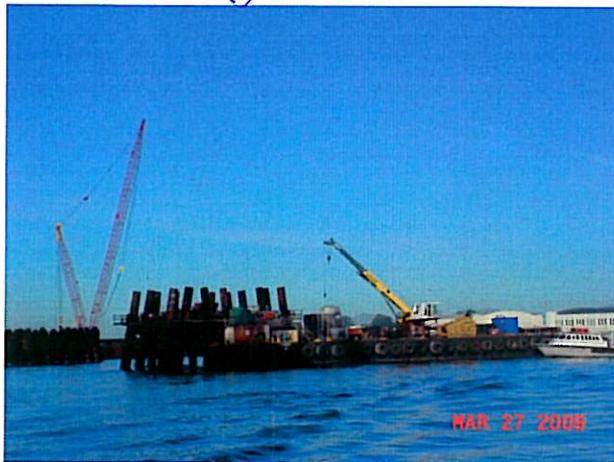

TTG South shear plate welding in progress
