

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 861
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1071
Form HC-10A (Rev. 6/80)	04-0120F4	Date	04/22/2009

Inspectors Hours	Start	1000	Stop	2130
Shift Hours	Start	24/24	Stop	24/24

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

THANH V LE

EQUIPMENT AND/OR LABOR:			HOURS - ITEM NO.								IDLE OR DOWN	REMARKS	
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT								Name	Contractor
		Foreman	8	2							Day	Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	2							Day	Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	8	2							Day	Price Adam	Traylor Dutra
		Operator	8	2							Day	Joseph Boracchi	Traylor Dutra
		Pile driver Journeyman	8	2							Day	Ventura Ochoa	Traylor Dutra
		Pile driver Journeyman	8	2							Day	Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	2							Day	Travis Logsdon	Traylor Dutra
		Operator	8	2							Day	Kurt Dillard	Traylor Dutra
		Pile driver Apprentice	8	2							Day	Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	8	2							Day	Todd Labar	Traylor Dutra
		Pile driver Journeyman	8	2							Day	Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	8	4							Night	Lee Tacker	
		Pile driver Journeyman	8	4							Night	Danny Vega	Traylor Dutra
		Pile driver Journeyman	8	4							Night	Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	8	4							Night	Jake Lavash	Traylor Dutra
		Pile driver Journeyman	8	4							Night	Gary Lewis	Traylor Dutra
		Operator	8	4							Night	Bud Germany	Traylor Dutra
		Operator	8	4							Night	Steve Gordon	Traylor Dutra
DB-5		Derrick Barge crane	8										
Big Digger		Marine barge	8										
Morty		Marine barge	8										
		Delmag 100	4										
		APE 600 - Vibrator									IDLE		
217		Marine barge	8										
L437	1	Multiquip Generator	8										
L472	1	Power Generation Cummine	8										
L478	1	Multiquip Generator									IDLE		
L270	1	Sullivan-Palatek Air Compressor	8										

	2	Red-D-Arc DC600 Welding Machines	8											
P242	1	Manlift	8											
L624	1	Light Station	8											
L625	1	Light Station	8											
L626	1	Light Station	8											
L629	1	Light Station	8											



**Weather:** Partly Cloudy Hi 67 °F, Lo 46 °F.

**Description of Operation:**

**1. Temporary Tower G: Pile driving TTG North/Pile splicing welding. ( 24/24 operation)**

**Activities:**

1. Office work:
  - Review plans, special provisions, RFI and ABF submittals for TTF and TTG
2. Field work:
  - A. Day shift:
    - DB5 crew drove four vertical piles to elevation 10.625 top of piles.( G129,G139, G131 and G132)
    - See Masoud Madanlou for pile driving blowcounts.
    - The crew continued installed working platform outer face of TTG north.
  - B. Night shift:
    - DB5 crew installed jacking system on top of piles G129, G130, G131 and G132.
    - Ron Martin was on board for night shift construction observation.
3. Conversation and discussion:
4. Overtime reason:  
Worked three hours overtime for construction observation because contractor worked overtime.

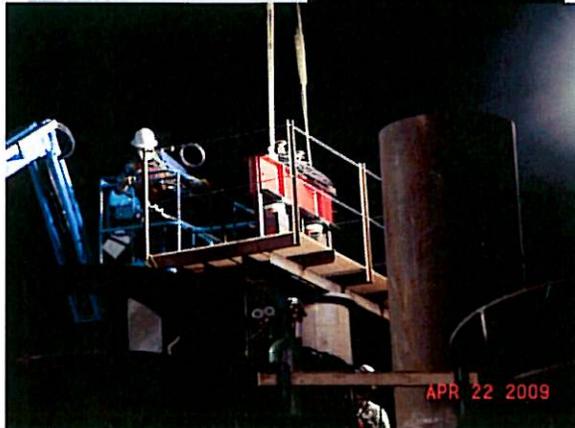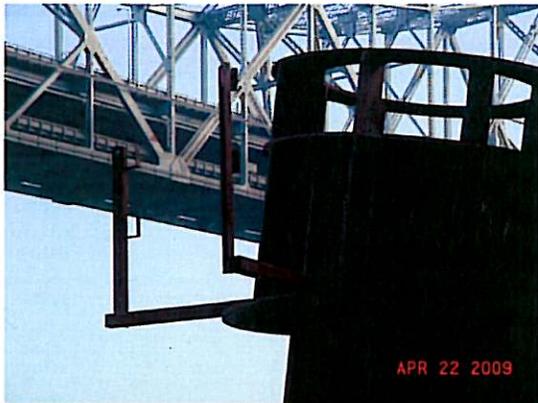

Jacking system installation

THAN H V. LE  
*[Handwritten signature]*
