

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 862
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1072
Form HC-10A (Rev. 6/80)	04-0120F4	Date	04/23/2009

Inspectors Hours	Start	8000	Stop	2130
Shift Hours	Start	24/24	Stop	24/24

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

THANH V LE

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS	
Equip. #	N O · M E N	DESCRIPTION (Of Equipment or Labor)	Regular	OT							IDLE OR DOWN	Name Contractor	
												Name	Contractor
		Foreman	8	4							Day	Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	4							Day	Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	8	4							Day	Price Adam	Traylor Dutra
		Operator	8	4							Day	Joseph Boracci	Traylor Dutra
		Pile driver Journeyman	8	4							Day	Ventura Ochoa	Traylor Dutra
		Pile driver Journeyman	8	4							Day	Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	4							Day	Travis Logsdon	Traylor Dutra
		Operator	8	4							Day	Kurt Dillard	Traylor Dutra
		Pile driver Apprentice	8	4							Day	Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	8	4							Day	Todd Labar	Traylor Dutra
		Pile driver Journeyman	8	4							Day	Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	8	4							Night	Lee Tacker	
		Pile driver Journeyman	8	4							Night	Danny Vega	Traylor Dutra
		Pile driver Journeyman	8	4							Night	Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	8	4							Night	Jake Lavash	Traylor Dutra
		Pile driver Journeyman	8	4							Night	Gary Lewis	Traylor Dutra
		Operator	8	4							Night	Bud Germany	Traylor Dutra
		Operator	8	4							Night	Steve Gordon	Traylor Dutra
DB-5		Derrick Barge crane	8										
Big Digger		Marine barge	8										
Morty		Marine barge	8										
		Delmag 100									IDLE		
		APE 600 - Vibrator									IDLE		
217		Marine barge	8										
L437	1	Multiquip Generator	8										
L472	1	Power Generation Cummine	8										
L478	1	Multiquip Generator									IDLE		
L270	1	Sullivan-Palatek Air Compressor	8										

	2	Red-D-Arc DC600 Welding Machines	8										
P242	1	Manlift	8										
L624	1	Light Station	8										
L625	1	Light Station	8										
L626	1	Light Station	8										
L629	1	Light Station	8										

**Weather:** Partly Cloudy Hi 67 °F, Lo 46 °F.

**Description of Operation:**

**1. Temporary Tower G: Shear plate welding. ( 24/24 operation)**



**Activities:**

1. Office work:
  - Review plans, special provisions, RFI and ABF submittals for TTF and TTG
  - 0800-1000: Safety Awareness Meeting.
2. Field work:
  - A. Day shift:
    - At 1043 AM, DB5 crew started lowering the driving frame to design elevation.
    - Troy Wahler – Traylor’s surveyor – was present to monitor elevation and position of the driving frame.
    - Mark Baker from TCI, Andrew Erthurm from CWI, and William Norris from Smith Emery were present for QA/ QC inspection.
    - Welding crew started shear plate welding at 1500, there are three welders at day shift such as: Ventura Ochoa, Gilbert Moya and Price Adam. Six shear plates were completed for pile G129, G131 and G132.
  - B. Night shift:
    - DB5 crew continued shear plate welding on piles G129, G130, G131 and G132.
    - Ron Martin was on board for night shift construction observation.
3. Conversation and discussion:
4. Overtime reason:
 


Worked four hours overtime for construction observation because contractor worked overtime.



Shear plates welding

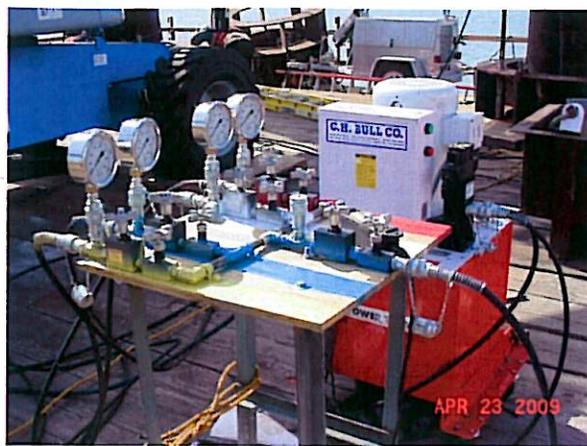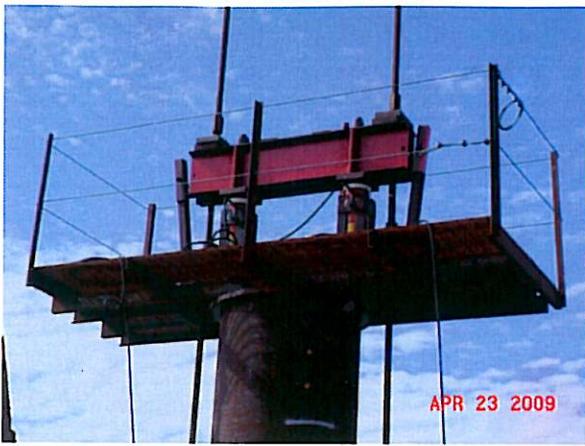

Jacking system

Thanh V Le  Trans Engineer (D)/Asst. Struct. Rep
