

Job Stamp
 04-0120F4
 SFOBB SAS

Const. Calendar Day No **885**
 Project Work Day No. **1095**
 Date **05/16/2009**
 Shift Hours Start **7:00** Stop **5:30**
 Inspector Shift **7:00 AM to 5:00 PM**

ASSISTANT STRUCTURAL
 REPRESENTATIVE.

CONTRACTOR - ABFJV

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
		Regular	Over Time	Surveying										IDLE OR DOWN
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)												
	1	Temp tower and trusses												
		Operator	8										Rodney Anderson	ABF/ JV
		Iron worker Foreman	8										Frank Brajkovich	ABF/ JV
		Iron worker Jrny	8										M Maday	ABF/ JV
		Iron worker Jrny	8										Richrd. Bazewicz	ABF/ JV
		Iron worker Jrny	8										Rory Hogan	ABF/ JV
		Iron worker Jrny	8										Carlos Valverde	ABF/ JV
		Iron worker Jrny												ABF/ JV
		Iron worker Jrny	8										Salvador Sandoval	ABF/ JV
		Iron worker Jrny	8										Harold W. Wheeler	ABF/ JV
		Iron worker Jrny	8										James Zhen	ABF/ JV
		Iron worker App.	8										Todd Jackson	ABF/ JV
		Iron worker App.	8										Ryan Lockwood	ABF/ JV
														ABF/ JV
														ABF/ JV
														ABF/ JV
	4	Welding machine												ABF/ JV
58084	1	RT 160 crane												ABF/ JV
6- 18-4293, 4217	2	IR Compressor												ABF/ JV
549 07 5006	1	Generator												ABF/ JV
OC 260, 261, 262, 265	4	Barge												ABF/ JV

Weather: Sunny, 75 F


Description of Operation:

Trusses

1. No activities on temporary towers or trusses on this weekend's day.

Miscellaneous

Additional Work on/off site:

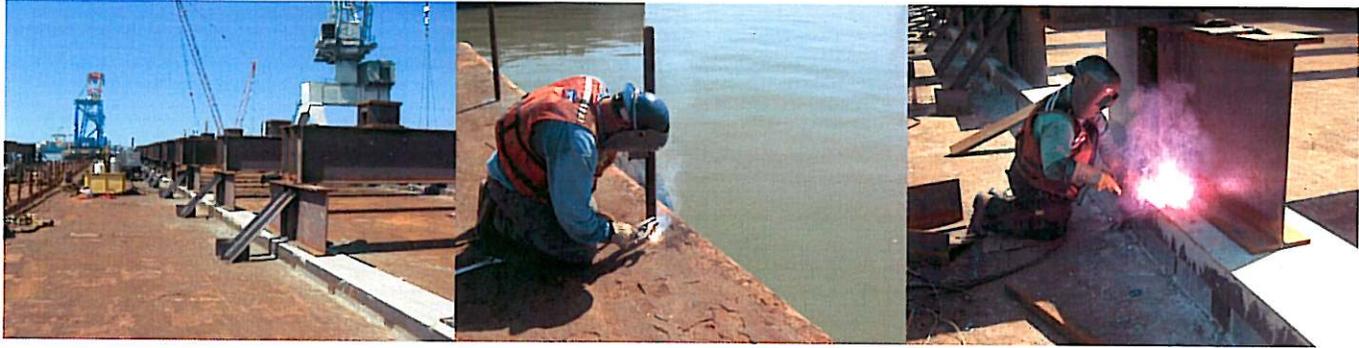

1. Cutting and welding steel pipe for barge's guardrails.
2. Welding guardrail stands.
3. Welding W 36 x 160 # section with embedded plate to support double stringers.
4. Welding T section on barge floor.
5. Welding angle iron to T section and W 36 x 160 # for bracing.
6. I worked 4.00 hours overtimes to cover contractor operation.

Inspector:

Masoud Modanlou  Trans Engineer (C)/Asst. Struct. Rep
