




STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 1020F - SFOBB -SAS - Superstructure
Larry Gustafson - Senior Scheduler
Week Ending 29-May-2009

Tuesday May 26, 2009: Observation from Engineer's Boat between 1315 and 1430 - Hazy sun, Cool and light wind.

- E2 - Westerly Elevation - Foundation deck has had soffit deck form material removed

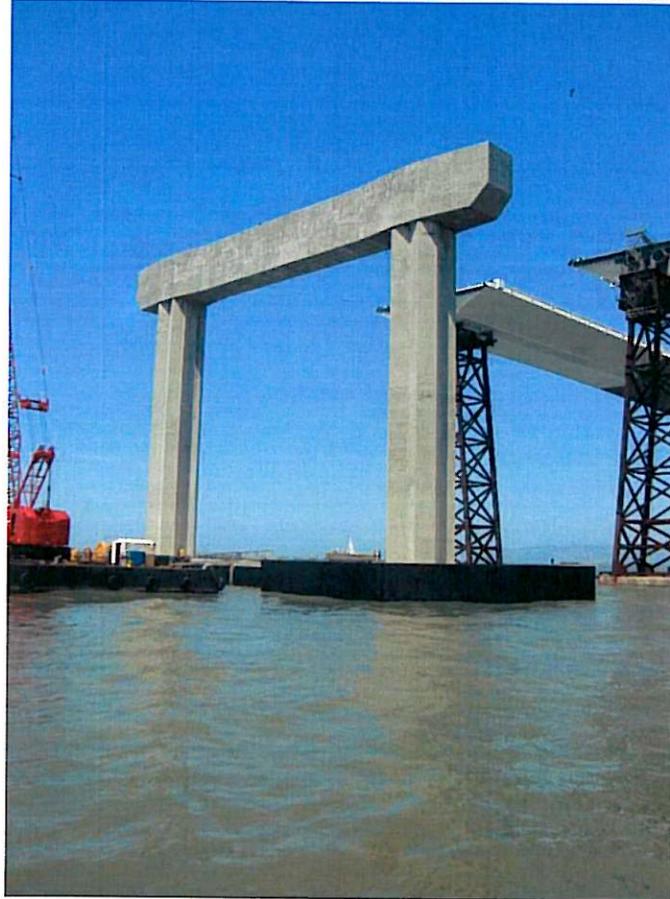

E2 - Prepping to remove support barge



REC'D '09 JUN-05 #009774

- **GW Foundation - Pile sleeve grouting in progress**



GW - Closer view



GW - Showing grouting equipment



GW & GE - West Elevation



- **Temporary "F" Towers - no observed activity**




- **W2 - East Elevation form water level**



- **T1 Foundation with Temporary "D" Towers - No observed activity**



- **E Line Temporary Truss @ ("D" +) - extension in progress - prepping for D-F East Truss lift**

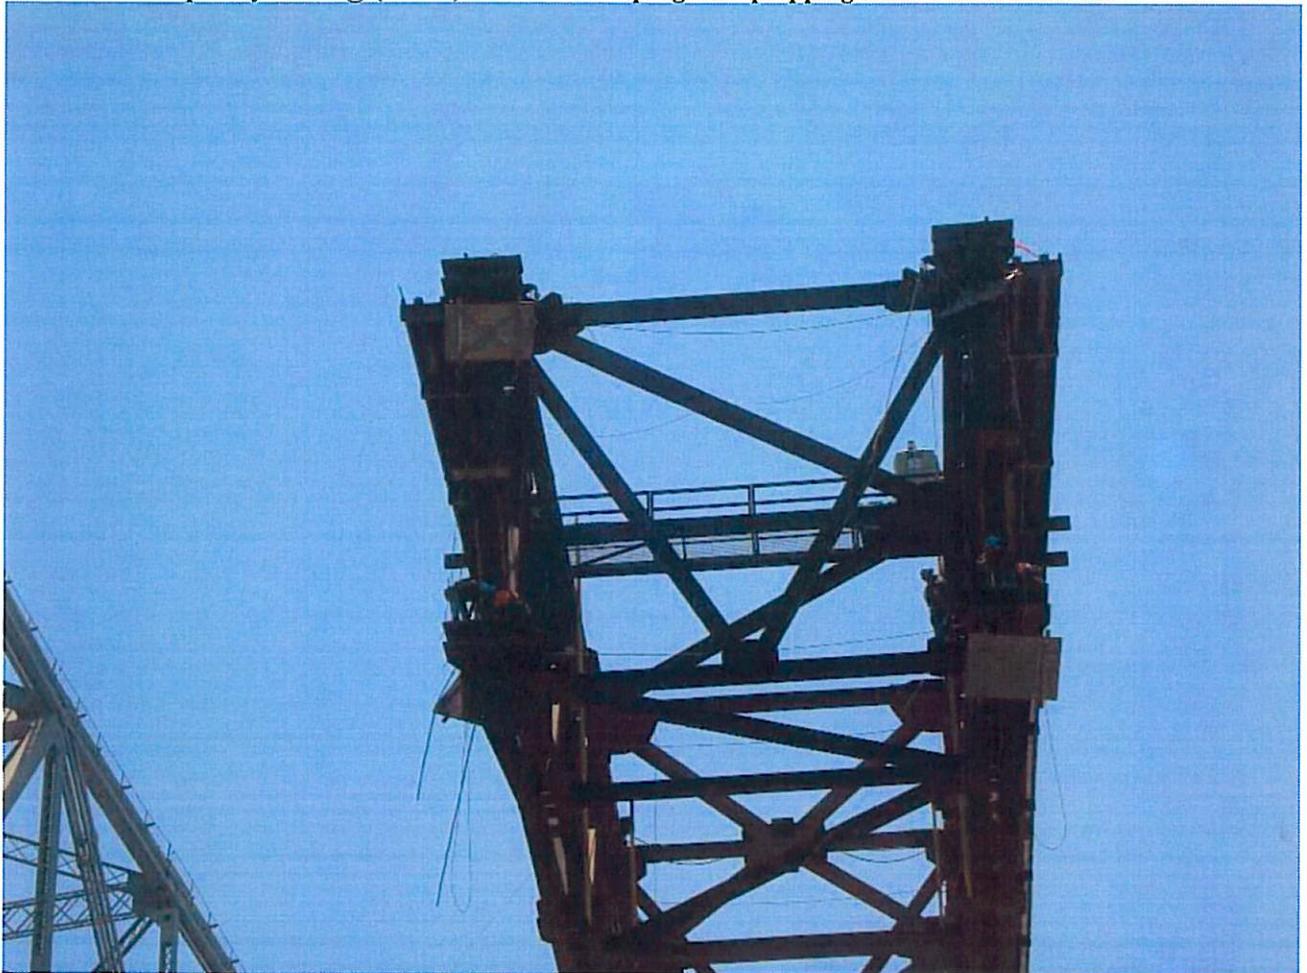

E Line @ Temporary Towers "D"



E Line from W2 to D+, W Line from W2 to B+



- **Shear Leg Crane (at Pier 6) prepping to make Temporary Truss pick @ "E" Line**



- **Temporary Trusses @ Pier 7**



Temporary Trusses E Line (D+ to F) at Pier 7 being prepped for erection



• Traylor-Dutra de-mobing @ Pier 7



Thursday May 28, 2009: Observation from Yerba Buena Island between 1300 and 1430 - Partly sunny (had been overcast in A M) Cool, High Wind

- **E2 - No observed activity**



- **North portion of T1 Foundation & DW Temporary Foundation - no observed activity**



- **Temporary Truss - extending from W2 (A) to (D+)**



Shearleg crane awaiting arrival of Temporary Truss E Line (D+ to F)



Temporary Truss "E" Line Truss (D+ to F+) being transported from Pier 7 to site



Temporary Truss E (D+ to F) being positioned (North of W Line) to be lifted by Shearleg Crane tomorrow (Friday)



- **W2 - West Elevation - Removal of form shoring continues**




W2 - East Elevation - Northern portion from W Line Temporary Truss



W2 - East Elevation - Southern portion from W Line Temporary Truss



W2 - Installation of Strand Jacks continue (South Elevation view)

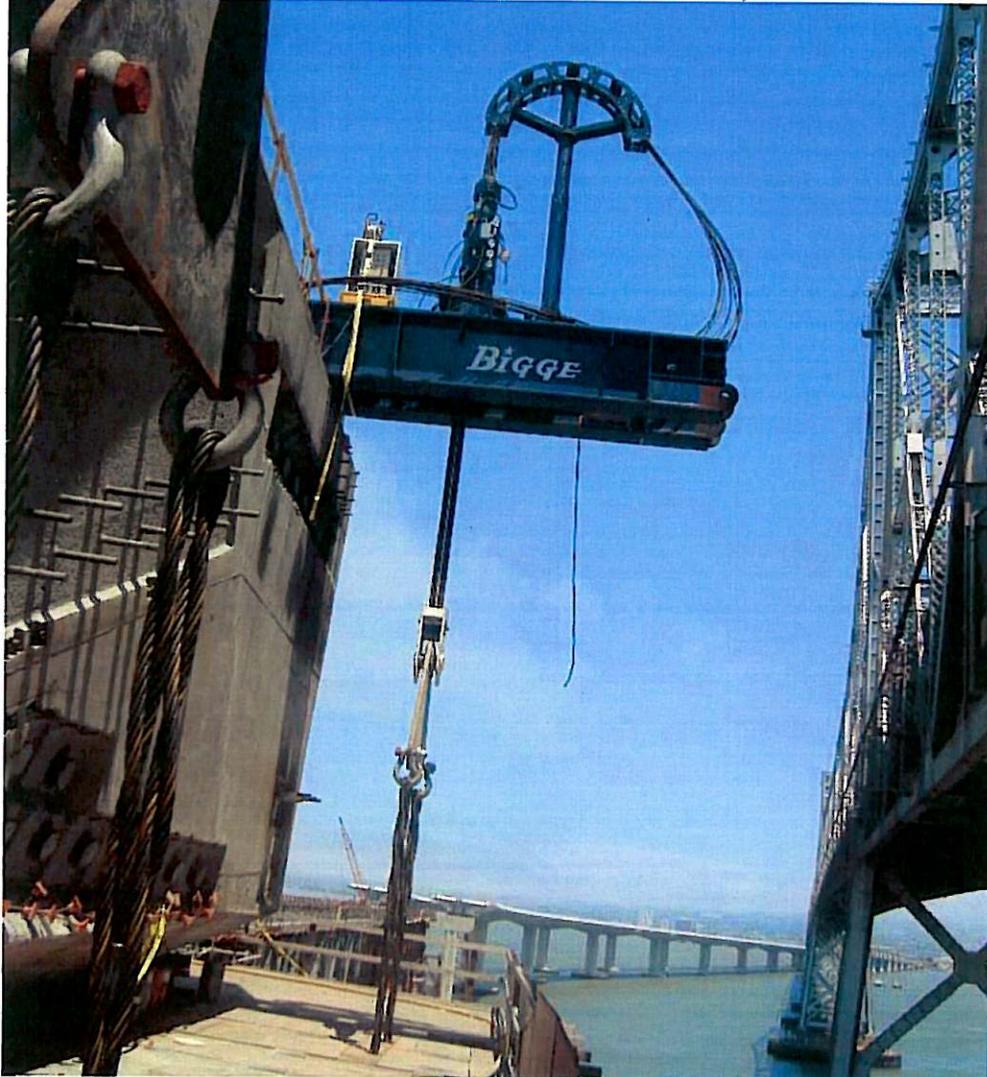

W2 - Strand Jack installation operation continues at top deck (North End)



Friday May 29, 2009: AM Observation from Yerba Buena Island between 0800 and 1030
- Overcast, Cool, Light

- Shearleg Crane making pick of Temporary Truss E Line (D+ to F+)



Shearleg Crane in motion toward "W" Line



Approaching "W" line - note worker on top of "FW" tower



Approaching "E" Line



Essentially aligned with "E" Line - move took approximately 2 hours



Friday May 29, 2009 : PM Observation from Engineer's Boat between 1300 and 1400 - Partly Sunny, Cool and Windy

- **Bolting Temporary Truss Line "E" (D+ to F+)**



View from GE Foundation area



Work continues on Temporary Trusses at Pier 7



Barge in foreground that carried Temp Truss "E" to site - Truss in background is "W" Line (B+ to D)

