




**STATE OF CALIFORNIA  
DEPARTMENT OF TRANSPORTATION  
Contract 1020F - SFOBB - SAS - Superstructure  
Larry Gustafson - Senior Scheduler  
Week Ending 12-Jun-2009**

**Monday June 8, 2009: Observation from Engineer's Boat between 1300 and 1400 - Mostly Sunny, Cool, Light Breeze**

- **E2 - East bound Skyway - removing platform**

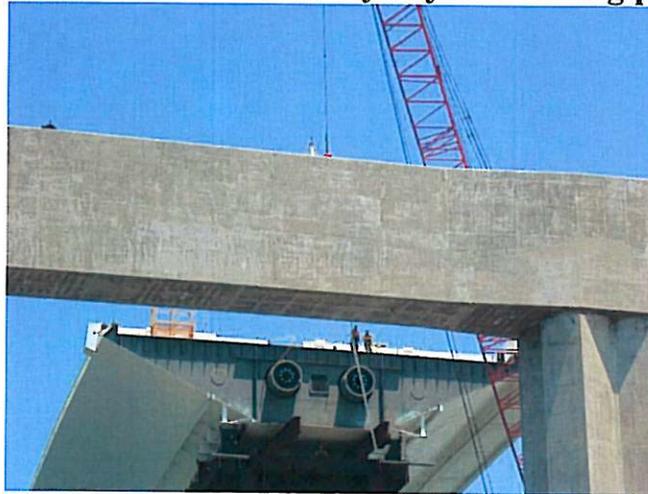

- **"GEE" Temporary Tower - Picking first lift from barge**



**"GEE" - Lifting first pick**



**"GEE" - Swinging first pick**



**"GEE" - Setting First Lift**



**"GEE" - Attaching First Lift**




**"E" Line Temp Truss (set Friday May 29, 2009)-Extending beyond TT "F"  
(Field Splice E11)**



**"E" Line Temporary Truss - Bolting Continues**



- **"W" Line Temporary Truss (B.5 to D set Thursday 4-Jun-09) - shown to right of TT "E" Line (in foreground)**

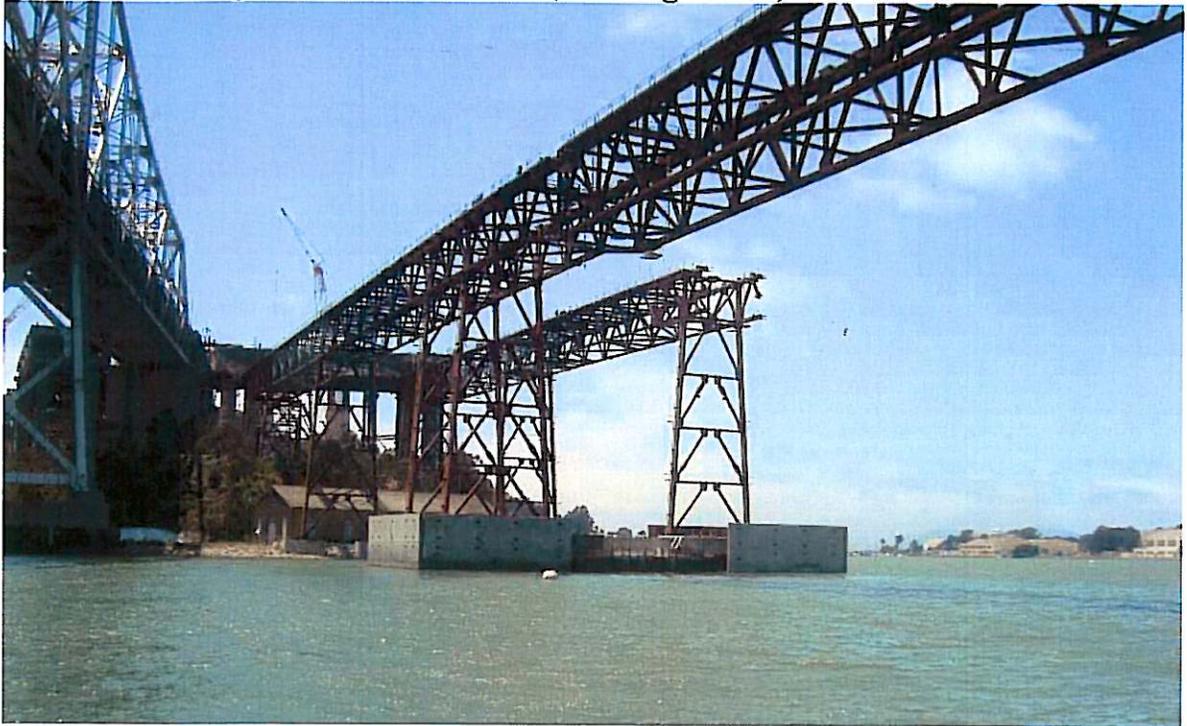

**"W" Line Temporary Truss - Bolting (between C & D)**



- **W2 - East Elevation from Water Level**



- **Shearleg Crane at anchor (North of "W" Line Temporary Truss)**



- **Temporary Tower lifts on barge at Pier 7**



- **Temporary Trusses "W" Line on barge at Pier 7 (to be placed on TT "F")**



**Tuesday June 9, 2009: Observation from Yerba Buena Island between 1000 and 1100 - Overcast, Cold and Windy.**

- **"E" Line Temporary Truss - Bolting between "D" & "F"**



**More 'E' Line - View to the East from approximately "C" - "W" Line to left**



- **"W" Line from Ground Level**



**"W" Line - East end at TT "D"**



- Shearleg Crane anchored North of "W" Line



Head on view of Shearleg Crane



- **T1 Tower Foundation - no observed activity**



- **W2 - West Elevation - Soffit form shores continue to be removed**



**W2 - flying removed shoring**




**W2 East Elevation**



**W2 - Strand Jacks at North end**



**W2 - rebar operation at South end**

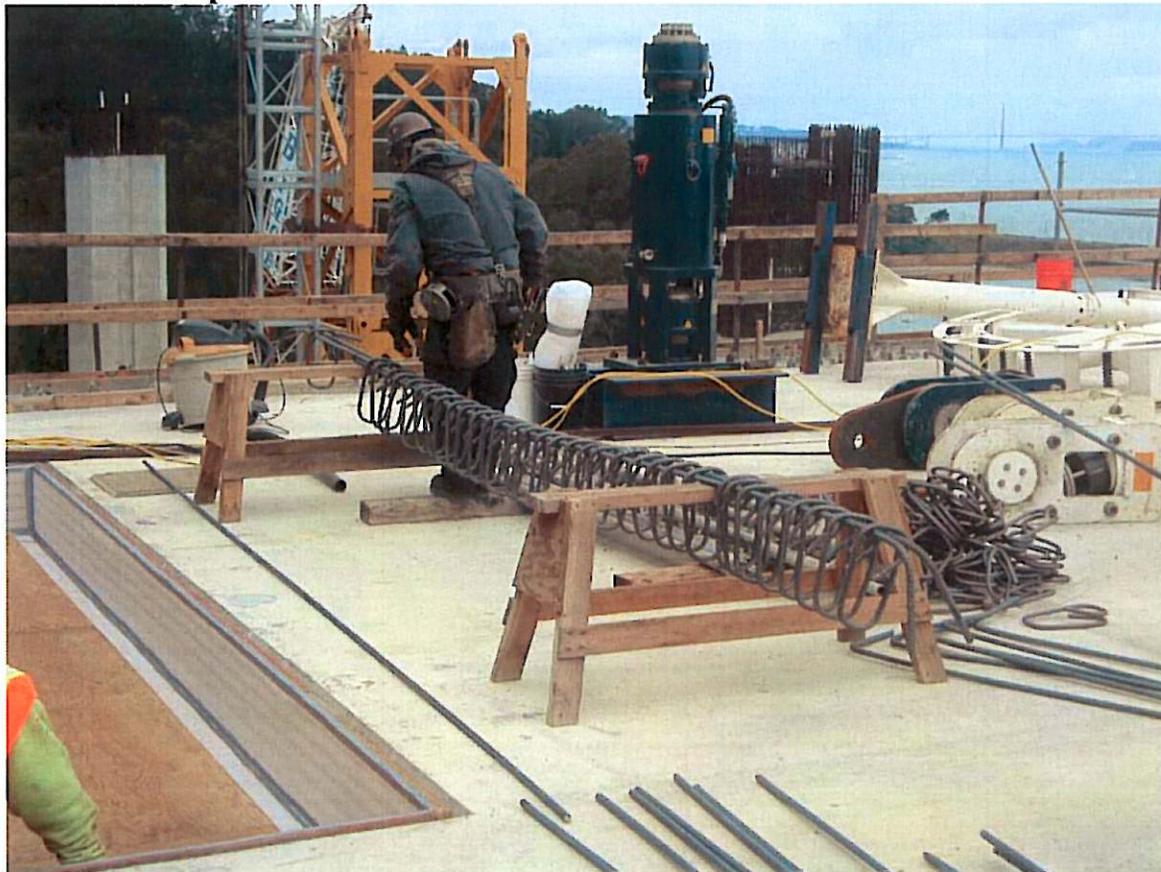

**Friday June 12, 2009: Observation from Engineer's Boat between 1000 and 1100 - Mostly Overcast, Cool, Calm**

- **Temporary Tower "GEE" - Erected this week**



**Temporary Tower "GEE" - View from West**



**T T "GEE" with E2 in background**



**• T1 Foundation**



- **"E" Line Truss - extending beyond TT "F" (Field Splice E11)**



- **"W" Line Truss - extending to TT "D" (T1 Foundation-Field Splice W9)**



- **W2 - East Elevation - from water level**



- **Shearleg Crane at Anchor North of "W" Line**



- Prepping "W" Line TT @ Pier 7 (to be placed on TT "F")



Close up of "W" Line Temp Truss (@ TT "F") -

