



Caltrans

**STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 1020F - SFOBB - SAS - Superstructure
Larry Gustafson - Senior Scheduler
Week Ending 19-Jun-2009**

**Monday June 15, 2009: Observation from Yerba Buena Island between 0930 and 1000 -
Overcast, cool, Light Breeze**

- **Temporary Truss "E" Line (Field Splice E13)**



Temp Trusses "E"(to right) & "W" (to left - view from YBI)



REC'D '09 JUN-19 #009949

- **Temporary Truss "W" Line - Current end @ TT-DW (Field splice W9)**



- **Shearleg Crane remains at anchor North of "W" Truss Line**



- **T1 (TT-D) Anchorage (no observed activity)**



- **View to East from W2 - Temp Tower "G" being erected beyond "E" Line (on right side)**



- **W2 - Leberherr Crane has been moved to East side (West side congested with Detour Work)**



W2 - Soffit Deck Shores continue to be removed



W2 - South portion East Elevation - no activity observed



W2- North portion of East Elevation - no activity observed



W2- Concrete repair at South Elevation




W2 - Strand Jack at North end



W2- Prepping lowering beams



W2 - Top Deck rebar at in fill

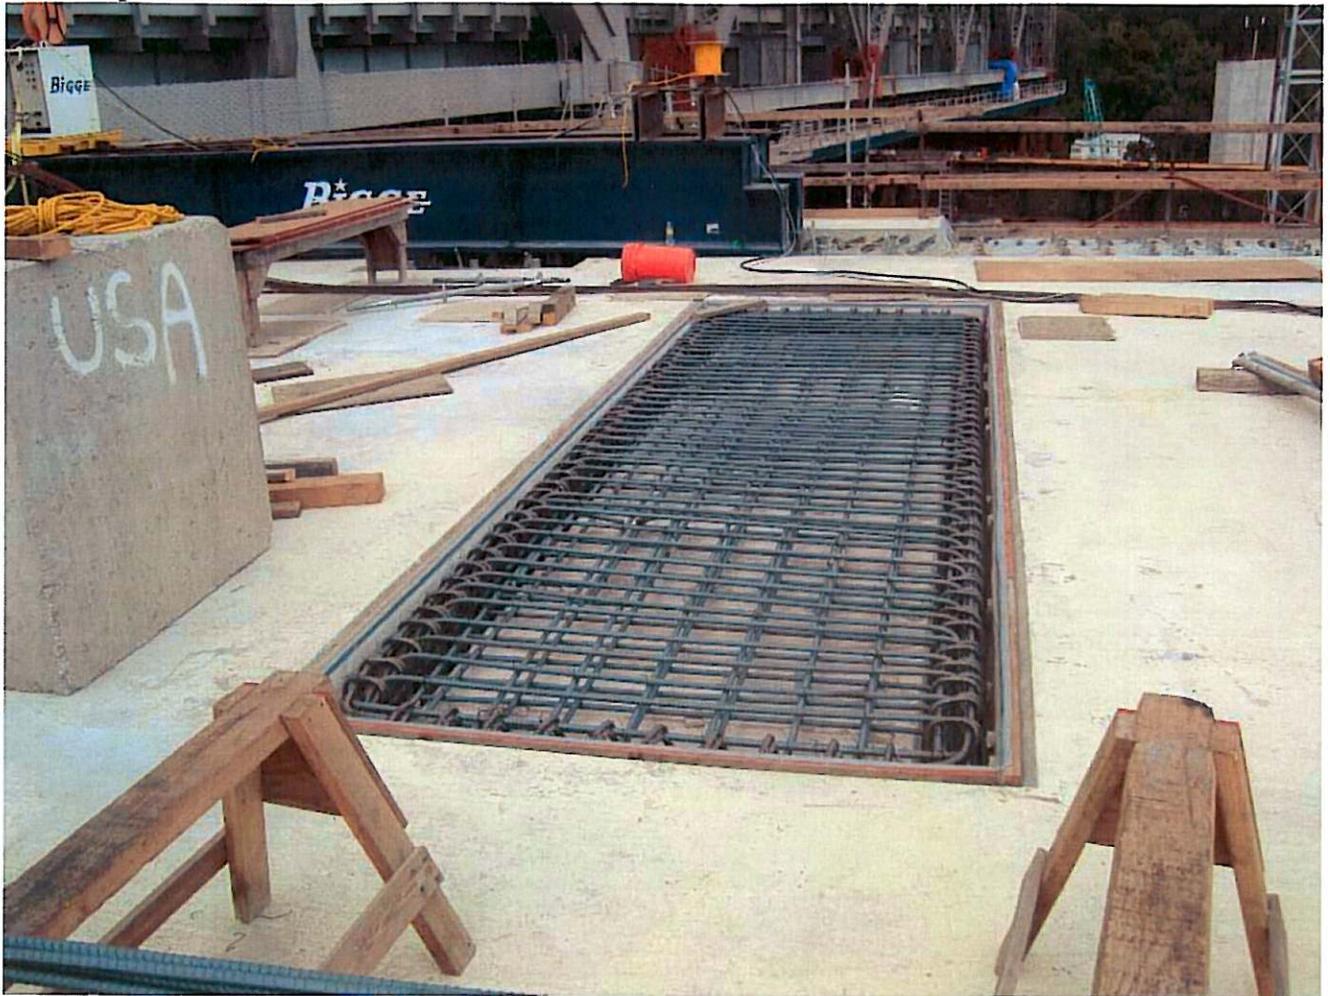

**Tuesday June 16, 2009 : Observation from Engineer's Boat between 1300 and 1400 -
Overcast, Cool, Breeze**

- **Setting "W" Temp Truss Field Splice W12-W13 @ TT "F"**



Temp Truss "E" to left - section of Temp Truss "W" @ TT "F" to right



Temp Truss "W" splice (W12-W13 @ TT F) erection



- Temp Truss "E" bolting continues @ Splice (E11 to E15)



Another view of Temp Truss "E" bolting @ Splice (E11 to E15)



- Erecting Temp Tower GEW



View of Temp Towers "G" illustrating location between Temp Truss "E" and "D2"

