

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 887
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1097
Form HC-10A (Rev. 6/80)	04-0120F4	Date	05/18/2009

Inspectors Hours	Start	0630	Stop	1700
Shift Hours	Start	0630	Stop	1700

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

THANH V LE

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT								IDLE OR DOWN	Name	Contractor
		Foreman	0	0									Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	2									Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	0	0									Price Adam	Traylor Dutra
		Operator	0	0									Joseph Boracci	Traylor Dutra
		Pile driver Journeyman	8	2									Ventura Ochoa	Traylor Dutra
		Pile driver Journeyman	0	0									Robert Utley	Traylor Dutra
		Pile driver Journeyman	0	0									Travis Logsdon	Traylor Dutra
		Operator	8	2									Kurt Dillard	Traylor Dutra
		Pile driver Apprentice	0	0									Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	0	0									Todd Labar	Traylor Dutra
		Pile driver Journeyman	0	0									Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	8	2									Lee Tacker	Traylor Dutra
		Pile driver Journeyman	8	2									Danny Vega	Traylor Dutra
		Pile driver Journeyman	8	2									Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	8	2									Jake Lavash	Traylor Dutra
		Operator	0	0									Gary Lewis	Traylor Dutra
		Operator	8	2									Bud Germany	Traylor Dutra
		CWI	8	2									Steve Gordon	Traylor Dutra
		CWI	8	2									Andrew Erthum	CWI
		CWI	8	2									Michael Johnson	Smith Emery
DB-5		Derrick Barge crane	0											
Big Digger		Marine barge	8											
		Delmag 100	0											
		APE 600 - Vibrator										IDLE		
217		Marine barge	8											
L437	1	Multiquip Generator	8											
L472	1	Power Generation Cummine	8											
L478	1	Multiquip Generator										IDLE		

L270	1	Sullivan-Palatek Air Compressor	8										
	2	Red-D-Arc DC600 Welding Machines	8										
P242	1	Manlift	0									IDLE	
L624	1	Light Station										IDLE	
L625	1	Light Station										IDLE	
L626	1	Light Station										IDLE	
L629	1	Light Station										IDLE	

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

**Description of Operation:**


**1. Temporary Tower G North: Shear connection plates welding.**

**Activities:**

1. Office work:
  - Review plans, special provisions, RFI and ABF submittals for TTG.
2. Field work:
  - A. DB5 crew demobilized to Alameda yard from construction site TTG North.
  - B. Big Digger crew mobilized to construction site at TTG North, and worked on connection plates welding:
    - Pile G104: 1 plate (before) + 4 plates (today) = total 5 plates
    - Pile G117: 1 plate (before) + 4 plates (today) = total 5 plates
    - Pile G119: 1 plate (before) + 5 plates (today) = total 6 plates
    - Pile G110: 3 plates (before) + 4 plates (today) = total 7 plates
    - Pile G111: 2 plates (before) + 5 plates (today) = total 7 plates
    - Pile G112: 1 plate (before) + 4 plates (today) = total 5 plates
  - C. Andrew Erthum from CWI and Michael Johnson from Smith Emery were present for QA/QC welding inspection.
3. Conversation and discussion:
 

There were no significant conversations today.
4. Overtime reason:
 

Worked two hours overtime for construction observation, because contractor worked overtime.

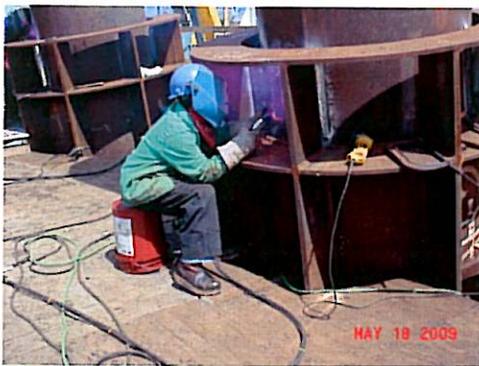

Shear connection plate welding

Thanh V Le

Trans Engineer (D)/Asst. Struct. Rep
