

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 891
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1101
Form HC-10A (Rev. 6/80)	04-0120F4	Date	05/22/2009

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

THANH V LE

EQUIPMENT AND/OR LABOR:			HOURS - ITEM NO.										REMARKS				
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT											IDLE OR DOWN	Name	Contractor
		Foreman	0	0												Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	0												Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	0	0												Price Adam	Traylor Dutra
		Operator	0	0												Joseph Boracci	Traylor Dutra
		Pile driver Journeyman	8	0												Ventura Ochoa	Traylor Dutra
		Pile driver Journeyman	0	0												Robert Utley	Traylor Dutra
		Pile driver Journeyman	0	0												Travis Logsdon	Traylor Dutra
		Operator	8	0												Kurt Dillard	Traylor Dutra
		Pile driver Apprentice	0	0												Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	0	0												Todd Labar	Traylor Dutra
		Pile driver Journeyman	0	0												Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	8	0												Lee Tacker	Traylor Dutra
		Pile driver Journeyman	8	0												Danny Vega	Traylor Dutra
		Pile driver Journeyman	8	0												Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	8	0												Jake Lavash	Traylor Dutra
		Pile driver Journeyman	8	0												Gary Lewis	Traylor Dutra
		Pile driver Journeyman	8	0												Randall Lesley	Traylor Dutra
		Operator	8	0												Steve Gordon	Traylor Dutra
DB-5		Derrick Barge crane	0														
Big Digger		Marine barge	8														
		Delmag 100	0														
		APE 600 - Vibrator													IDLE		
217		Marine barge	8														
L437	1	Multiquip Generator	8														
L472	1	Power Generation Cummine	8														
L478	1	Multiquip Generator													IDLE		

L270	1	Sullivan-Palatek Air Compressor	8										
	2	Red-D-Arc DC600 Welding Machines	8										
P242	1	Manlift	0									IDLE	
L624	1	Light Station										IDLE	
L625	1	Light Station										IDLE	
L626	1	Light Station										IDLE	
L629	1	Light Station										IDLE	

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

Description of Operation:

1. Temporary Tower G North: Annulus grouting.


Activities:

1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTG.
2. Field work:
 - A. Big Digger crew was present at TTG North and worked on annulus plugs grouting:
 - The grouting operation was started at 0800 and it took 15 min. for each pile in the sequence as follows: G120, G118, G104, G103, G102, G101, G117, G119, G121, G109, G110, G111, G112, and G122. The grouting operation completed around noon time.
 - B. Diving crew from West Diving was present to monitor the leak of the annulus during grouting operation with video camera. The diving crew members were Tony Boyle (Foreman), Ryan Willis (Diver) and Mathew Ponder (Diver)
 - C. Marino Salvador from Smith Emery was present to take one set of grout cube for quality testing.
 - D. ABF survey crew (Robert Andres, James Allen, Terry Dennis and Chris Robert) was present to perform as built survey for tower socket of TTG South.
3. Conversation and discussion:

There were no significant conversations today.
4. Overtime reason:



Annulus grouting operation

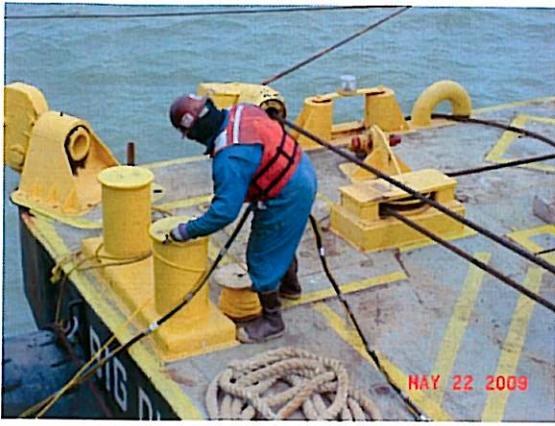

Diver monitor grouting operation

Thanh V Le

A handwritten signature in black ink, appearing to read "Thanh V Le".

Trans Engineer (D)/Asst. Struct. Rep
