

MS

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 882
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1092
Form HC-10A (Rev. 6/80)	04-0120F4	Date	05/13/2009

Inspectors Hours	Start	0630	Stop	1730
Shift Hours	Start	0630	Stop	1730

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

THANH V LE

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS		
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT								IDLE OR DOWN	Name	Contractor
		Foreman	8	2.5									Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	2.5									Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	8	0									Price Adam	Traylor Dutra
		Operator	8	2.5									Joseph Boracci	Traylor Dutra
		Pile driver Journeyman	8	2.5									Ventura Ochoa	Traylor Dutra
		Pile driver Journeyman	8	0									Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	0									Travis Logsdon	Traylor Dutra
		Operator	8	2.5									Kurt Dillard	Traylor Dutra
		Pile driver Apprentice	8	0									Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	8	2.5									Todd Labar	Traylor Dutra
		Pile driver Journeyman	8	2.5									Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	8	2.5									Lee Tacker	Traylor Dutra
		Pile driver Journeyman	8	2.5									Danny Vega	Traylor Dutra
		Pile driver Journeyman	8	2.5									Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	8	2.5									Jake Lavash	Traylor Dutra
		Pile driver Journeyman	8	2.5									Gary Lewis	Traylor Dutra
		Operator	8	0									Bud Germany	Traylor Dutra
		Operator	8	0									Steve Gordon	Traylor Dutra
		CWI	8	2.5									Andrew Erthum	CWI
		CWI	8	2.5									Michael Johnson	Smith Emery
DB-5		Derrick Barge crane	8											
Big Digger		Marine barge	8											
		Delmag 100										IDLE		
		APE 600 - Vibrator										IDLE		
217		Marine barge	8											
L437	1	Multiquip Generator	8											
L472	1	Power Generation Cummine	8											
L478	1	Multiquip Generator										IDLE		

L270	1	Sullivan-Palatek Air Compressor	8												
	2	Red-D-Arc DC600 Welding Machines	8												
P242	1	Manlift	0										IDLE		
L624	1	Light Station											IDLE		
L625	1	Light Station											IDLE		
L626	1	Light Station											IDLE		
L629	1	Light Station											IDLE		

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

Description of Operation:

1. Temporary Tower G North: Splicing 42" dia. piles.


Activities:

1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTG.
2. Field work:
 - DB5 crew was at TTG North to continue pile splicing and connection plate welding operation:
 - * The crew spliced three new piles:G117-100% completion and UT,G121- 100% completion and UT, G122 – 50% completion not yet UT.
 - * Continued and finished 100% and UT on pile G118.
 - * Welding connection plates an piles: 5 plates @G101, 5 plates @ G102, 2 plates @ 103, and 4 plates @ G109.
 - Andrew Erthum from CWI and Michael Johnson from Smith Emery were present for QA/QC welding inspection.
3. Conversation and discussion:
4. Overtime reason:

Worked two and half hours overtime for construction observation because contractor worked overtime reason.



Splicing piles in angle position

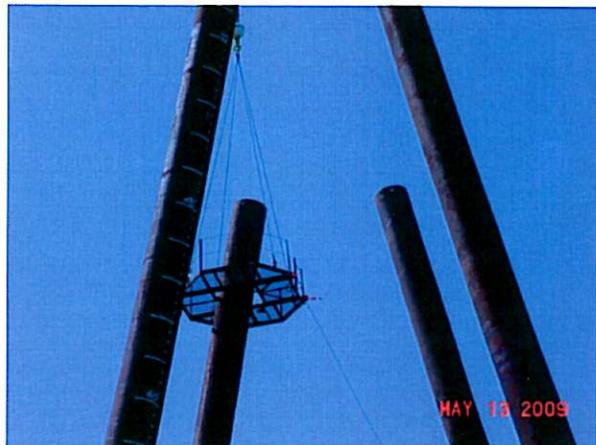


Removed working platform



Continued splicing piles



QA and QC perform UT test

Thanh V Le  Trans Engineer (D)/Asst. Struct. Rep
