

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 884
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1094
Form HC-10A (Rev. 6/80)	04-0120F4	Date	05/15/2009

Inspectors Hours	Start	0630	Stop	1500
Shift Hours	Start	0630	Stop	1500

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

THANH V LE

EQUIPMENT AND/OR LABOR:		HOURS - ITEM NO.										REMARKS	
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT							IDLE OR DOWN	Name Contractor	
												Name	Contractor
		Foreman	8	0								Terry Murray	Traylor Dutra
		Pile driver Journeyman	8	0								Gilbert Moya	Traylor Dutra
		Pile driver Journeyman	8	0								Price Adam	Traylor Dutra
		Operator	8	0								Joseph Boracci	Traylor Dutra
		Pile driver Journeyman	8	0								Ventura Ochoa	Traylor Dutra
		Pile driver Journeyman	8	0								Robert Utley	Traylor Dutra
		Pile driver Journeyman	8	0								Travis Logsdon	Traylor Dutra
		Operator	8	0								Kurt Dillard	Traylor Dutra
		Pile driver Apprentice	8	0								Richard Hiebert J.	Traylor Dutra
		Pile driver Journeyman	8	0								Todd Labar	Traylor Dutra
		Pile driver Journeyman	8	0								Richard Hiebert	Traylor Dutra
		Pile driver Journeyman	8	0								Lee Tacker	Traylor Dutra
		Pile driver Journeyman	8	0								Danny Vega	Traylor Dutra
		Pile driver Journeyman	8	0								Stephen Mc Grew	Traylor Dutra
		Pile driver Journeyman	8	0								Jake Lavash	Traylor Dutra
		Pile driver Journeyman	8	0								Gary Lewis	Traylor Dutra
		Operator	8	0								Bud Germany	Traylor Dutra
		Operator	8	0								Steve Gordon	Traylor Dutra
		CWI	8	0								Andrew Erthum	CWI
		CWI	8	0								Michael Johnson	Smith Emery
DB-5		Derrick Barge crane	8										
Big Digger		Marine barge	8										
		Delmag 100	8										
		APE 600 - Vibrator									IDLE		
217		Marine barge	8										
L437	1	Multiquip Generator	8										
L472	1	Power Generation Cummine	8										
L478	1	Multiquip Generator									IDLE		

L270	1	Sullivan-Palatek Air Compressor	8										
	2	Red-D-Arc DC600 Welding Machines	8										
P242	1	Manlift	0									IDLE	
L624	1	Light Station										IDLE	
L625	1	Light Station										IDLE	
L626	1	Light Station										IDLE	
L629	1	Light Station										IDLE	

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

Description of Operation:

1. Temporary Tower G North: Driving 42" dia. piles.

Activities:

1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TTG.
2. Field work:
 - DB5 crew was present at TTG North for piles driving and connection plates welding operation:
 - The crew drove six @42" piles to elevation at 68.00 at top of the annulus ring (reference elev. + 6.99)
 - Continued welding connection plates on piles: G101 – 100% completion, G102 – 100% completion, G103 – 100% completion, G109 – 100% completion, G111 – 3 plates, G112 – 1 plate, G104 – 1 plate, G117 – 1 plate, G119 – 1 plate.
 - Manuel Reyes from Klohn Crippen Berger was present to observed pile driving operation and take the blowcounts.
 - Phil Thorson and Sean Hanser from SRS consultant were present for mammal monitoring.
 - Jered Mc Daniel was present for Acoustical Testing.
 - Andrew Erthum from CWI and Michael Johnson from Smith Emery were present for QA/QC welding inspection. Michael Johnson performed (50%) UT test for pile G120 and together with Andrew Erthum continued inspecting shear plates welding.
3. Conversation and discussion:


There were no significant conversations today.
4. Overtime reason:




End Of Drive blowcount



Beginning Of Drive blowcount

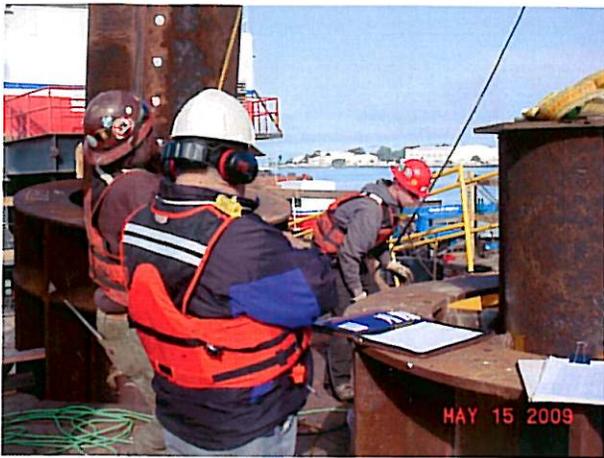

Reyes Manuel from KCB records blowcounts

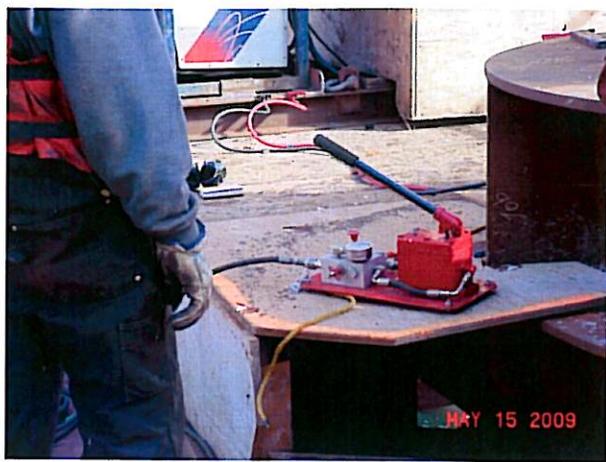


Gas pump control for hammer



Lubricant hammer after driving each pile



Last driven pile of TT project G120

Thanh V Le  Trans Engineer (D)/Asst. Struct. Rep
