

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 89915
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1125
Form HC-10A (Rev. 6/80)	04-0120F4	Date	06/15/2009

Inspectors Hours	Start	0700	Stop	1530
Shift Hours	Start	0700	Stop	1530

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

THANH V LE

EQUIPMENT AND/OR LABOR:			HOURS - ITEM NO.								REMARKS		
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)	Regular	OT							IDLE OR DOWN	Name	Contractor
		Iron worker Foreman	8	0								E.J Meyer III	ABF/JV
		Iron worker Jrny	8	0								Chris Biskner	ABF/JV
		Iron worker Jrny	8	0								Stanley Dalie	ABF/JV
		Iron worker Jrny	8	0								Kevin Ratcliffe	ABF/JV
		Iron worker Jrny	8	0								Mathew Cochran	ABF/JV
		Iron worker Jrny	8	0								Jerry Kubala	ABF/JV
		OE	8	0								Mike Klein	ABF/JV
		OE	8	0								Daniel Martinez	ABF/JV
240ft boom	1	Ringer barge I											
260ft boom	1	Ringer barge II											
	2	Welding machine											
58084	1	RT 160 crane											
6 18 4293,4217	2	IR Compressor											
549 07 5006	1	Generator											
412 10 7101 417 40 5029	1	Forklift											
Wetar I,II,XII	3	Barge											
KRS 180 B 318	2	Barge											
TEC 35,36,27	3	Barge											
YC 1333	1	Barge											
OC 260, 261, 262,265	4	Barge											
481 93 5006 481 40 7013	2	Man lift											

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

Description of Operation:

1. Temporary Tower G South: Tower erection.


Activities:

1. Office work:
 - Review plans, special provisions, RFI and ABF submittals for TT trusses.
2. Field work:
 - ABF's crew continued bolting tower assemblies TTG South – East leg, and erection lower assembly TTG South - West leg.
3. Conversation and discussion:

There were no significant conversations today.
4. Overtime reason:



Actual gap is 17mm > 12mm (according to plan)

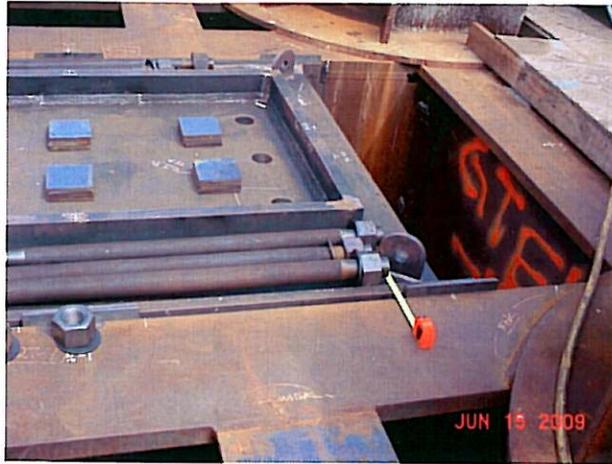

Tower pocket positions before setting tower legs



Continued bolting



Lower assembly setting for West leg – TTG South

Thanh V Le

Trans Engineer (D)/Asst. Struct. Rep
