

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 89917
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1127
Form HC-10A (Rev. 6/80)	04-0120F4	Date	06/17/2009

Inspectors Hours	Start	0700	Stop	1530
Shift Hours	Start	0700	Stop	1530

ASSISTANT RESIDENT ENGINEER'S

CONTRACTOR - ABFJV

THANH V LE

		HOURS - ITEM NO.										
EQUIPMENT AND/OR LABOR:		Regular	OT							IDLE OR DOWN	REMARKS	
Equip. #	NO. OF MEN										Description (Of Equipment or Labor)	Name
		8	0								E.J Meyer III	ABF/JV
		8	0								Chris Biskner	ABF/JV
		8	0								Stanley Dalie	ABF/JV
		8	0								Kevin Ratcliffe	ABF/JV
		8	0								Mathew Cochran	ABF/JV
		8	0								Jerry Kubala	ABF/JV
		8	0								Mike Klein	ABF/JV
		8	0								Daniel Martinez	ABF/JV
		8	0								Dick Chafer	ABF/JV
1700 tons	1											
240ft boom	1											
280ft boom	1											
	2											
58084	1											
6 18 4293,4217	2											
549 07 5006	1											
412 10 7101 417 40 5029	1											
Wetar I,II,XII	3											
KRS 180 B 318	2											
TEC 35,36,27	3											
YC 1333	1											
OC 260, 261, 262,265	4											
481 93 5006 481 40 7013	2											

Weather: Partly Cloudy Hi 67 °F, Lo 46 °F.

**Description of Operation:**

**1. Temporary Tower G South: Tower erection.**


**Activities:**

1. Office work:
  - Review plans, special provisions, RFI and ABF submittals for TT trusses.
2. Field work:
  - ABF's crew installed upper assembly for TTG South – West leg, and continued bolting/tightening middle assembly to lower assembly.

3. Conversation and discussion:

There were no significant conversations today.


4. Overtime reason:

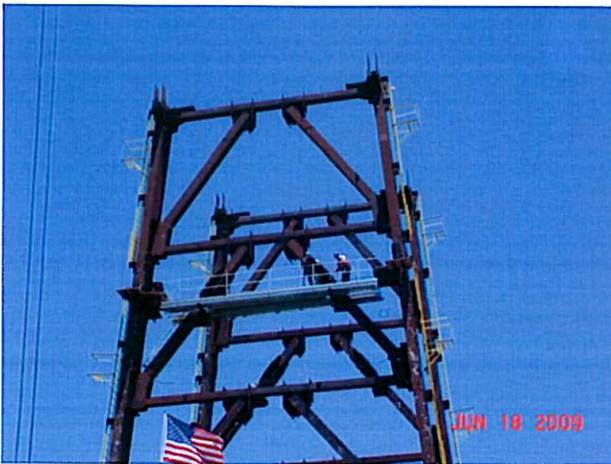


Installed TTG South – West leg



Bolting diagonal beams

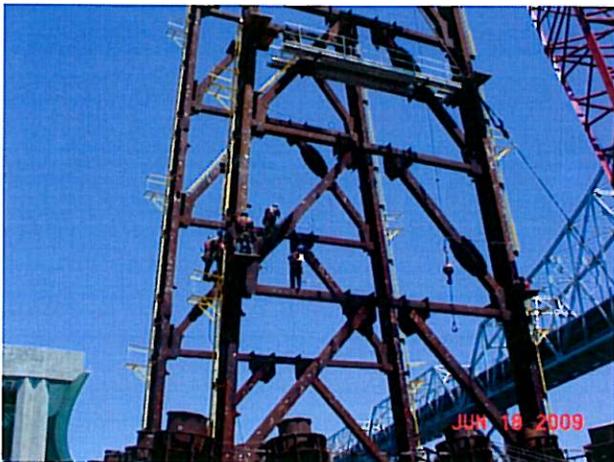

Bolting/tightening middle assembly to lower assembly

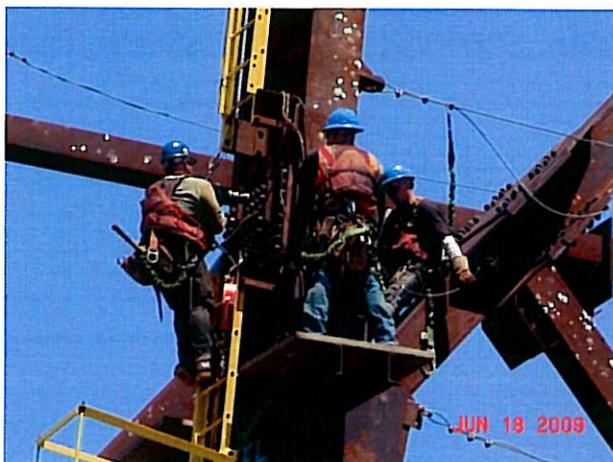

Thanh V Le

Trans Engineer (D)/Asst. Struct. Rep
