

STATE OF CALIFORNIA  
DEPARTMENT OF TRANSPORTATION  
Contract 1020F - SFOBB - SAS - Superstructure  
Larry Gustafson - Senior Scheduler  
Week Ending 28-Aug-2009

Monday 24 August 2009: Observation from Engineer's Boat between 1300 and 1400 -  
Clear, Cool, Light Breeze

- Temporary Trusses status "E" Line remains to F + (FS-E14)



"W" Line Temporary Truss status "W" Line remains to C+



RECT H31 AUG-31 #010518

**Portion of Temp Truss "W" at Temp Towers WFW & WFE remains as before**



**Status of T1 Erection Tower Lifts 1 & 2, South & East Frame remains as before**



- **W2 East Elevation**



- **Shear leg crane moored near Pier 7**



**E2 Temporary Trusses in storage on barges at Pier 7**



**Temp Trusses being assembled @ Pier 7**



**Thursday 27-August-2009: Observation from Yerba Buena Island 0930 and 1100 - Clear, Temperate. Calm**

- **Temporary Truss "W" Line (F to G) being erected)**



**Temp Truss "W" Line showing gap between D & F for later T1 erection**



- Temp Truss 'W' Line on left, 'E' line on right



- W2 - Stressing ducts in foreground



**W2 Cable Tie Down Cover Slab had been removed**



**Mobilizing to commence vertical stressing on Monday 31-August-2009**



**Cleaning Stress Ducts at East Elevation**




**Form removal continues at South Void - enclosed space procedures**



**W2 East Elevation - Northern portion**



**W2 East Elevation - Southern portion**

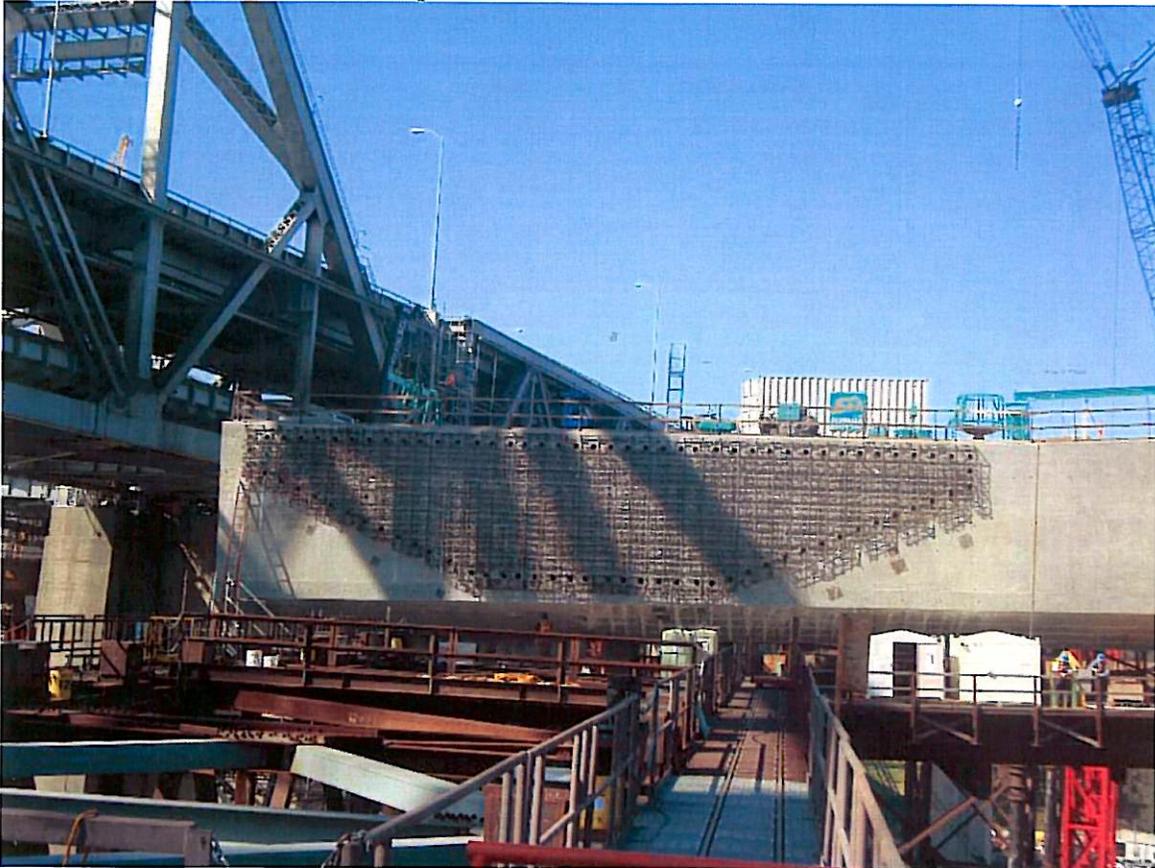

**Concrete surface finish grinding**



**W2 - Soffit & working platform**

