

04-SF-80-13.2/13.9  
04-0120F4  
SFOBB - SAS

Report No 800 (7 Workday Calendar)

Date Feb 20, 2009

M T W T **F** S S Circle Day  
Hours Start on Wk 1:00pm to 3:00pm

Prime Contractor: ABF

*CCO 3651*

**ASSISTANT RESIDENT ENGINEER'S DAILY** T1 (1/4) Anchorage Mock Up on Pier 7 Yard **REPORT**

Location & Description of Operation Contractors placed 2" x 4" brace form work around the South & West faces of T1 (1/4) Anchorage area (see Photo 1-2). Four 16" long extended steel pipes were nailed into the concrete pad (see Photo 3). The missing threaded rod was not installed. I marked up the location on the concrete pad and informed both field & office engineers.

Reference: mock up procedure STEP # 2 & 3.

EQUIPMENT AND/OR LABOR			HOURS-ITEM NO.							WEATHER
EQPT NO	NO OF MEN	DESCRIPTION OF EQUIPMENT OR LABOR	Cont. 2nd lift (3") conc. pad form work.	Placed 4 extended 16" steel pipes						Sunny
										Temp: 65°F
										REMARKS Reason for Idleness or other remarks
		Everadeo Hernandez (Laborer Foreman)								
		Froylan Ruiz (Laborer)	0							
		Daniel Schwartz (Laborer Apprentice)	0							
2074		AC Generator with mobile lights								Generator was used to power circular saw for 2" x 4" wood
		Genie TML 4000N								

Katherine Quillin: ABF Field Engineer  
Andre Markarian: ABF Office Engineer  
ABF-CAL-TRN-001947 (T1 - Anchorage Grout Mock up Procedure)

Hours were verbally verified with field engineer on Feb 20, 2009


REC'D HBI AUG-31 #010920

*Michelle Chui*  
\_\_\_\_\_  
Michelle Chui, PE

ARE  
Title

*km*


Looking East

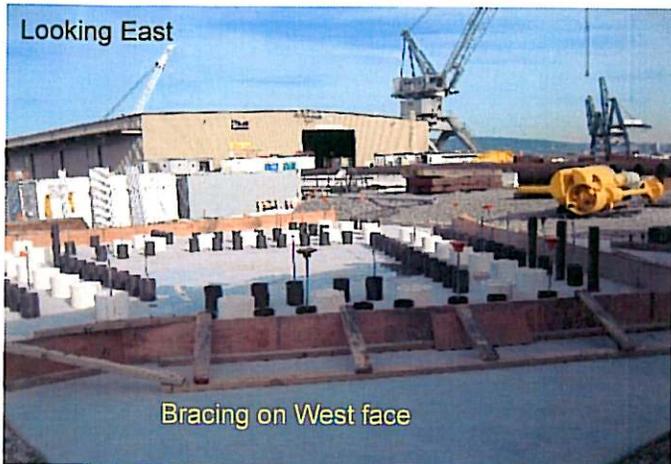

Bracing on West face

Photo 1  
20-Feb-09  
T1 (1/4) Anchorage Mock Up  
on Pier 7 Yard


Looking North

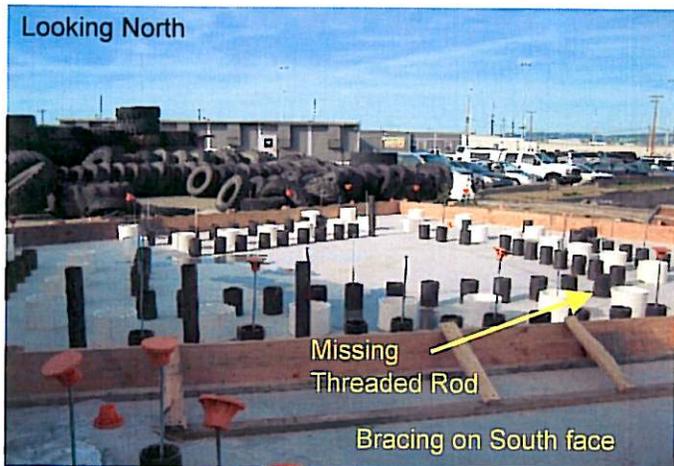

Missing  
Threaded Rod

Bracing on South face

Photo 2  
20-Feb-09  
T1 (1/4) Anchorage Mock Up  
on Pier 7 Yard

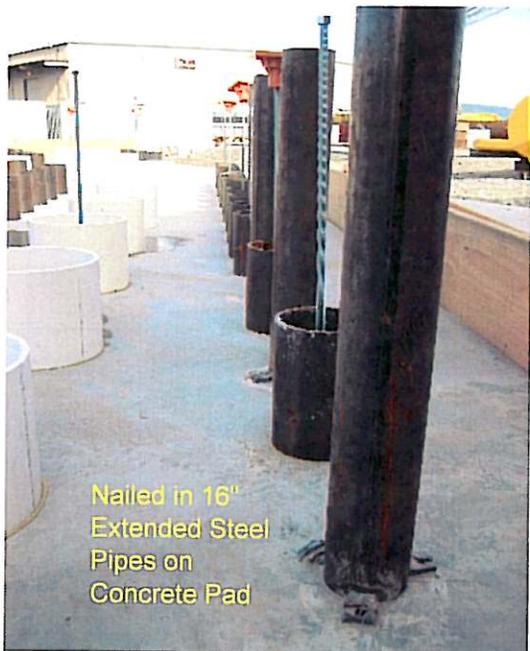

Nailed in 16"  
Extended Steel  
Pipes on  
Concrete Pad

Photo 3  
20-Feb-09  
T1 (1/4) Anchorage Mock Up  
on Pier 7 Yard
