

STATE OF CALIFORNIA	Job Stamp	7-day Const. Calendar	Day No. 1006
DEPARTMENT OF TRANSPORTATION	SFOBB SAS	Project Work Day No.	Day No. 1216
Form HC-10A (Rev. 6/80)	04-0120F4	Date	9/14/2009

Weather: Overcast and cool (AM)
Partly Cloudy and warm (PM)

Inspectors Hours Start 0700 Stop 1600

Shift Hours Start 0700 Stop 1530

ASSISTANT STRUCTURE REP.
JASON WILCOX

CONTRACTOR – American Bridge - Fluor JV

HOURS - ITEM NO. 8												REMARKS		
EQUIPMENT AND/OR LABOR:			REGULAR	OVERTIME	DOUBLE TIME	NIGHT PAY						IDLE OR DOWN	Name Contractor	
Equip. #	NO. MEN	DESCRIPTION (Of Equipment or Labor)											Name	Contractor

Description of Operation:
Erect Temporary Truss and Towers:

FIELD WORK:


The components for segments E13 and E14 have been separated and are being assembled to segment E12 here at pier 7. Masoud Modanlou is observing the operation and will have the detailed diary for the operation including labor and equipment. The segments arrived from China as two halves, connected by pipe sections to facilitate delivery over sea. Last week the pipes were removed, and the northern and southern halves of the segments were picked and placed, then bolted up. These segments are the portion of the Temp Trusswork that go under the E2 crossbeam. Since the portion that goes under the crossbeam dips down, the Contractor decided to set segment E12 on top of W7 to allow for the assembly of the segments without them going into the water. See pictures.

As of now, both the North and South sides of segments 13 and 14 are bolted on, but the fill-in pieces are being placed, holes being drilled, and bolts being installed.

There are some workers assembling the walkways on the top chord as well.

I spoke with Scott Tudor about what was to come of the threaded rods for the Tower H base plate connection at E2. He said that the rods should be on site, but that Bill O'Sullivan is watching this operation and that he or John Callaghan would have more information on this operation. As of today, there was no work going on out there.

REC'D H31 NOV-04 #011366

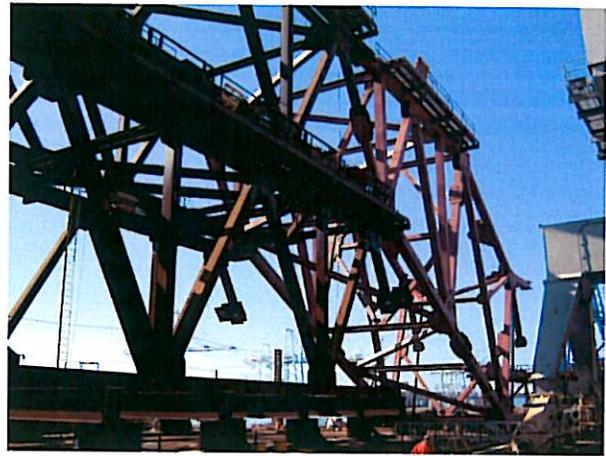

OFFICE WORK:

- Diary work
- Reviewed Submittal 1350 – Temp Works Erection Plan – FS E17 to FS E20

CONVERSATIONS:

OVERTIME: No overtime accrued today.

Inspector: Jason Wilcox

Transportation Engineer (D)/Asst. Structure Rep.
