

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F04 - SFOBB - Superstructure
Martin Chandrawinata, PE – Construction Engineer
Week Ending 26 February 2010

Monday 22 Feb. 2010: Observation from W2 at 8.30am - 9.30am. Sunny ~ 60F

- View of Utility Opening at W2 West Footing. No Activity.



- View of Lift 1 East – Lift 3 East on Temporary Trusses.



REC'D H32 MAR 03 #012113

- **Workers cleaning the splice connection between L1E and L2E.**



- **Overview from Lift 3 East**



- Lift 4 East Cradle being lifted unto the Temporary Trusses.



Tuesday 23 Feb. 2010: Observation from W2 at 6.15am-7.30am. Clear ~ 55F

- Lift 4 East being lifted for placement




- **Lift 4 East being lifted for placement**



- **Overview of Lift 1 East – Lift 3 East**




- Overview of Lift 1 East – Lift 3 East

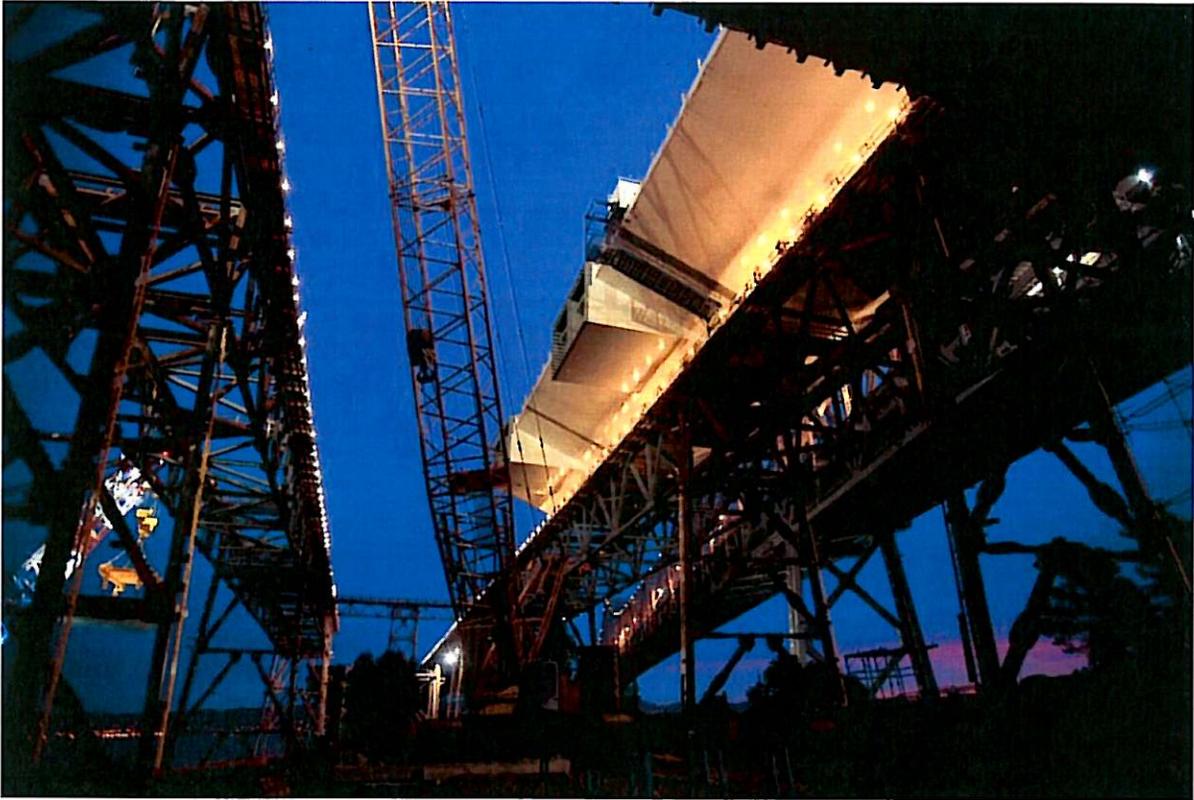

- Lift 4 East being lifted for placement



- Overview of Lift 3 East and the sunrise at around 6.45am

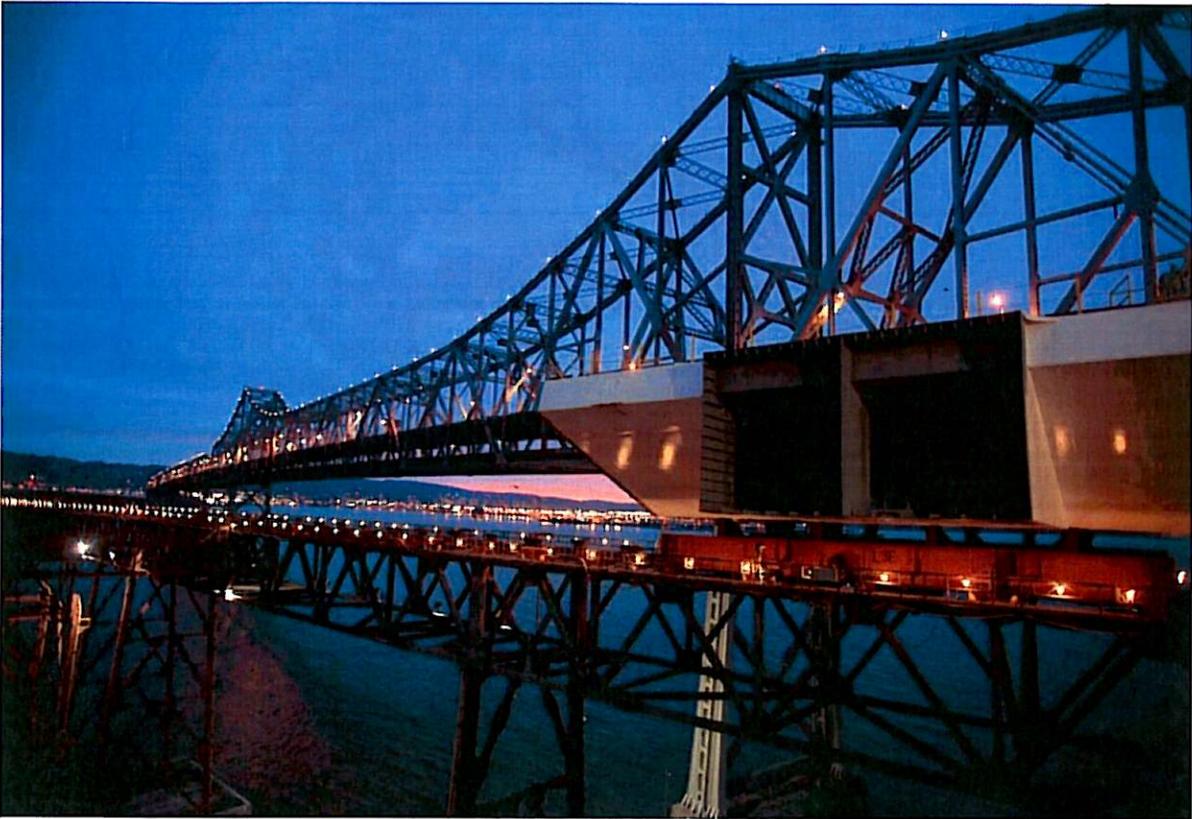


- Workers are placing the epoxy and preparing for the L4E placement.



- **Lift 4 East being lifted for placement**



- **Overview of the Left Coast Lifter Crane**

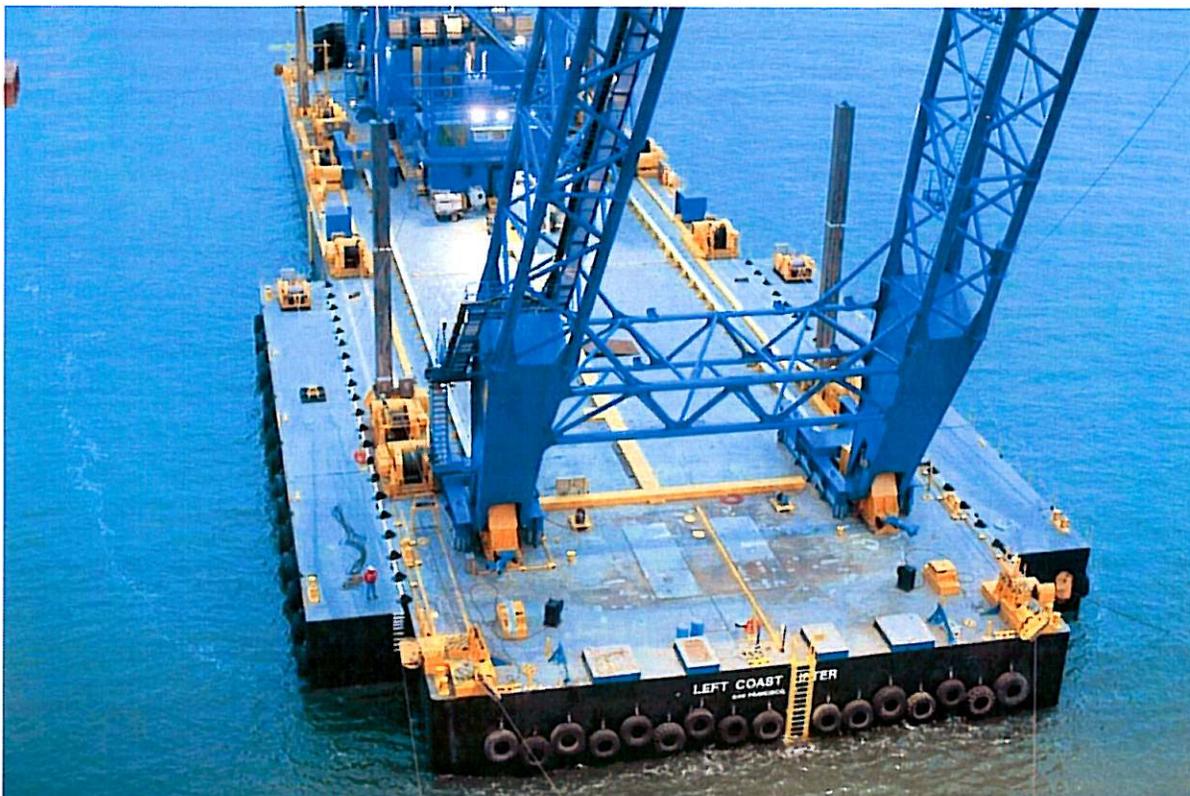

- Lift 4 East being lifted for placement



- Lift 4 East being lifted for placement



- Lift 4 East being lifted for placement



- Overview of Lift 3 East



- Lift 4 East being lifted for placement



- Lift 4 East being lifted for placement



- **Lift 4 East being lifted for placement**



- **Lift 4 East being lifted for placement**



- Covers have been placed on the Cable Tie-Downs on W2 Cap Beam



Wednesday 24 Feb. 2010: Observation from the Boat at 12.00pm - 12.30pm. Sunny ~ 65F

- Lift 4 East is being pushed to join L3E

