

STATE OF CALIFORNIA
DEPARTMENT OF TRANSPORTATION
Contract 0120F04 - SFOBB - Superstructure
Martin Chandrawinata, PE – Construction Engineer
Week Ending 5 March 2010

Wednesday 3 March 2010: Observation from W2 from 8.00am – 11.30am. Sunny ~ 50F

- Placement of Segment L1W. L1W is on barge at 8.00am



- L1W is on barge at 8.00am



REC'D H32 MAR-17 #012183

46.02

- LCL begins lifting L1W at 9.00am



- LCL begins lifting L1W at 9.00am



- LCL begins lifting L1W ~ 9.00am



- LCL lifting L1W ~ 9.00am



- Barge is leaving at around 9.10am



- L1W is being lifted ~ 9.15am



- **L1W is being lifted ~ 9.15am**



- **L1W is being lifted ~ 9.15am**



- L1W is being lifted ~ 9.30am



- L1W is being lifted ~ 9.30am




- Workers and L1W ~ 9.45am




- Overview of Lift 1 West, Cradle, and Pushing frame ~ 9.45am



- View of the bearing pads and L1W in the background ~ 9.45am

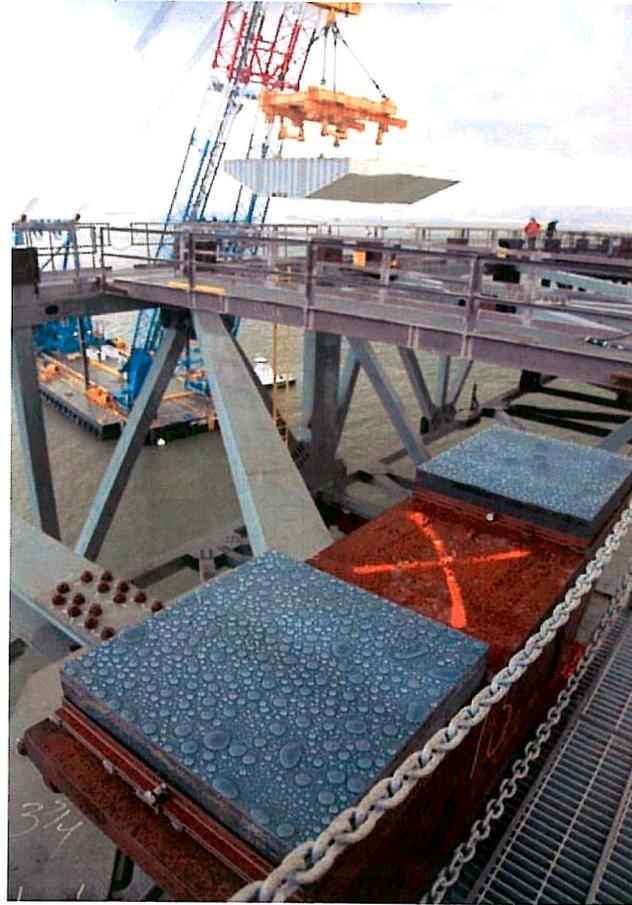

- Lift 1 West, Cradle, and Pushing frame ~ 9.45am

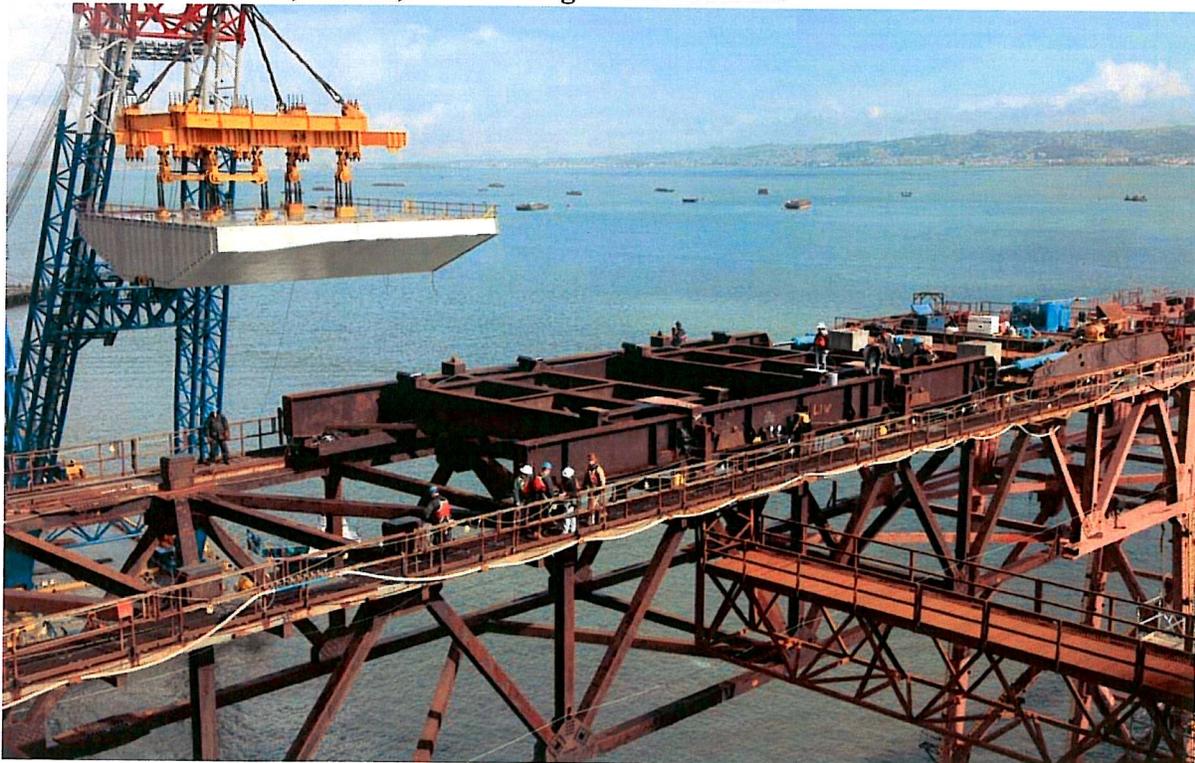

- **Lift 1 West, Cradle, and Pushing frame ~ 9.45am**



- **Overview of the T1 and the Temporary Trusses from L4E ~ 10.00am**



- **Lift 1 West is about to be placed on the cradle ~ 10.30am**



- **Lift 1 West is about to be placed on the cradle ~ 10.30am**



- Lift 1 West is about to be placed on the cradle ~ 10.30am



- Lift 1 West is about to be placed on the cradle ~ 10.50am



- Lift 1 West is about to be placed on the cradle ~ 11.00am



- Lift 1 West is about to be placed on the cradle ~ 11.00am



- **Lift 1 West is about to be placed on the cradle ~ 11.00am**



- **Lift 1 West is about to be placed on the cradle ~ 11.00am**



- Lift 1 West is about to be placed on the cradle ~ 11.00am



- Lift 1 West is about to be placed on the cradle ~ 11.15am



- Lift 1 West is about to be placed on the cradle ~ 11.15am




- Lift 1 West is placed on the cradle ~ 11.20am



- Lift 1 West is placed on the cradle ~ 11.20am



- Lift 1 West is placed on the cradle ~ 11.20am

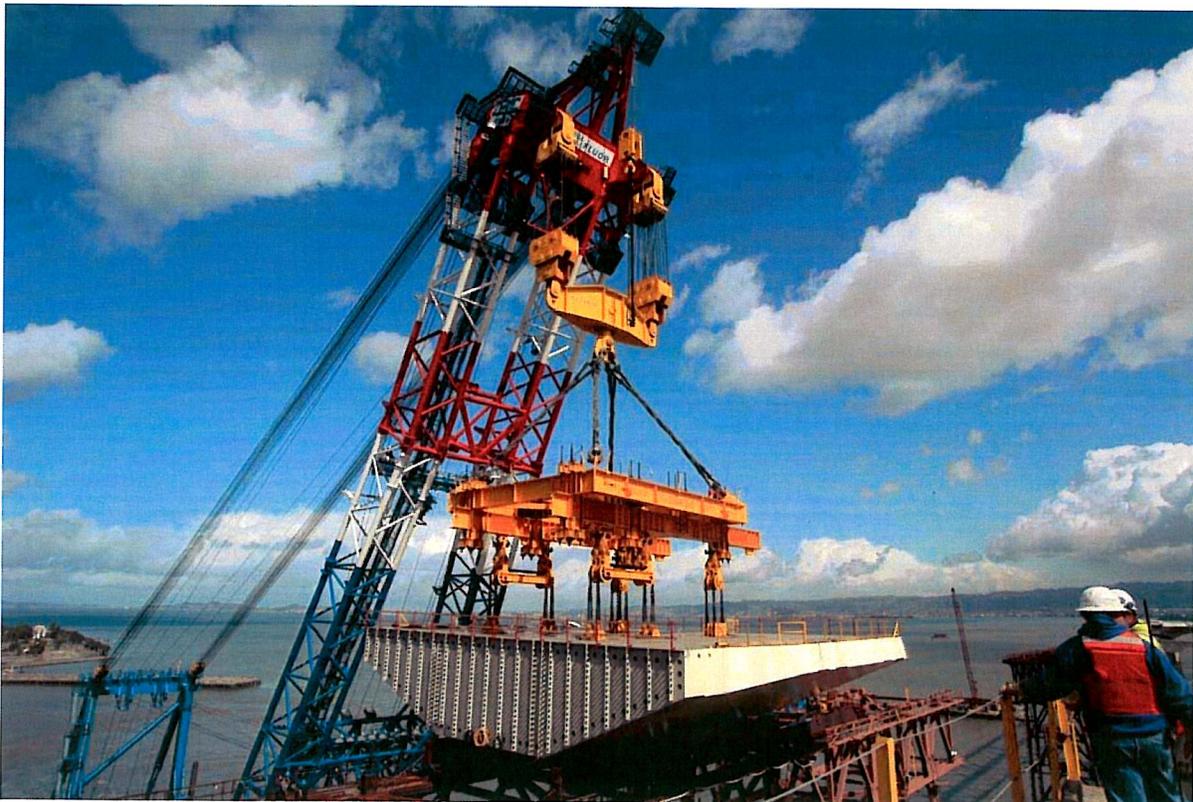

- Lift 1 West is placed on the cradle ~ 11.20am




- Lift 1 West is placed on the cradle ~ 11.20am



- Overview from the Treasure Island at 5.00pm. L1W has been slightly pushed.




- Observed 2 workers working on the Utility Opening, W2 West Footing ~ 8.00am

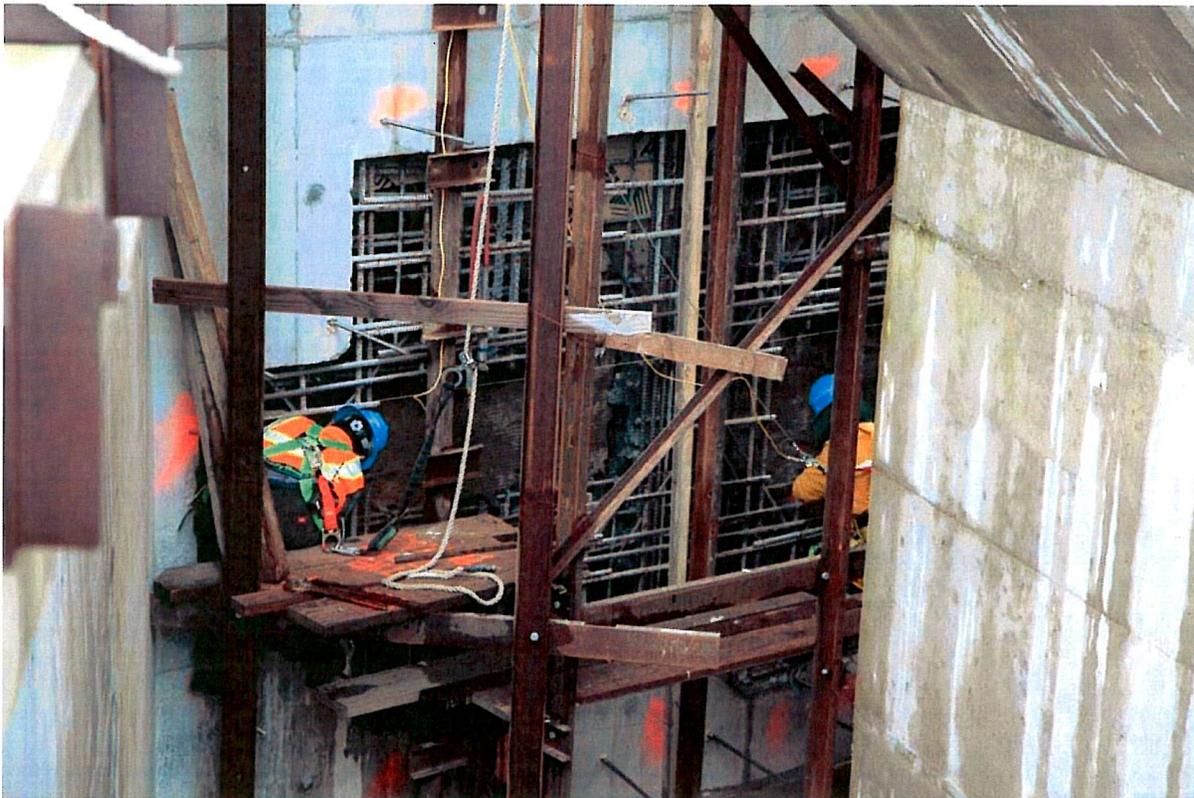

- Observed 2 workers working on the precast forms and box opening for the Utility Openings at W2 West Footing ~ 9.30am



- Observed 2 workers welding and grinding welding seams between L1E & L2E ~ 10.00am

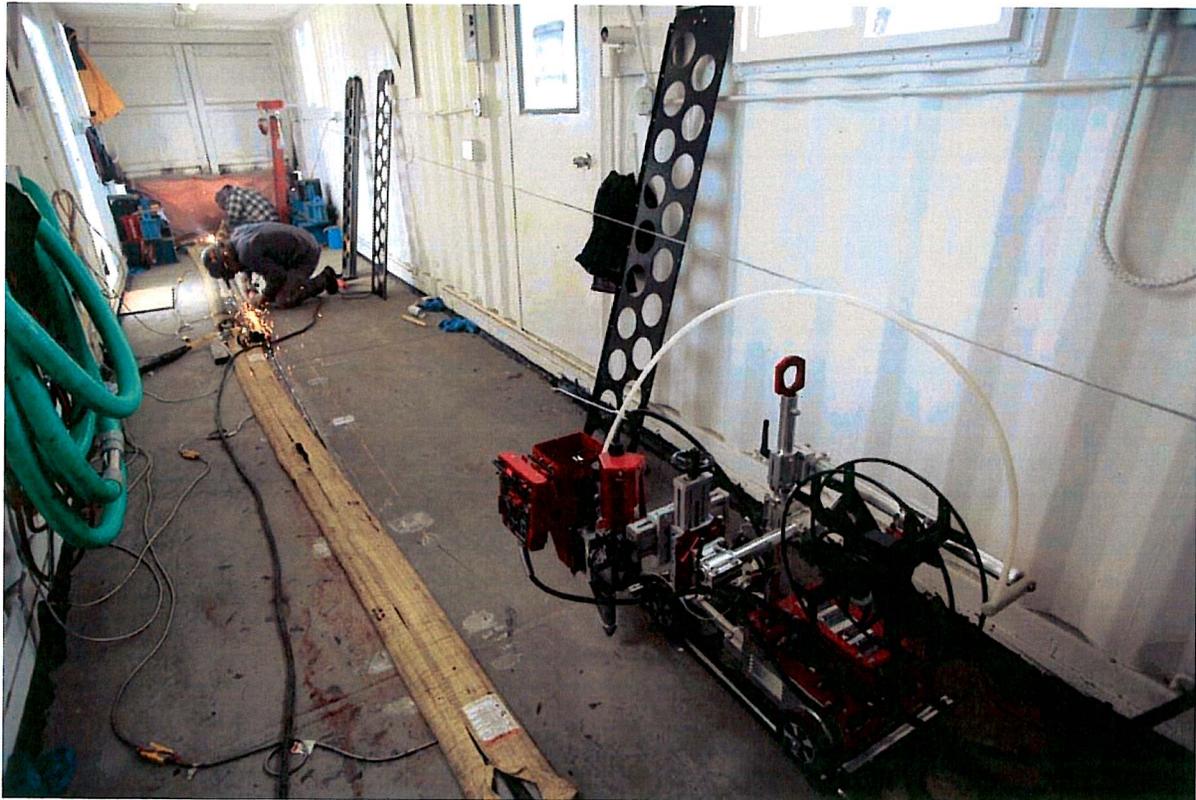

- View of the welding seams between L1E and L2E ~ 11.30am

