



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 3:56 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 037 Const Calendar Day: 182 Date: 09-Mar-2010 Tuesday

Inspector Name: He, Philip Title: Transportation Engineer

Inspection Type:

Shift Hours: 06:00 am 05:00 pm Break: Over Time:

Federal ID:

Location:

Reviewer: Liu, Tai-Lin Approved Date: 01-Apr-10 Status: Approved

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 12 PM 4PM

Precipitation Condition

Working Day If no, explain:

04-0120F4 Bid Item: 056 X-L02-CBM.056 E-W Line Cross Over Lift 02 Cross Beam

AMERICAN BRIDGE/FLUOR, A JV

Diary:

Dispute

Work description. 056 X-L02-CBM.056

1. Lifting crossbeam 01.

A. Eddie Meyer's crew of about 8 people worked on the barge before the lifting of the crossbeam 01 with the gantry system.

B. Eddie's crew went to temp. truss to finish the erection of the gantry also

2. Concrete pour for the closure pour at north and south ends of the W2 cap beam.



Attachment



Releasing the Lifting frame to gantry system



Crossbeam with gantry system lifted to temp. truss level



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name He, Philip

Diary #: 037

Date: 09-Mar-2010


Tuesday



Crossbeam 01 in Air



Crossbeam with gantry system erected on temp. truss

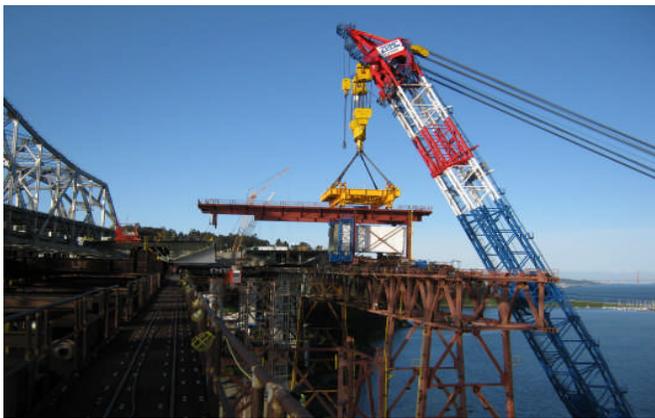


Crossbeam with gantry system erected on temp. truss



Crossbeam with gantry system lifted to temp. truss level



Start to Lift Crossbeam 01

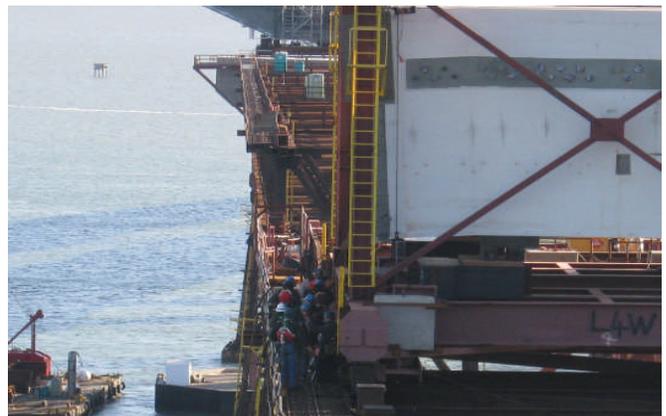

Tie down the gantry system to the temp. truss

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name He, Philip

Diary #: 037

Date: 09-Mar-2010


Tuesday



Concrete pour to the closure on sides of W2 capbeam



Releasing the Lifting frame to gantry system

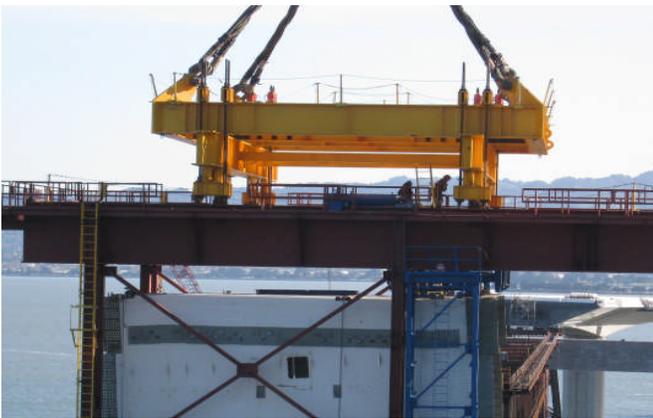

Releasing the Lifting frame to gantry system



Iron workers who just worked on shear leg barge.



Crossbeam with gantry system lifted to temp. truss level



Start to Lift Crossbeam 01

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name He, Philip

Diary #: 037


Date: 09-Mar-2010 Tuesday



Start to Lift Crossbeam 01



Installing safety devices on "W" line temp. truss

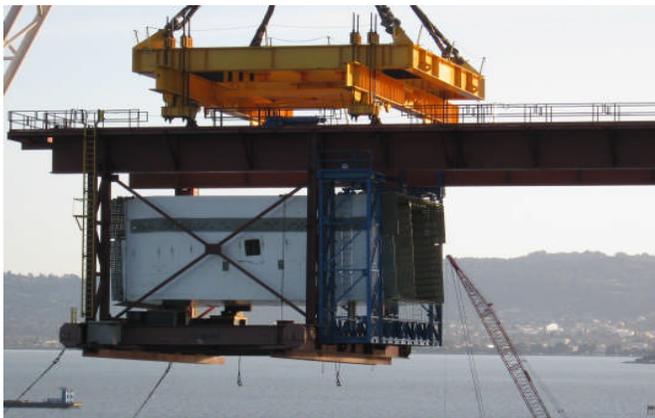

Crossbeam in Air
