



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 039 Const Calendar Day: 184 Date: 11-Mar-2010 Thursday

Inspector Name: He, Philip Title: Transportation Engineer

Inspection Type:

Shift Hours: 06:30 am 05:00 pm Break: Over Time:

Federal ID:

Location:

Reviewer: Liu, Tai-Lin Approved Date: 09-Apr-10 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature	7 AM	12 PM	4 PM
Precipitation			Condition

Working Day If no, explain:

04-0120F4 Bid Item: 056 X-L02-CBM.056 E-W Line Cross Over Lift 02 Cross Beam

AMERICAN BRIDGE/FLUOR, A JV

Diary:

Dispute

Work description. 056 X-L02-CBM.056

1. Safety meeting for SAS staff in the morning.
2. Pushed the Gantry system with the crossbeam 01 to the final location longitudinal direction along the bridge profile.
 Iron workers chained the gantry system down to the deck of "E" Line OBG lifts
3. Assemble the side platform on top of W2 cap beam.
4. Removing weld shad house from the splicing between L1E and L2E to the splice between L2E and L3E.
5. Scaffolding inside the crossbeam 01.

Attachment



Gantry in Pushing Process



Support at Gantry Leg

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name He, Philip

Diary #: 039

Date: 11-Mar-2010


Thursday



Tied Down Gantry System



Complete Gantry System

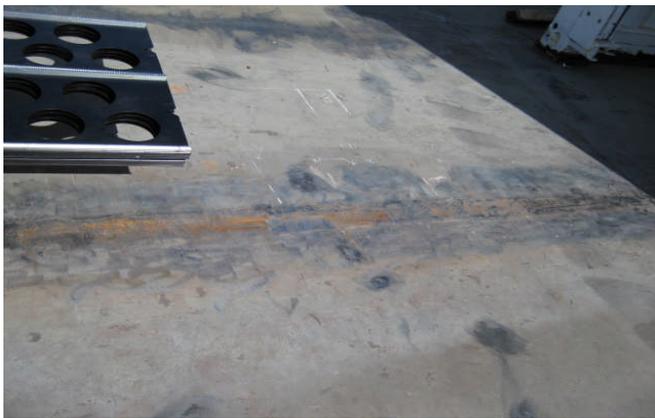

The Splice Welding between L1E and L2E



Mobil Crane RT890E



Assemble the Side Platform



Scaffolding inside the Crossbeam

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name He, Philip

Diary #: 039

Date: 11-Mar-2010

Thursday



Mobil Crane RT890E



Mobil Crane RT890E



Gantry in Pushing Process



The support of the Gantry System at the Leg Location



Gantry Parked on Temp Truss
