



# SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 22-Nov-14

Time 3:46 PM

## Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 053 Const Calendar Day: 198 Date: 25-Mar-2010 Thursday

Inspector Name: He, Philip Title: Transportation Engineer

Inspection Type:

Shift Hours: 06:30 am 05:00 pm Break: Over Time: 02:00

Federal ID:

Location:

Reviewer: Liu, Tai-Lin Approved Date: 20-Apr-10 Status: Approved

04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge

### Weather

Temperature 7 AM 12 PM 4PM

Precipitation Condition

Working Day  If no, explain:

04-0120F4 Bid Item: 056 X-L03-CBM.056 E-W Line Cross Over Lift 03 Cross Beam

AMERICAN BRIDGE/FLUOR, A JV

### Diary:

Dispute

**Work description.** 056 X-L03-CBM.056

1. Preparing Crossbeam 03 at Pier 7.
2. Relocating the welding shad from splice of L2E and L3E to L3E and L4E.
3. Connecting the strand jack to the crossbeam.
4. continuous splicing the crossbeam to L2E. Darryl's group is doing the bolt splicing for the operation.
5. Use crane RT890E, all Aaron's crew to reinstall 2 jacks damaged in the gantry system.

### Attachment



Fixing the Jack 02



Relocate the Weld Shad from previous place to new splice location



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name He, Philip

Diary #: 053

Date: 25-Mar-2010

Thursday



Gantry System supported on deck of the OBG



Gantry System supported on deck of the OBG



Damaged Jack from the Gantry System



Bolt Splicing of the crossbeam 01 and OBG Lift L2W



Preparing Crossbeam 03 at Pier 7



Relocate the Weld Shad from previous place to new splice location

# Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name He, Philip


Diary #: 053

Date: 25-Mar-2010


Thursday



Fixing the Jack 03

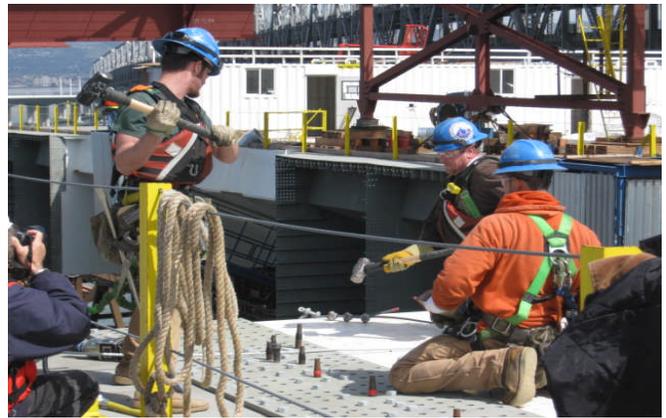

Bolt Splicing of the crossbeam 01 and OBG Lift L2W

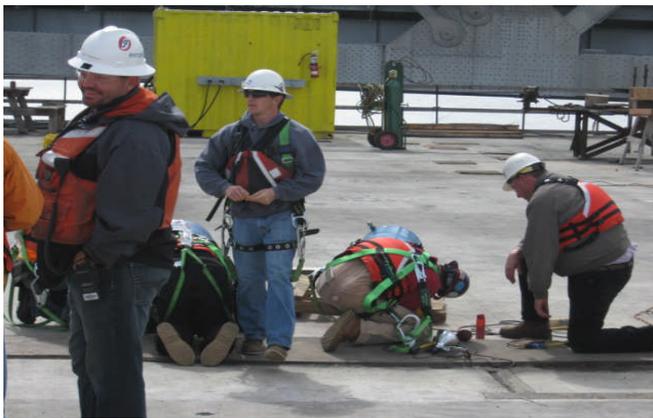


Fixing the Jack 01



Bolt Splicing of the crossbeam 01 and OBG Lift L2W



Fixing the Jack 04

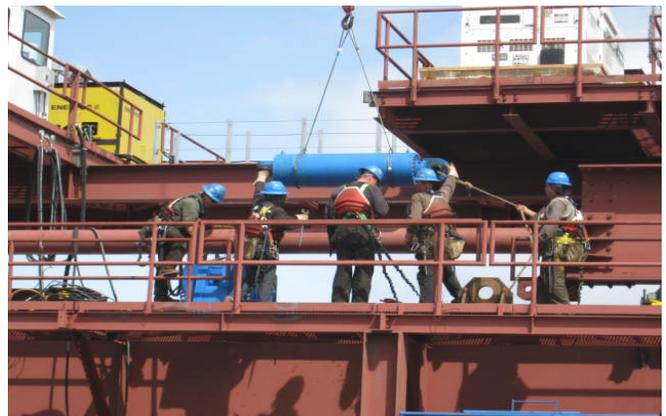

Fixing the Jack 06

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name He, Philip

Diary #: 053

Date: 25-Mar-2010 Thursday



Gantry System supported on deck of the OBG



Gantry System supported on deck of the OBG



Fixing the Jack 05
