



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 061 Const Calendar Day: 206 Date: 02-Apr-2010 Friday
 Inspector Name: He, Philip Title: Transportation Engineer

Inspection Type:
 Shift Hours: 05:30 am 05:00 pm Break: Over Time: 03:30

Federal ID:

Location:

Reviewer: Liu, Tai-Lin Approved Date: 23-Apr-10 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 12 PM 4PM
 Precipitation Condition

Working Day If no, explain:

04-0120F4 Bid Item: 056 W-L03-OBG.056 W Line Lift 03 OBG Erect structural steel (bridge box girder)
 AMERICAN BRIDGE/FLUOR, A JV

Diary:

Dispute


Work description. 056 W-L03-OBG.056

1. Lifting the OBG Lift L3W from barge to temp. truss.
2. Workers chained down the OBG Lift L3W to temp. truss. No pushing to the OBG Lift, very windy and showers on and off.
3. Jacking the north supports on the OBG to make the 2% slope. NW: 2800 psi, NE: 1600 psi.
4. Connected temp. seismic shear plates from soffit of the OBG to cradle frame on the on the north side of the OBG. Snug tight and pretension of the bolts have been checked and filed in the forms signed by both ABF and CT.

Attachment



Unhook the OBG to the Lifting Frame of the Shear Leg Barge Crane

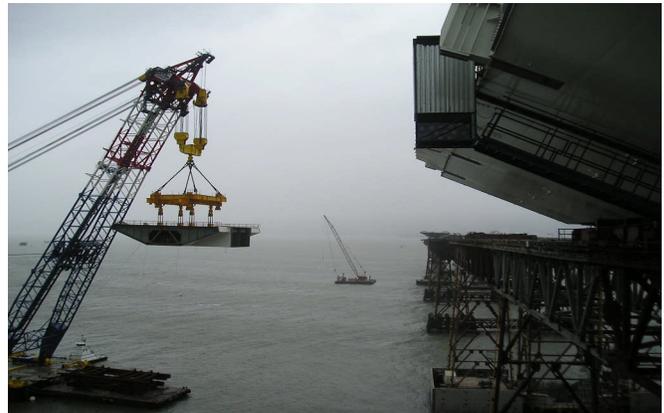

Lifting OBG Lift L3W

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name He, Philip

Diary #: 061

Date: 02-Apr-2010

Friday



Lifting OBG Lift L3W



Lifting OBG Lift L3W



Checking the Welding Splice at the Soffit of the OBG



Chaining down the OBG Lift to the temp. truss



Lifting OBG Lift L3W



Workers work on the Cradle

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name He, Philip

Diary #: 061

Date: 02-Apr-2010


Friday



Lifting OBG Lift L3W



Workers working while L3W is being lifted

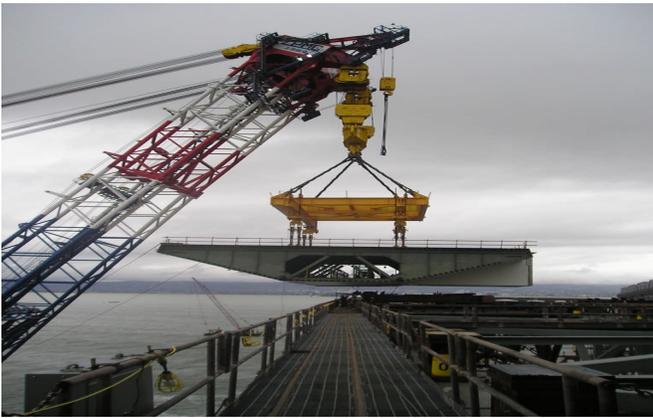

Lifting OBG Lift L3W
