



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 062 Const Calendar Day: 524 Date: 14-Feb-2011 Monday  
 Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer  
 Inspection Type:  
 Shift Hours: Break: Over Time:  
 Federal ID:  
 Location:  
 Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

**Weather**

Temperature	7 AM	12 PM	4PM
Precipitation			Condition

Working Day  If no, explain:

**Diary:**

Dispute

**Work description.**

GENERAL WORK


HINGE K FRAMING

1. Because of the rain, the crew who were involved in setting up the hinge K framing left early in the morning.
2. ABF crews started filling up the West hinge K framing by water at 12:30 and shut off the water valve at 2:00 PM because of excessive water leakage at different location of the framing. No washing of the dumped EMACO 503 powder was observed.

**ABF Crews:**

- Jose Avila (Laborer, from 12:30 to 2 PM)
- Riyobato Compas (Laborer, from 12:30 to 2 PM)

**Attachment**

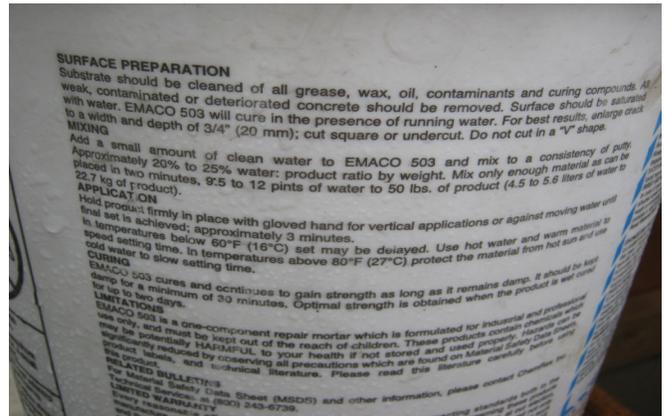

**Daily Diary Report by Bid Item**

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 062

Date: 14-Feb-2011

Monday

