



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 249 Const Calendar Day: 538 Date: 28-Feb-2011 Monday
 Inspector Name: Bruce, Matt Title: Transportation Engineer
 Inspection Type: Intermittent
 Shift Hours: 07:00 am 04:30 pm Break: 00:30 Over Time: 01:00
 Federal ID:
 Location:
 Reviewer: Mathur, Lalit Approved Date: 11-Apr-11 Status: Approved

04-0120F4
 04-SF-80-13.2/13.9
 Self-Anchored
 Suspension Bridge

Weather

Temperature 7 AM 40 - 50 12 PM 50 - 60 4PM 40 - 50
 Precipitation 0.00" Condition Partly Overcast

Working Day If no, explain:


Diary:

Dispute

Work description.

- Continued to prepare for the upcoming grouting operation of the Hinge K pipe beam assembly grout pads. Also calculated volume quantities for the grout and water to be used for the bearing pad.
- See Abbas Iranmanesh's diary for ABFs labor, equipment, and operations in regards Hinge K pipe beam assembly grout pad formwork and water testing.
- Attended weekly OBG staff meeting at 3:30pm.

Attachment

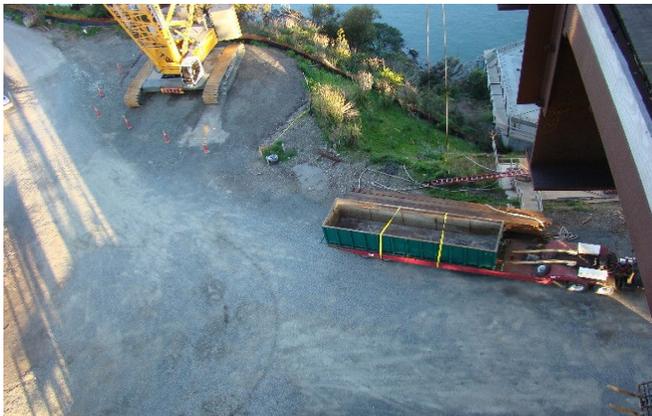

Baker tank arrives onsite as SWPPP preparations continue for the Hinge K grouting operation.



ABF laborers working on the drainage channel under the W2W Hinge K pipe beams.
