



### SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 20-Nov-14

Time 11:32 PM

## Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 156 Const Calendar Day: 707 Date: 16-Aug-2011 Tuesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 05:30 PM Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge

### Weather

Temperature 7 AM 40 - 50 12 PM 4PM 60 - 70

Precipitation None Condition

Working Day  If no, explain:

### Diary:

Dispute

#### Work description.

ABF Crews activities:

The crews continued installing the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2". The main frames which are connected to saddle at the end and rest by a pin on the front edge of the saddle and the curved beam which carries the PWS have been installed at both the East and West Line saddles so far. ABF is reinforcing the main frames by welding additional stiffeners at two locations, at the end of the frames where the frame is connected to the saddle and above the pin in front of the saddle as shown in the pictures. The work is being continued by two crews, the installers and the welders.

The extra holes drilled for PWS framing along the pier W2 was patched by two ABF crews as shown in the picture.

NOTE: ABF Labor and Equipment list is not updated.

ABF crews involved in the PWS secondary hauling system

- Jerry Kubala (FOR- Instalation)
- Im Bandol
- Rigovertto Garcia
- Walter Hernandez
- Melgar Fleix
- Joseph Stone (Only in the afternoon)
- Henry Hernandez (only in the afternoon)
- Kevin Alger (Crane Operator)
- Ian Murphy (Only in the afternoon)
- Rick Clayman (FOR- Welding)(Only in the afternoon)
- Salvador Sandoval (Only in the afternoon)

ABF Equipment:

Crane Terex RT160

Miller welding machine

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

### Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								

## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name:** Iranmanesh, Abbas    **Diary #:** 156    **Date:** 16-Aug-2011    **Tuesday**

Ironworker	JNM	FELIX MELGAR	8.00	2.00	0.00	10.00	<input type="checkbox"/>
		Im Bandoi	8.00	2.00	0.00	10.00	<input type="checkbox"/>
		Rick Clayman	4.00	2.00	0.00	6.00	<input type="checkbox"/>
Ironworker	JNM	SALVADOR SANDOVAL	4.00	2.00	0.00	6.00	<input type="checkbox"/>
Ironworker	APP	IAN MURPHY	4.00	2.00	0.00	6.00	<input type="checkbox"/>
Operator	OTH	KEVIN ALGER	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	APP	HENRY HERNANDEZ	4.00	2.00	0.00	6.00	<input type="checkbox"/>
Ironworker	JNM	JOSEPH STONE	4.00	2.00	0.00	6.00	<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELED	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	2.00	0.00	10.00	<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	2.00	0.00	10.00	<input type="checkbox"/>

Equipment						Rental Company	
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV							
2154	EQUIPMENT, CRANE, 60 TON					No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00		
002242	WELDING EQUIPMENT					No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00		

**04-0120F4    Bid Item: 060    W-W2C-WDS.060    W Line W2 Cap West Deviation Saddle**  
 AMERICAN BRIDGE/FLUOR, A JV

**Attachment**



**Daily Diary Report by Bid Item**


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 156

Date: 16-Aug-2011

Tuesday

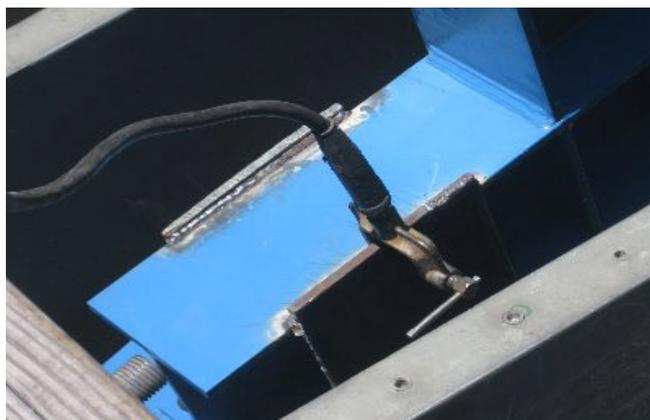

# Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 156

Date: 16-Aug-2011

Tuesday

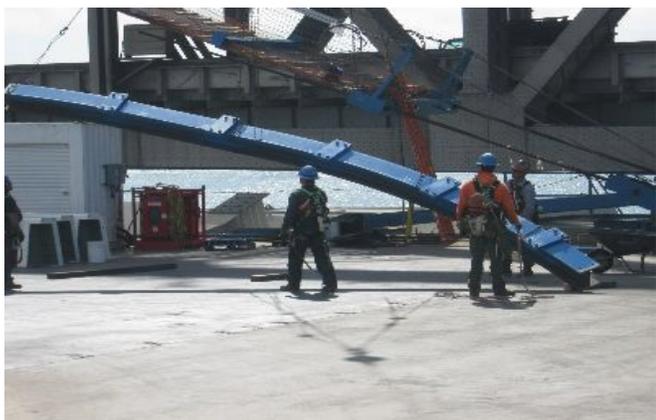

---

**Daily Diary Report by Bid Item**

**Job Name:** 04-0120F4

**Inspector Name:** Iranmanesh, Abbas

**Diary #:** 156

**Date:** 16-Aug-2011 **Tuesday**

---

