



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 158 Const Calendar Day: 709 Date: 18-Aug-2011 Thursday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time: 2:00

Federal ID:

Location:

Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

**Weather**

Temperature 7 AM 40 - 50 12 PM 4PM 60 - 70

Precipitation None Condition

Working Day  If no, explain:

**Diary:**

Dispute

**Work description.**

ABF Crews activities:

The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" as follows:

- A) All the brackets holding the PWS frames on the pier W2 wall surface were installed. Since all the driven holes were not perpendicular to the pier wall surface most of the anchor bolts were tightened in a bending condition, some of the brackets fitted by the help of a heavy hammer. The anchor bolts were driven while the anchor plate was in the right position.
- B) One of the PWS frames was fabricated incorrectly in the shop. The leg was cut, rotated 180 degree and welded again. Besides, one of the PWS anchor plates needed some modifications which correction was done at the job site.
- C) The reinforcing the PWS framing stem is being continued and not completed yet. The welding crews have been informed to cover the saddle while welding.
- D) Another ABF crews started installing the scaffolding required for the PWS hauling system at the East line saddle.
- E) The attached pictures explain the detail of the work.

NOTE: ABF Labor and Equipment list is not updated.

ABF crews involved in the PWS secondary hauling system

A) Installation crews:

- Jerry Kubala (FOR- Installation)
- Im Bandol
- Rigovertto Garcia
- Walter Hernandez
- Melgar Fleix
- Joseph Stone
- Henry Hernandez
- Kevin Alger (Crane Operator)
- Clinton Montgomery (Lift Truck Operator)

B) Welding Crews

- Ian Murphy
- Rick Clayman (FOR- Welding)
- Salvador Sandoval

## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name:** Iranmanesh, Abbas    **Diary #:** 158    **Date:** 18-Aug-2011    **Thursday**

C) Scaffolding  
 -Julian Paul  
 -Jack Hunter  
 - Jeff Stewart  
 - David Lucero  
 - Jose Avila (Laborer)

ABF Equipment:  
 Crane Terex RT160  
 Miller welding machine (ABF002242)  
 Lincoln Welding machine (ABF002082)  
 Liftman 4x4 GS2668RT  
 ForkLift (GRADALL)

**04-0120F4    Bid Item: 060    E-W2C-WDS.060    E Line W2 Cap West Deviation Saddle**

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	FELIX MELGAR	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELED	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	JOSEPH STONE	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	OTH	KEVIN ALGER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	IAN MURPHY	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	SALVADOR SANDOVAL	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
		Im BandoI	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	DAVID LUCERO	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	HENRY HERNANDEZ	4.00	2.00	0.00	6.00		<input type="checkbox"/>
Ironworker	JNM	JACK HUNTER	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	JEFFERY STEWART	8.00	0.00	0.00	8.00		<input type="checkbox"/>
		Julian Paul	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	JOSE AVILA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Operator	APP	CLINTON MONTGOMERY	0.00	2.00	0.00	2.00		<input type="checkbox"/>
		Rick Clayman	8.00	2.00	0.00	10.00		<input type="checkbox"/>

**Equipment**

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
000437	FORKLIFT, GRADALL 544D 10,000 LBS						No	<input type="checkbox"/>
		0.00	2.00	0.00	0.00			<input type="checkbox"/>
*E0120406							No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
2154	EQUIPMENT, CRANE, 60 TON						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
002242	WELDING EQUIPMENT						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
002082	WELDER, LINCOLN 500-549 AMP DSL/TOW						No	<input type="checkbox"/>
		8.00	2.00	0.00	0.00			<input type="checkbox"/>

**04-0120F4    Bid Item: 060    W-W2C-WDS.060    W Line W2 Cap West Deviation Saddle**

AMERICAN BRIDGE/FLUOR, A JV

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 158

Date: 18-Aug-2011 Thursday

### Attachment



# Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 158

Date: 18-Aug-2011

Thursday



# Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 158

Date: 18-Aug-2011

Thursday

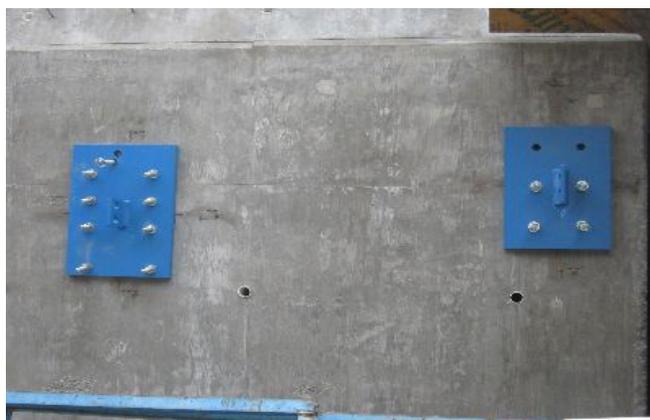

# Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 158

Date: 18-Aug-2011

Thursday



## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 158

Date: 18-Aug-2011 Thursday

