



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 159 Const Calendar Day: 710 Date: 19-Aug-2011 Friday  
 Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer  
 Inspection Type: Intermittent  
 Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time: 02:00

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

Federal ID:

Location:

Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

**Weather**

Temperature 7 AM 40 - 50 12 PM 4PM 60 - 70  
 Precipitation None Condition partly cloudy

Working Day  If no, explain:

**Diary:**

Dispute

**Work description.**

ABF Crews activities:

- A) ABF-SUB-2312R00. "Cable Erection Plan-Primary PWS Hauling System": The bracket of the Tramway Guide Sheaves of the PWS primary hauling system was installed at the south side of the East line..
- B) ABF-SUB-2171R01. "PWS Restraint System at Pier W2": Two frames are connected to the brackets which were installed on the wall of pier W2.
- C) Another ABF crews continued installing the scaffolding required for the secondary PWS hauling system at North side of the West line saddle.
- D) ABF-SUB2019R02 "West End Tramway:: ABF crew started drilling holes for the bracket of the End Tramway. From 34 drilled holes, 24 of them reached the bar reinforcement. No further action is taken.
- E) NOTE: ABF Labor and Equipment list is not updated.

ABF crews involved in the PWS secondary hauling system

A) Installation crews:

- Jerry Kubala (FOR- Installation)
- Rigoverta Garcia
- Walter Hernandez
- Fleix Melgar
- Joseph Stone
- Henry Hernandez
- Jose Avila (laborer)
- Kevin Alger (Crane Operator)

B) Welding Crews

- Salvador Sandoval
- Paul Fambrini

C) Scaffolding

- Julian Paul
- Jack Hunter
- Jeff Stewart
- David Lucero

- Rogelio Ruiz

ABF Equipment:

Crane Terex RT160

Miller welding machine (ABF002242)



## Daily Diary Report by Bid Item

Job Name: 04-0120F4    Inspector Name: Iranmanesh, Abbas    Diary #: 159    Date: 19-Aug-2011    Friday

Lincoln Welding machine (ABF002082)  
Liftman 4x4 GS2668RT

**04-0120F4    Bid Item: 060    E-W2C-WDS.060    E Line W2 Cap West Deviation Saddle**

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	JACK HUNTER	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELED	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	JOSEPH STONE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Operator	OTH	KEVIN ALGER	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	SALVADOR SANDOVAL	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	HENRY HERNANDEZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	DAVID LUCERO	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	JEFFERY STEWART	8.00	0.00	0.00	8.00		<input type="checkbox"/>
		Julian Paul	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	ROGELIO RUIZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	MORRIS ROBERSON	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	APP	PAUL FAMBRINI	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	JOSE AVILA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>

**Equipment**

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
*E0120406							No	<input type="checkbox"/>
2154	EQUIPMENT, CRANE, 60 TON	4.00	0.00	0.00	0.00		No	<input type="checkbox"/>
002242	WELDING EQUIPMENT	8.00	0.00	0.00	0.00		No	<input type="checkbox"/>
002082	WELDER, LINCOLN 500-549 AMP DSL/TOW	8.00	0.00	0.00	0.00		No	<input type="checkbox"/>
		8.00	0.00	0.00	0.00		No	<input type="checkbox"/>

**04-0120F4    Bid Item: 060    W-W2C-WDS.060    W Line W2 Cap West Deviation Saddle**

AMERICAN BRIDGE/FLUOR, A JV

Attachment

# Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 159

Date: 19-Aug-2011

Friday



# Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 159

Date: 19-Aug-2011

Friday

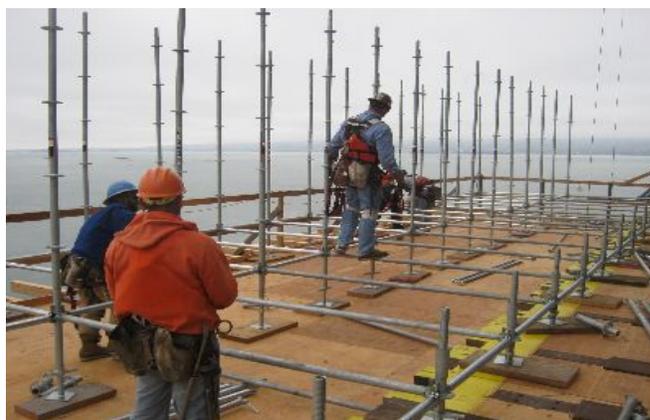

# Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 159

Date: 19-Aug-2011

Friday



---

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 159

Date: 19-Aug-2011

Friday

---

