



**SAS Superstructure**

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 20-Nov-14

Time 11:26 PM

**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 161 Const Calendar Day: 713 Date: 22-Aug-2011 Monday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 05:30 pm Break: 00:30 Over Time: 02:00

Federal ID:

Location:

Reviewer: Boal, Brian Approved Date: 10-Oct-13 Status: Approved

04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge

**Weather**

Temperature 7 AM 50 - 60 12 PM 4PM 60 - 70

Precipitation None Condition Clear

Working Day  If no, explain:

**Diary:**

Dispute

**Work description.**

ABF Crews activities:



1- The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" as follows:

- A) The PWS guide beam and channel sections supporting the rollers were installed. In three locations the welded plate provided for connection to the supporting frame was mismatched. The correction is being done by relocating the plates.
- B) The reinforcing of the PWS framing system is being continued at the West line framing by welding the bracing system. The work was mainly on the North side framing of the W-Line. The saddle was covered by protective fabric during the welding as instructed.
- C) Welding also was performed on the South side of the East line framing system by welding stiffeners above the pine located at the second support of the frames in front of the saddle.
- D) The PWS framing on the pier W2 wall still is not stable, after necessary adjustment additional connections welding will make it stable.

2- Another ABF crew completed the installing scaffolding required for the PWS hauling system at the North side of the West line saddle.

The attached pictures show the detail of the performed activities.

NOTE: ABF Labor and Equipment list is not updated.

ABF crews involved in the PWS secondary hauling system

A) Installation crews:

- Jerry Kubala (FOR- Installation)
- Walter Hernandez
- Melgar Fleix
- Rigoverto Garcia
- Kevin Alger (Crane Operator)

B) Welding Crews

- Salvador Sandoval
- Jose Torres
- Michael Jimenez
- Rick Clayman (Only 3 hours)
- Ian Murphy (Only 3 hours)

## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name:** Iranmanesh, Abbas    **Diary #:** 161    **Date:** 22-Aug-2011    **Monday**

C) Scaffolding Crews  
 - David Lucero (FOR)  
 -Julian Paul  
 - Jeff Stewart  
 - Jack hunter  
 - John Power  
 - Rogelio Ruiz

Laborer:  
 - Jose Avila

ABF Equipments:  
 Crane Terex RT160  
 Miller welding machine (ABF002242)  
 Miller Welding Machine (ABF002303)  
 Lincoln Welding machine (ABF002082) (Only 3 hours)  
 Liftman 4x4 GS2668RT

**04-0120F4      Bid Item: 051      0-000-000.051      ERECT STRUCTURAL STEEL (BRIDGE)**  
 AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4      Bid Item: 060      E-W2C-WDS.060      E Line W2 Cap West Deviation Saddle**  
 AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	ROGELIO RUIZ	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELED	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Operator	OTH	KEVIN ALGER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	DAVID LUCERO	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	JACK HUNTER	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JEFFERY STEWART	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	FOR	JOSE AVILA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
		GLEN PAULK	8.00	2.00	0.00	10.00		<input type="checkbox"/>
		RICK CLAYMAN	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Ironworker	APP	IAN MURPHY	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Ironworker	JNM	SALVADOR SANDOVAL	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL JIMENEZ	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	JOHN POWER	8.00	0.00	0.00	8.00		<input type="checkbox"/>

**Equipment**


Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
*E0140406	WELDING EQUIPMENT						No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
*E0130406							No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>
002154	Equipment, Crane, 60 Ton						No	
		8.00	2.00	0.00	0.00			<input type="checkbox"/>

## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name:** Iranmanesh, Abbas    **Diary #:** 161    **Date:** 22-Aug-2011    **Monday**

002242	WELDING EQUIPMENT		8.00	2.00	0.00	0.00	No	<input type="checkbox"/>
002082	WELDER, LINCOLN 500-549 AMP DSL/TOW		3.00	0.00	0.00	0.00	No	<input type="checkbox"/>
<b>04-0120F4</b>	<b>Bid Item: 060</b>	<b>W-W2C-WDS.060</b>	<b>W Line W2 Cap West Deviation Saddle</b>					
AMERICAN BRIDGE/FLUOR, A JV								
<b>04-0120F4</b>	<b>Bid Item: 060</b>	<b>X-W2C-JKS.060</b>	<b>E-W Line Cross Over W2 Cap Jacking Saddle</b>					
AMERICAN BRIDGE/FLUOR, A JV								

**Attachment**

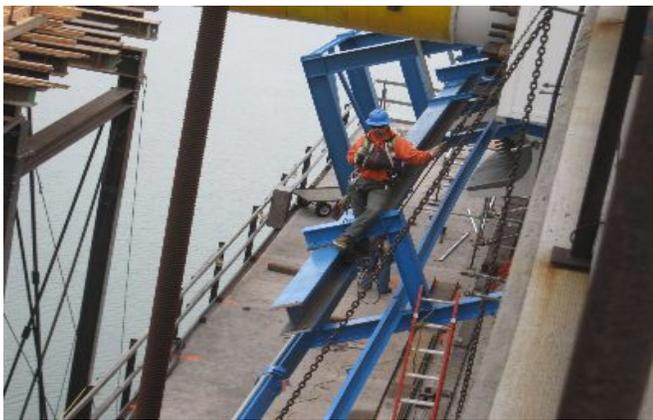

# Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 161

Date: 22-Aug-2011

Monday



# Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 161

Date: 22-Aug-2011

Monday

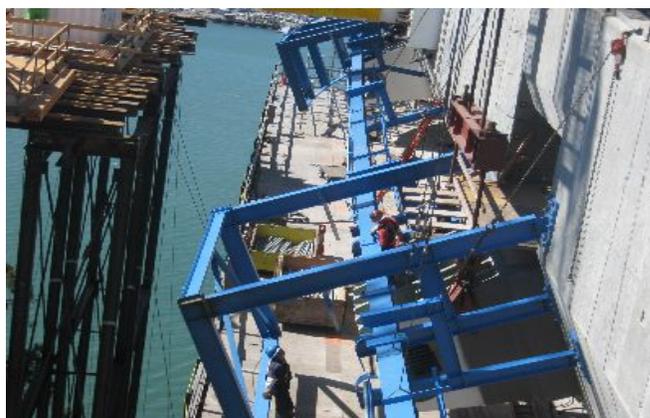

# Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 161

Date: 22-Aug-2011

Monday

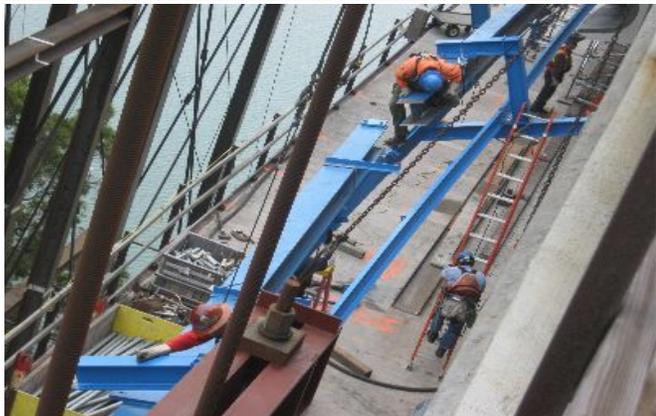

# Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name: Iranmanesh, Abbas

Diary #: 161

Date: 22-Aug-2011

Monday

