



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 1:23 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 170 Const Calendar Day: 723 Date: 01-Sep-2011 Thursday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4  
04-SF-80-13.2/13.9  
Self-Anchored  
Suspension Bridge

Weather

Temperature 7 AM 50 - 60 12 PM 4PM 70 - 80  
Precipitation None Condition partly cloudy

Working Day  If no, explain:

Diary:

Dispute

Work description.

ABF Crews activities:

1- The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" and Primary PWS with respect to submittal ABF-2312R00, "Primary PWS Hauling System", as follows:

INSTALLATION:

- Two rows of cables were attached to the outside member of the saddle frames for protection while the Secondary PWS hauling system is in operation.
• Since the two channels steel sections provided for the rollers have shown considerable lateral deflection, ABF has decided to add steel angles at intervals in order to limit the lateral deflection. The paint at these locations along the channels at the steel angles position was removed.
• The ABF crew tightened all the bolts of the North and South Tramway Haul rope Deflection Sheave Structures.
• The last segment of the Rail beam (PWS Guide Beam) at the south side of Pier W2 was welded and the deflection sheave bracket shown in the Drawing No. ABN-02-19/6 of the submittal ABF-SUB--2283R00 was put in place by force. As shown in the pictures, the height of the sheave bracket is short and the Ironworkers are planning to fix it tomorrow.

FORMING:

2- The ABF crew are providing framing around the winch base steel frame and making it ready for grouting, Drawing No. DE431B of the submittal ABF-SUB--2283R00.

3- The attached pictures show the detail of the performed activities.

ABF crew involved in Secondary hauling system

- Installation crew:
- Jerry Kubala (FOR- Installation)
- Walter Hernandez
- Melgar Fleix
- Rigoverto Garcia
- Patrick Oleary
- Scott Ross (Crane Operator)
- Rick Clayborn



## Daily Diary Report by Bid Item

**Job Name:** 04-0120F4    **Inspector Name** Iranmanesh, Abbas    **Diary #:** 170    **Date:** 01-Sep-2011    **Thursday**

- Ian Murphy

ABF Crew involved in framing.

- Froylan Ruiz
- Raca Campos

ABF Equipments:

- Crane Terex RT160
- Lincoln Welding Machine
- Generator 7000 WATT

**04-0120F4      Bid Item: 051      0-000-000.051      ERECT STRUCTURAL STEEL (BRIDGE)**  
 AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4      Bid Item: 060      E-W2C-WDS.060      E Line W2 Cap West Deviation Saddle**  
 AMERICAN BRIDGE/FLUOR, A JV

Labor								Dispute
Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV								
		RACA CAMPOS	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FROYLAN RUIZ-AYALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker		RICK CLAYBORN	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Ironworker	APP	IAN MURPHY	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Ironworker	APP	PATRICK OLEARY	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Operator	APP	SCOTT ROSS	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

Equipment							Dispute
Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Remarks	
<b>Contractor:</b> AMERICAN BRIDGE/FLUOR, A JV							
002202	GENERATOR, 7000 WATT	8.00	0.00	0.00	0.00	No	<input type="checkbox"/>
002082	WELDER, LINCOLN 500-549 AMP DSL/TOW	3.00	0.00	0.00	0.00	No	<input type="checkbox"/>
002154	Equipment, Crane, 60 Ton	3.00	0.00	0.00	0.00	No	<input type="checkbox"/>

**04-0120F4      Bid Item: 060      W-W2C-WDS.060      W Line W2 Cap West Deviation Saddle**  
 AMERICAN BRIDGE/FLUOR, A JV

**04-0120F4      Bid Item: 060      X-W2C-JKS.060      E-W Line Cross Over W2 Cap Jacking Saddle**  
 AMERICAN BRIDGE/FLUOR, A JV

**Attachment**



## Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 170

Date: 01-Sep-2011

Thursday

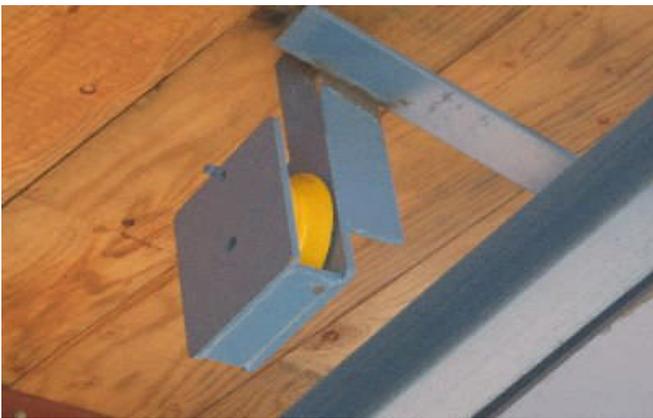

# Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 170

Date: 01-Sep-2011

Thursday

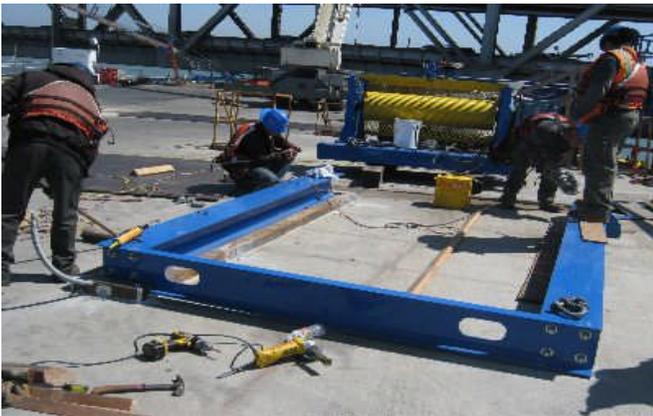

**Daily Diary Report by Bid Item**


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 170

Date: 01-Sep-2011

Thursday

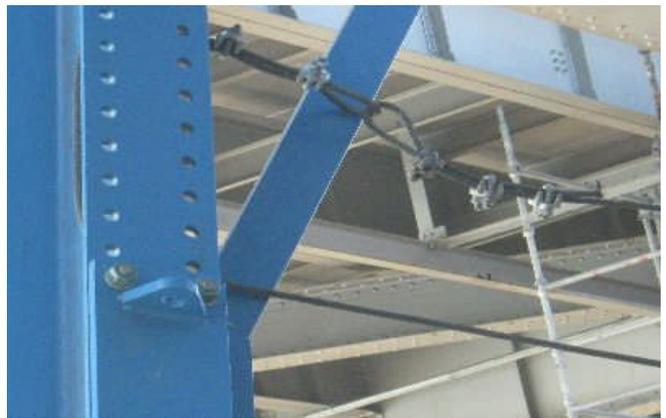

**Daily Diary Report by Bid Item**

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 170

Date: 01-Sep-2011

Thursday

