



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 1:11 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 183 Const Calendar Day: 743 Date: 21-Sep-2011 Wednesday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:00 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 70 - 80 12 PM 4PM 80 - 90

Precipitation None Condition Clear

Working Day If no, explain:

Diary:

Dispute

Work description.

ABF Crews activities:

1- The crews continued working on the framing system of the secondary PWS with respect to the submittal ABF-SUB-2171R01, "PWS Restraint System at Pier W2" and submittal ABF-2283R00, "Cable Erection Plan-Secondary PWS Hauling System", as follows:

INSTALLATION:

- The post HSS 76x76x9.5 shown in drawing No. DE419QT, Sections A, B, & C which includes the framing system between the two saddles has been modified from the inclined position to the vertical condition. The modified drawings of the submittal ABF-SUB-2171R01 will be submitted latter. Almost half of The horizontal arms have been installed, total of 22.
- ABF superintendent, Jerry King and ABF crew set up the power supply terminal and tested the winch with a temporary rope. The winch showed a good performance after several times of testing. ABF will set up the permanent rope very soon.
- Some adjustments were performed on the rollers of the E-line saddle frames.
- ABF crew repaired some of the guardrails close to the North side of Pier W2.

2- The attached pictures show the detail of the performed activities.

ABF crew involved in the Secondary hauling system

Installation crew:

- Jerry Kubala (FOR. - Installation)
- Walter Hernandez
- Melgar Fleix
- Rigovertto Garcia

- Guardrails Repair:

- Jose Avila
- Victor Hernanadez

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV



Daily Diary Report by Bid Item

Job Name: 04-0120F4 **Inspector Name** Iranmanesh, Abbas **Diary #:** 183 **Date:** 21-Sep-2011 **Wednesday**

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle
 AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Semi-Skilled Laborer	FOR	JOSE AVILA	2.00	0.00	0.00	2.00		<input type="checkbox"/>
Semi-Skilled Laborer	APP	VICTOR HERNANDEZ	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	0.00	0.00	8.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	0.00	0.00	8.00		<input type="checkbox"/>

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle
 AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 X-W2C-JKS.060 E-W Line Cross Over W2 Cap Jacking Saddle
 AMERICAN BRIDGE/FLUOR, A JV

Attachment



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 183

Date: 21-Sep-2011

Wednesday

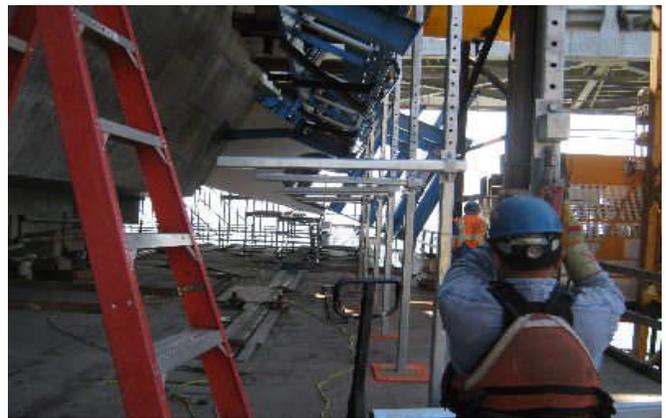

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 183

Date: 21-Sep-2011

Wednesday

