



SAS Superstructure

Location: 04-SF-80-13.2 / 13.9

Client Name: CalTrans

Run date 21-Nov-14

Time 1:05 PM

Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 189 Const Calendar Day: 751 Date: 29-Sep-2011 Thursday

Inspector Name: Iranmanesh, Abbas Title: Transportation Engineer

Inspection Type: Intermittent

Shift Hours: 07:30 am 03:30 pm Break: 00:30 Over Time:

Federal ID:

Location:

Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 60 - 70 12 PM 4PM 70 - 80

Precipitation None Condition Clear

Working Day If no, explain:

Diary:

Dispute

Work description.

ABF Crews activities:

1- The crews continued working At Pier W2 with respect to some of the following submittals

- ABF-SUB-2171R01, "PWS Restraint System at Pier W2".
- ABF-2283R00, "Cable Erection Plan-Secondary PWS Hauling System".
- ABF-SUB-002019R02, "West End Tramway".
- ABF-SUB-002506R00, "Cable Erection Plan-W2 Transfer Arms".
- ABF-SUB-002393R00, "Pier W2 Access Platform".

INSTALLATION:

- ABF crews cleaned the saddles with the compressed air and removed all the extra steel pieces from the PWS hauling area.
- Much work is done on the connecting of the hydraulic hoses between the hydraulic jacks of all the steel frames.
- The ABF crews completed widening the diameter of the Tramway Strand Anchorage Frame holes at pier W2 (North) in order to make more room for the anchor bolt epoxy.
- The ABF crews completed installing the grease cap of the Hinge-K Macalloy rods with neoprene seal washer plates with bolts at the South side Hinge-K of the E-Line after cleaning the rods.
- ABF crews are setting up a platform on top of the jacking saddle.
- ABF crews started the process of installing the Transfer Arm at the North side of Pier W2.

2-The attached pictures show the detail of the performed activities.

ABF crew involved in the Secondary hauling system

Installation crew:

- Jerry Kubala (FOR. - Installation)
- Melgar Fleix
- Rigovertto Garcia
- Walter Hernandez
- John Power
- Scott (Crane Op.)

Installing the hydraulic jacks and hoses

- Gene Pratt
- Jack Hunter



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 189 Date: 29-Sep-2011 Thursday

-David Lucero
 -Rogelio Ruiz
 -Jeff Stewart
 Julian Paul
 - Eulises Torres

Cleaning the PWS hauling area crews:

-Ian Murphy
 -Jose Torres

Jacking saddle platform

-Jose Prado
 -Froylan Ruiz

Equipment:

Grove crane (ABF-002363)

04-0120F4 Bid Item: 051 0-000-000.051 ERECT STRUCTURAL STEEL (BRIDGE)

AMERICAN BRIDGE/FLUOR, A JV

04-0120F4 Bid Item: 060 E-W2C-WDS.060 E Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV

Labor

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	JACK HUNTER	2.50	0.00	0.00	2.50		<input type="checkbox"/>
Ironworker	JNM	FELIX MELGAR	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	WALTER HERNANDEZ-ZELE	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	JOHN POWER	5.00	0.00	0.00	5.00		<input type="checkbox"/>
Ironworker	APP	IAN MURPHY	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Mechanic	FOR	GENE PRATT	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JOSE TORRES	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Operator	APP	SCOTT ROSS	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Ironworker	FOR	DAVID LUCERO	0.50	0.00	0.00	0.50		<input type="checkbox"/>
Ironworker	JNM	ROGELIO RUIZ	0.50	0.00	0.00	0.50		<input type="checkbox"/>
Ironworker	APP	JEFFERY STEWART	2.50	0.00	0.00	2.50		<input type="checkbox"/>
		JULIAN PAUL	2.50	0.00	0.00	2.50		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	JOSE PRADO	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Semi-Skilled Laborer	JNM	FROYLAN RUIZ-AYALA	3.00	0.00	0.00	3.00		<input type="checkbox"/>
Operator	APP	EULISES TORRES	8.00	2.00	0.00	10.00		<input type="checkbox"/>

Equipment

Equipment ID	Description	RT Hrs	OT Hrs	ST Hrs	IT Hrs	Rental Company	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
*E0250406						No		
		3.00	0.00	0.00	0.00			<input type="checkbox"/>

04-0120F4 Bid Item: 060 W-W2C-WDS.060 W Line W2 Cap West Deviation Saddle

AMERICAN BRIDGE/FLUOR, A JV



Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Iranmanesh, Abbas Diary #: 189 Date: 29-Sep-2011 Thursday

04-0120F4	Bid Item: 060	X-W2C-JKS.060	E-W Line Cross Over W2 Cap Jacking Saddle
AMERICAN BRIDGE/FLUOR, A JV			

Attachment



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 189

Date: 29-Sep-2011

Thursday



Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 189

Date: 29-Sep-2011

Thursday



Daily Diary Report by Bid Item


Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 189

Date: 29-Sep-2011

Thursday

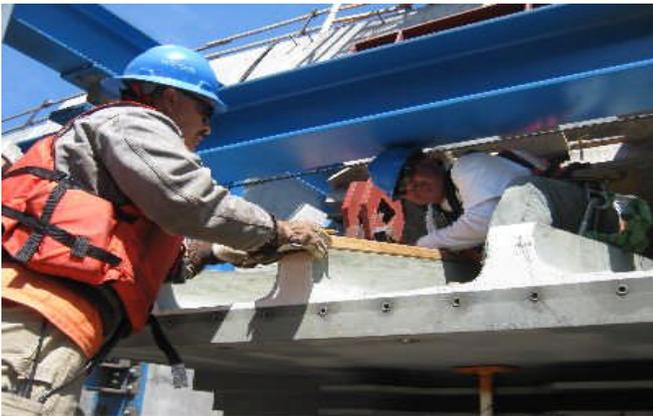

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Iranmanesh, Abbas

Diary #: 189

Date: 29-Sep-2011

Thursday

