



Daily Diary Report by Bid Item

Contract No.: 04-0120F4

Diary #: 458 Const Calendar Day: 828 Date: 15-Dec-2011 Thursday

Inspector Name: Bruce, Matt Title: Transportation Engineer

Inspection Type:

Shift Hours: Break: Over Time:

Federal ID:

Location:

Reviewer: Mathur, Lalit Approved Date: Status: Submit

04-0120F4
04-SF-80-13.2/13.9
Self-Anchored
Suspension Bridge

Weather

Temperature 7 AM 40 - 50 12 PM 50 - 60 4PM 40 - 50
 Precipitation 0.00" Condition Fog to partly cloudy

Working Day If no, explain:

Diary:

Dispute

Work description.


- Attended weekly SAS Safety Tailgate meeting at 8:00am.
- Showed Alta Vista consultants Dave Garrett (survey party chief), Chris Ferrucci (instrumentman), and Erol Schaller (rodman) the control on Treasure and Yerba Buena Islands with Rick Erskine. All three consultants worked 8 hours today.
- Shot across the bay from both San Francisco to Oakland using control points WP306 to MOLE to check the distance between the points with the Alta Vista total station.
- Gave Alta Vista surveyors Dave Garrett and Chris Ferrucci some of the documents related to the first cable strand survey and the Caltrans SFOBB project control file list.
- Continued processing surveying data from last week and earlier this week since I was showing the consultants around the project and familiarizing them with the upcoming 1st cable strand survey.



Attachment



Alta Vista surveyors preparing to take a shot across the bay from WP306 to MOLE.

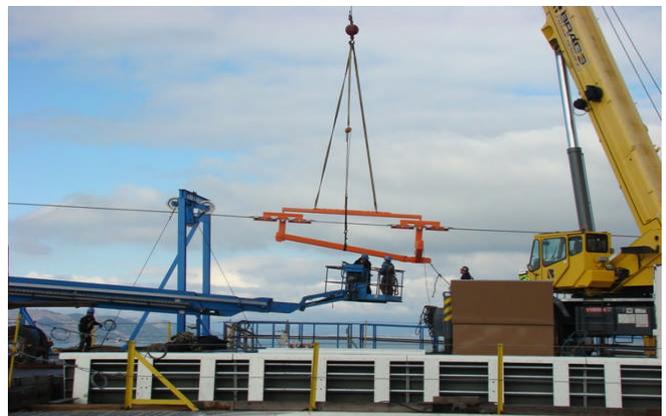

Hauling frame placed on the hauling rope cable today near the W-Line anchorage.

Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Bruce, Matt

Diary #: 458

Date: 15-Dec-2011

Thursday



The Trimble total station used by the Alta Vista surveyors set-up to take a shot across the bay from MOLE to WP306.



Working platforms constructed in OBG lift 13E for the upcoming cable strand hauling/placement.
