



**Daily Diary Report by Bid Item**

Contract No.: 04-0120F4

Diary #: 069 Const Calendar Day: 853 Date: 09-Jan-2012 Monday  
 Inspector Name: Altamirano, Victor Title: Transportation Engineer  
 Inspection Type:  
 Shift Hours: Break: Over Time:  
 Federal ID:  
 Location:  
 Reviewer: Schmitt, Alex Approved Date: Status: Submit

04-0120F4  
 04-SF-80-13.2/13.9  
 Self-Anchored  
 Suspension Bridge

**Weather**

Temperature 7 AM 50 - 60 12 PM 40 - 50 4PM 40 - 50  
 Precipitation Condition SUNNY

Working Day  If no, explain:

**Diary:**

Dispute

**Cable Hauling**

West End:

Morning: Hauling stand # 3 started today.

Jimmy's crew prepping to install winch line on side span catwalk.

Afternoon: Primary to secondary hauling completed and hauling proceeded. When hauling frame was hauled, the pully on the west loop rattled, ABF confirmed haul rope was centered.

Observed that strand was snagged by roller frames at West Loop. It occurred about 10' from the socket leading end. Told the guys at the east end to verify that wires weren't damaged.

2:19pm: Socket leading end reached the end of the west loop and workers were prepping to install socket from Secondary to Primary haul frame on south side span. Observed pws strand stuck against the transfer arm, workers used a crowbar and chain falls to release strand from strand.

2:40pm: Hauling of primary system proceeded east towards tower.

4pm: Jimmy's crew installed two pws clamps on strand # 2.

4:40pm: On south side span, observed about 15' of strand did not have tape and strand wires had slack and bulging out. Told iron worker and Anchor (ABF engineer) that tape was needed & tape was applied to this area and it was resolved.

My hours worked: 11 hours total including 3 hours OT.

04-0120F4 Bid Item: 067 C-PWS-001.067 Install & Adjust PWS 1-5

AMERICAN BRIDGE/FLUOR, A JV

**Labor**

Trade	Class	Name	RT Hrs	OT Hrs	DT Hrs	Total	Remarks	Dispute
Contractor: AMERICAN BRIDGE/FLUOR, A JV								
Ironworker	JNM	MICHAEL DRAPER	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	MICHAEL PORTILLO	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	Tony Miranda	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	RYAN EVANCHIK	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	JAMES BENNINGHOVE	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	RYAN NASH	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	FOR	JERRY KUBALA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	JNM	RIGOVERTO GARCIA	8.00	2.00	0.00	10.00		<input type="checkbox"/>
Ironworker	APP	JONATHAN CANITES	8.00	2.00	0.00	10.00		<input type="checkbox"/>



# Daily Diary Report by Bid Item

Job Name: 04-0120F4 Inspector Name Altamirano, Victor Diary #: 069 Date: 09-Jan-2012 Monday

Ironworker	JNM	JOSEPH STONE	8.00	2.00	0.00	10.00	<input type="checkbox"/>
------------	-----	--------------	------	------	------	-------	--------------------------

## Attachment



Socket leading end on secondary hauling frame



Strand bulging and loose wires @ South Side Span. Worker applied tape.



Hauling proceeded towards tower.



Strand # 2 post Installation: Wires out of position @ SDS



Socket installed to Primary Hauling frame at South side span

Socket leading end on secondary hauling frame

## Daily Diary Report by Bid Item

Job Name: 04-0120F4

Inspector Name Altamirano, Victor


Diary #: 069

Date: 09-Jan-2012

Monday



Strand # 3 hauling west towards West End on the side span

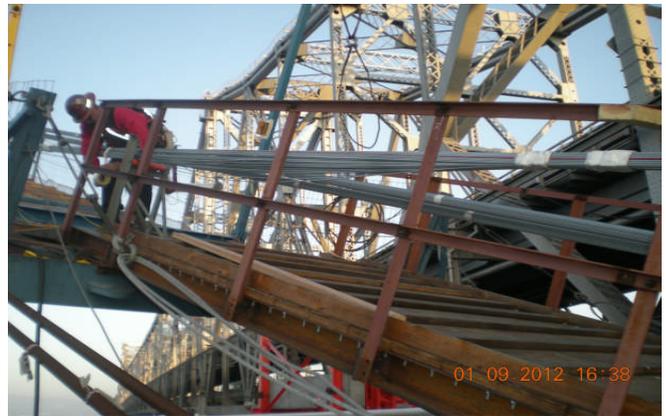

Strand bulging and loose wires @ South Side Span. Worker applied tape.



Installing come-along @ north side span



Strand socket installed at transfer arm on South side



Strand # 2 post Installation: Wires out of position @ SDS near the top of the saddle

Chain-fall attached to socket
